togetherforbetter

CLARK COUNTY, NEVADA

CMAR CONSTRUCTION SERVICES CONTRACT

RFP NO. 607319-24
NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE

THE WHITING-TURNER CONTRATING COMPANY
NAME OF FIRM
Paul Schmitt, Senior Vice President
DESIGNATED CONTACT, NAME AND TITLE (Please type or print)
6720 Via Austi Parkway, Suite 550 Las Vegas, Nevada 89119
ADDRESS OF FIRM INCLUDING CITY, STATE AND ZIP CODE
(702) 650-0700
(AREA CODE) AND TELEPHONE NUMBER
(702) 650-2650
(AREA CODE) AND FAX NUMBER
Paul.Schmitt@Whiting-Turner.com
E-MAIL ADDRESS

607319-24

NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE

THIS CMAR CONSTRUCTION CONTRACT (the "Contract") is made and entered into, effective as of _____ (the "Effective Date"), by and between the County of Clark, a political subdivision of the State of Nevada, (the "Owner"), and THE WHITING-TURNER CONTRACTING COMPANY (the "Construction Manager at Risk" or "CMAR"). The Owner and the CMAR are sometimes individually referred to herein as "Party" and collectively as "Parties."

RECITALS

WHEREAS, the Owner intends to construct NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE (the "Project"); and

WHEREAS, the Owner is authorized under NRS 338.1685-338.16995 to contract with a qualified CMAR for an eligible public work following the selection procedures contained therein; and

WHEREAS, the Owner and CMAR have entered into a contract for CMAR Preconstruction Services for the Project; and

WHEREAS, the Owner desires to retain a contractor to perform construction services, and the CMAR desires to provide these services hereinafter set forth below;

NOW, THEREFORE, in consideration of the mutual covenants herein contained, the Parties hereto, intending to be legally bound, agree as follows:

1. PROJECT DESCRIPTION

The Project consists of the construction more fully set forth and described in the Contract Documents.

2. CONSTRUCTION COVENANT

The CMAR hereby covenants and agrees to undertake and complete the Work (defined in the Contract Documents) in a good, substantial and workmanlike manner. The CMAR further agrees to provide the materials, labor, tools, and equipment necessary to properly and expeditiously complete the Work in strict accordance with the requirements of the Contract and other Contract Documents and to accept payment of the Contract Amount, subject to any adjustments under the terms of the Contract, as complete compensation therefor (including all of the expenses, direct or indirect, incurred by the CMAR in connection therewith).

3. CONTRACT AMOUNT

For furnishing all labor, materials, equipment, tools and services and for doing everything required by this Contract and the other Contract Documents, the Owner will pay, and the CMAR shall accept the Contract Price, as defined in the General Conditions, which in no event shall exceed the **Guaranteed Maximum Price** of **$ 93,005,177**. The Guaranteed Maximum Price (GMP) includes, Cost of the Work, General Conditions, CMAR Fee, and CMAR Contingency.

The CMAR's Guaranteed Maximum Price (GMP) for the entire Work on the Project consists of:

A.	Cost of the Work (excluding General Conditions)	**$ 75,705,520**
B.	General Conditions*	**$ 9,442,177**
C.	CMAR's Fee*	**$ 2,669,833**
D.	CMAR's Contingency**	**$ 2,326,838**
E.	Insurance and Bonds***	**$ 2,860,809**
	Total Guaranteed Maximum Price	**$ 93,005,177**

Percentage Split of GMP Savings:	Owner	CMAR
	70%	30%

Savings includes underrun of the total Guaranteed Maximum Price, including CMAR's contingency remaining at the end of the project; savings does NOT include unused Owner's Contingency. One hundred percent (100%) of the unused Owner's Contingency, shall be retained by the Owner.

* The General Conditions and CMAR's Fee shall be calculated as a percentage of the Cost of the Work.

** The **CMAR's Contingency** shall be used at the discretion of the CMAR; however, the CMAR shall notify the Owner in writing of the intent to utilize the CMAR's contingency prior to any expenditures. The CMAR's Continency shall be used: (1) for expenditure(s) less than $100,000, at the discretion of the CMAR; and (2) for expenditure(s) of $100,000 or more, upon Owner's written approval, which shall not be unreasonably withheld or delayed. In no event shall CMAR's Contingency be used for expenditures not covered under Section 4.04(a).

*** Insurance and Bonds shall be calculated as a percentage of the sum of the Cost of the Work, General Conditions, CMAR's Fee, and CMAR's Contingency.

4. DOCUMENT INCORPORATION

The Contract consists of this three (3) page document and the following documents incorporated herein by this reference as a part hereof:

A. General Conditions, Exhibit "A" attached hereto

B. GMP Schedule of Values, Exhibit "B" attached hereto

C. Schedule of GMP Allowances, Qualifications and Clarifications, Exhibit "C"

D. Exhibit "C-1" Owner Contingency attached hereto

E. Technical Specifications and Drawings for the Project, Exhibit "D" and Addenda, if any attached hereto

F. Copy of Key Personnel List, Exhibit "E" attached hereto

G. Geotechnical and Environmental Reports, Exhibit "F" attached hereto

H. List of Work Estimated by CMAR to Exceed 1% of Cost of Public Work, Exhibit "G" attached hereto

I. Baseline Project Schedule, Exhibit "H" attached hereto

J. Prevailing Wage Rates, Exhibit "I" attached hereto

5. COMMENCEMENT AND CONTRACT TIME

Time is of the essence in the performance and completion of this Contract. The CMAR shall commence the Work on the date set by the Owner in the Notice to Proceed, and shall achieve Substantial Completion of the entire Work as shown in Exhibit H (Baseline Project Schedule) thereafter, subject to adjustments of the Contract Time as provided in the Contract Documents.

6. LIQUIDATED DAMAGES

The CMAR agrees that time is of the essence of this Contract and further agrees to satisfactorily complete the Work in accordance with the Contract Documents. If the CMAR shall neglect, fail, or refuse to complete the Work for any reason within the time specified for Substantial Completion in the Contract plus any adjustments to the Contract Time resulting from approved Change Orders, then the CMAR does hereby agree, as a part consideration for the awarding of this Contract, to pay to the Owner, as liquidated damages and not as a penalty, as follows:

Liquidated damages shall not accrue after the date of Substantial Completion provided the CMAR completes all punch-list work within thirty (30) calendar days after the date of the Certificate of Substantial Completion. Liquidated damages shall accrue at the sum of **$1,000 per calendar day** if the CMAR does not complete all punch-list work within the time limit stipulated in the Certificate of Substantial Completion. [For projects with multiple GMPs, see D1 progress schedules].

The said amounts are fixed and agreed on by and between the CMAR and the Owner because of the impracticability and extreme difficulty of fixing and ascertaining the true value of the damages which the Owner will sustain by failure of the CMAR to complete the Work on time, such as architectural and engineering inspection, supervision and contract administration, loss of revenue, cancellation costs for schedule performances, interest charges, delays caused to other construction activities of Owner by failure to perform this Contract, and other damages, some of which are indefinite and not susceptible of easy proof, said amount is agreed to be a reasonable estimate of the amount of damages which the Owner will sustain and said amount shall be deducted from any monies due or that may become due to the CMAR.

7. NOTICES

Any notice required to be given under the Contract shall be deemed to have been given when the notice is (i) delivered personally, (ii) transmitted by facsimile with confirmation of transmission, (iii) transmitted by email with confirmation of receipt

by addressee, or (iv) sent by U.S. mail via certified mail-return receipt requested at the following addresses:

To the Owner:	Clark County Government Center Attn: Purchasing Manager 500 South Grand Central Parkway, 4th Floor Las Vegas, Nevada 89101
To the CMAR:	The Whiting-Turner Contracting Company Attn: Paul Schmitt 6720 Via Austi Parkway, Suite 550 Las Vegas, Nevada 89119
To the CMAR: (For insurance notices)	The Whiting-Turner Contracting Company Attn: Patricia Hardimon 6720 Via Austi Parkway, Suite 550 Las Vegas, Nevada 89119 Email:Patricia.Hardimon@whiting-turner.com

Any change in the addresses stated above shall be made in writing and delivered in the manner provided herein.

[Signatures on following page]

IN WITNESS WHEREOF, the parties have caused this Contract to be executed as of the Effective Date.

COUNTY:

CLARK COUNTY, NEVADA

By:_____ _____

JESSICA COLVIN
Chief Financial Officer

DATE

CMAR:

THE WHITING-TURNER CONTRACTING COMPANY

By:_____ 4-13-2026

PAUL SCHMIDT
Senior Vice President

DATE

APPROVED AS TO FORM:

STEVEN B. WOLFSON
District Attorney

By: Sarah Schaerrer
Sarah Schaerrer (Apr 15, 2026 11:43:41 PDT)

SARAH SCHAERRER
Deputy District Attorney

04/15/2026

DATE

EXHIBITS OF THE CONSTRUCTION SERVICES CONTRACT

EXHIBIT A - General Conditions

EXHIBIT B - GMP Schedule of Values

EXHIBIT C - Schedule of GMP Allowances, Qualifications and Clarifications

EXHIBIT C-1 - Exhibit "C-1" Owner Contingency

EXHIBIT D - Technical Specifications and Drawings for the Project (Drawings Attached to Final Contract)

EXHIBIT E - Copy of Key Personnel List

EXHIBIT F - Geotechnical and Environmental Reports

EXHIBIT G - List of Work Estimated by CMAR to Exceed 1% of Cost of Public Work

EXHIBIT H - Baseline Project Schedule

EXHIBIT I - Prevailing Wage Rates (Attached to Final Contract)

EXHIBIT J – Bonds and Insurance Requirements

EXHIBIT K – Subcontractor Information

EXHIBIT A
NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE
GENERAL CONDITIONS

SECTION 1. DEFINITIONS

SECTION 2. CMAR'S RIGHTS AND RESPONSIBILITIES

2.01 Responsibility for the Security of the Work and Project Site
2.02 Responsibility for Protecting Adjacent Areas
2.03 Responsibility for Construction Safety
2.04 Responsibility for Clean-Up of the Work Site
2.05 Responsibility for Construction Procedures
2.06 Responsibility for Employment of Competent Project Personnel
2.07 Responsibility for Uncovering and Correcting the Work
2.08 Responsibility for Permits and Fees
2.09 Responsibility for Record Documents
2.10 Responsibility for Substitution of Materials, Products or Services
2.11 Responsibility for Delivery and Storage of Materials and Equipment
2.12 Responsibility for Emergencies
2.13 Responsibility for Payment of Subcontractors and other Parties
2.14 Responsibility for Schedule of Values
2.15 Responsibility for Site Inspection

SECTION 3. OWNER'S RIGHTS AND RESPONSIBILITIES

3.01 Owner's Designated Representative
3.02 Right to Perform or Award Separate Contracts for Portions of the Work
3.03 Right to Perform Additional Work Within or Near the Project Site
3.04 Progress Meetings
3.05 Right of Suspension
3.06 Right of Termination for Convenience
3.07 Right to Replace Subcontractor

SECTION 4. CONTRACT COMMENCEMENT, PROGRESS AND COMPLETION

4.01 Notice to Proceed
4.02 Baseline Project Schedule
4.03 Progress of the Work
4.04 Payment Terms and Definitions
4.05 Progress Payments and Retainage

SECTION 5. COMPLETION OF THE PROJECT

5.01 Substantial Completion
5.02 Punch List
5.03 Final Inspection and Final Acceptance of the Work
5.04 Final Payment
5.05 Non-Conforming Work Not Accepted

SECTION 6. LIQUIDATED AND DELAY DAMAGES

6.01 Owner's Recovery of Liquidated Damages
6.02 Delay Damages

SECTION 7. BONDING REQUIREMENTS

7.01 Required Bonds
7.02 Acceptable Surety
7.03 Failure to Maintain Bonds

SECTION 8. INSURANCE REQUIREMENTS

8.01 Required Insurance
8.02 Acceptable Insurance
8.03 Failure to Maintain Insurance

SECTION 9. INDEMNITY

9.01 General Indemnity
9.02 Patent Indemnity

SECTION 10. BREACH OF CONTRACT AND REMEDIES

10.01 Definition of Breach
10.02 Event of Default
10.03 Damages
10.04 Termination for Cause
10.05 Owner's Right to Perform the Work
10.06 Deduction from Progress Payments
10.07 Rights and Remedies are Cumulative

SECTION 11. REPRESENTATIONS AND WARRANTIES

11.01 General Representations and Warranties
11.02 Warranty of Merchantability and Fitness for Particular Purpose
11.03 Warranty Work Conforms with Requirements of the Contract
11.04 Warranty Exclusions Prohibited

SECTION 12. DISPUTES BETWEEN PARTIES

12.01 In General
12.02 Work to Proceed
12.03 Alternate Dispute Resolution Costs and Fees
12.04 Notice of Disputes
12.05 Right of Judicial Action

SECTION 13. COMPLIANCE WITH THE LAWS

13.01 General
13.02 Compliance with Labor Laws
13.03 Compliance with Americans with Disabilities Act (ADA)
13.04 Compliance with Immigration Reform Control Act of 1986
13.05 Air Pollution Control
13.06 Fire Prevention
13.07 Provisions Required by Law
13.08 Stormwater Pollution Control
13.09 Disposal of All Wastes (Hazardous, Toxic, and Non-Hazardous)
13.10 Compliance with National Environmental Policy Act (NEPA)
13.11 Use of Apprentices

SECTION 14. CONTRACT INTERPRETATION

14.01 General
14.02 Intent and Correlation
14.03 Governing Order of Contract Documents
14.04 Conflicting Conditions
14.05 Graphic Enhancement

SECTION 15. MISCELLANEOUS PROVISIONS

15.01 Regulatory Authorities
15.02 Subcontracts
15.03 Audit of Records
15.04 Independent Contractor
15.05 Severability
15.06 Assignment of Contractual Rights
15.07 Ownership and Use of Documents
15.08 Prohibited Interest
15.09 Waiver
15.10 No Personal Liability
15.11 Contract Modification
15.12 Required Reporting for Bidder's Preference on Public Work Projects
15.13 Owner's Recovery of Bidders Preference Penalties
15.14 Counterpart Signatures
15.15 Prison Rape Elimination Act Compliance
15.16 Detention Facilities
15.17 Gratuities
15.18 Covenant
15.19 Disclosure of Ownership Form
15.20 Authority
15.21 Non-Endorsement
15.22 Public Records
15.23 Companies that Boycott Israel
15.24 State of Nevada Legal Holidays
15.25 Close-out Documentation
15.26 Utilities
15.27 Taxes
15.28 Labor Strife
15.29 Change Orders
15.30 Uniform Standard Specifications for Public Works Construction Off-Site Improvements

SECTION 1 DEFINITIONS

The following definitions shall apply to the Contract:

a) **"Addendum"** means a written change or other written instrument issued by the Owner via the Clark County Purchasing and Contracts division that amends or otherwise changes the GMP Setting Documents prior to submission of the GMP.

b) **"Applicable Law"** means (1) any federal, state, or local law, code, or regulation; or (2) any formally adopted and generally applicable rule, requirement, determination, standard policy, implementation schedule, or other order of any governmental body having appropriate jurisdiction to the extent it relates specifically to the construction of the project and the responsibilities of the CMAR under the Contract. Each and every provision of law and clause required by law to be inserted in the Contract shall be deemed to be inserted therein, and the Contract shall be read and enforced as though such provision were included therein, and if through mistake or otherwise, any such provision is not inserted, or is not correctly inserted, then upon the application of either party, the Contract shall be physically amended to make such insertion or correction. The Owner acknowledges that the respective design professionals and/or Owner, and not the CMAR, are responsible for Contract Document compliance with Applicable Law. This acknowledgement in no way limits the responsibility of the CMAR to diligently perform the Scope of Services in the Contract for Construction Manager at Risk Preconstruction Services for dated Insert Preconstruction Services Execution Date, between the Owner and the CMAR.

c) **"As-Builts"** means record drawings or drawings representing the 'as-built' condition of the Work.

d) **Baseline Project Schedule"** means the initial schedule of the Work submitted by the CMAR and accepted by the Owner at the outset of the Project which is used as the baseline for comparing the progress of the Project. Such schedule is further described in Section 01 32 16 (Progress Schedules) of the Technical Specifications.

e) **"Certified Payroll Report"** means the record required to be compiled, maintained, and submitted by the CMAR and its Subcontractors to the Owner in compliance with NRS 338 and any other provisions of Nevada law.

f) **"Construction Change Directive"** means a written order from the Owner directing immediate changes in the Work for which a modification to the Contract Amount, Contract Time or other provision of the Contract may be appropriate but may not have been negotiated at the time of issuance. The CMAR is to proceed immediately with the implementation of the Construction Change Directive.

g) **"Change Order"** means a written order to the CMAR signed by the Owner and CMAR issued after execution of the Contract that authorizes a change in the Work, Contract Amount or Contract Time. Except as allowed by the Contract Documents, the Contract Amount or Contract Time may be changed only by the issuance of a Change Order. The execution of the Change Order indicates the CMAR's agreement to the terms set forth therein including the adjustment, if any, in the Contract Amount or Contract Time.

h) **"County"** means the County of Clark, a political subdivision of the State of Nevada.

i) **"CMAR Fee"** means the CMAR overhead and profit as further defined in Section 4 of this Contract.

j) **"CMAR General Conditions"** means the costs as further defined in Section 4 of this Contract.

k) **"Contingency- CMAR"** means the allowance that may be utilized by the CMAR to cover certain Cost of the Work as further defined in these General Conditions.

l) **"Contingency – Owner"** means the Owner's Contingency shall consist of 1) Conflicts and Contingencies, 2) Risk Allowance, and 3) Owner directed scope addition(s).

m) **"Conflicts and Contingencies - Owner"** means the method of payment for additional work as directed by the Owner and is included in the Owner Contingency; Exhibit C-1.

n) **"Construction Manager at Risk" (CMAR)** means the contractor with whom the Owner has entered into this Contract to perform the Work.

o) **"Construction Manager at Risk Work", "CMAR Work" or "Work"** means everything required to be furnished and done for and relating to the construction of the Project by the CMAR pursuant to this Contract. CMAR Work includes the employment and furnishing of all construction services, labor, materials, equipment, supplies, tools, scaffolding, transportation, utilities, temporary facilities and other things and services of every kind whatsoever necessary for the full performance and completion of the CMAR's responsibility to obtain Permits, except as detailed in the Technical Specifications and "Exhibit" Contract Documents attached hereto, procurement of equipment and materials, construction, management, coordination and related obligations with respect to the construction of the Project under this Contract, including all completed structures, assemblies, fabrications, acquisitions and installations, and all of the CMAR's administrative, accounting, record keeping, notification and similar responsibilities of every kind whatsoever under this Contract pertaining to such obligations. A reference to CMAR Work shall mean any part and all of the CMAR Work unless the context otherwise requires, and shall include all extra CMAR Work authorized by Change Order or Work Change Directive.

p) **"Consultant"** means the licensed Architect, Engineer or other design professional and its consultants, retained by the Owner to perform design services for the Project.

q) **"Contract"** means the CMAR Construction Contract, which does not come into existence until executed by all parties, and all other documents incorporated therein by reference. The Contract is a contract for the cost of the work, plus a fee, with a guaranteed maximum price.

r) **"Contract Amount"** means the compensation to be paid the CMAR to construct the Work and is included in the "Amount of Contract" section of the Contract by the Owner.

s) **"Contract Award Date"** means the date this Contract is awarded by the Owner to the CMAR and date this Contract becomes effective.

t) **"Contract Documents"** means the Owner-CMAR Construction Contract, General Conditions, Technical Specifications, Drawings and, if applicable, the Addenda or other Modifications made to the aforementioned documents.

u) **"Contract Time"** means the number of days set forth in the Owner-CMAR Construction Contract for constructing the Work for achieving Substantial Completion of the Work, including the authorized extensions thereto, which commences to start with the date set forth in the Notice to Proceed.

v) **"Cost of the Work"** means the cost to construct the Work, as further defined in Section 4.04(a).

w) **"Critical Path"** means the path through the project schedule indicating the minimum time in which it is possible to complete the Work, and the tasks that, if delayed, will delay Substantial Completion of the Work."

x) **"Date of Substantial Completion"** means the date established and certified by the Owner when construction is sufficiently complete, in accordance with the Contract Documents, so the Owner can occupy or utilize the Work, or designated portion thereof, for the use for which it is intended.

y) **"Day"** means a calendar day unless otherwise specifically designated.

z) **"Designated Representative"** means the person authorized pursuant to Section 3.01 (Designated Representative) of the Contract to act or make decisions on behalf of the Owner.

aa) **"Drawings"** mean the diagrammatic representations of the requirements for construction of the Work that are incorporated as a part of the Contract.

bb) **"Final Completion"** occurs on the date when the obligations of the CMAR under this Contract are complete and accepted by the Owner and final payment becomes due and payable.

cc) **"Force Majeure"** The CMAR shall be excused from performance hereunder during the time and to the extent that the CMAR is prevented from obtaining, delivering, or performing in the customary manner, disruptions in labor or materials resulting from a health crisis regardless of whether epidemic, pandemic or isolated to areas from which such labor and materials are supplied; by acts of God, fire, war, loss or shortage of transportation facilities, lockout or commandeering of raw materials, products, plants or facilities by the government or acts of terrorism. The CMAR shall provide the Owner evidence that nonperformance is due to other than fault or negligence of the CMAR.

dd) **"Good Construction Practices"** means those methods, techniques, standards and practices which, at the time they are to be employed and in light of the circumstances known or reasonably believed to exist at such time, are generally recognized and accepted as good equipping, installation, construction, commissioning and testing practices for the construction and improvement of capital assets in the construction industry as followed in the southwestern region of the United States.

ee) **"Governing Body"** means the Clark County Board of Commissioners or any federal, state, regional or local legislative, executive, judicial or other governmental board, agency, city, county, commission, administration, court or other body, or any official thereof having jurisdiction.

ff) **"Guaranteed Maximum Price" or "GMP"** means the maximum amount which the Owner is obligated to pay CMAR for construction of the Project, inclusive of all costs, general conditions, and fees of CMAR in connection with the Work.

gg) **"GMP Setting Documents"** means the Technical Specifications and Drawings prepared by the Architect/Engineer, reviewed by the CMAR during Pre-Construction Service and utilized by the CMAR to prepare the GMP.

hh) **"Hazardous Material"** means any substance or material identified now or in the future as hazardous under any federal, state or local law or regulation, or any other substance or material that may be considered hazardous or otherwise subject to statutory or regulatory requirement governing handling, disposal or clean-up.

ii) **"Insurance Requirement"** means any rule, regulation, code, or requirement issued by any insurance company which has issued a policy of required insurance under this Contract, as in effect during this Contract, compliance with which is a condition to the effectiveness of such policy.

jj) **"Key Personnel"** means those individuals identified by CMAR in Exhibit E of its Proposal.

kk) **"Labor Commissioner"** means the person appointed and functioning pursuant to NRS Chapter 607 who is charged with enforcing the labor laws of the State of Nevada.

ll) **"Lien"** means any and every lien against the Project or against any monies due or to become due from the Owner to the CMAR under this Contract, for or on account of the Work, including mechanics', materialmen's, laborers' and lenders' liens.

mm) **"Major Change in the Work"** means changes to the Work ordered by the Owner in writing that involve adjustment to the Contract Amount or extension of the Contract Time and may be inconsistent with the Construction Documents.

nn) **"Minor Change in the Work"** means changes to the Work ordered by the Owner in writing that do not involve adjustment to the Contract Amount or extension of the Contract Time and are not inconsistent with the Construction Documents.

oo) **"Modification"** means (i) any Addenda related to the GMP Setting Documents (ii) a written Change Order, (iii) a written interpretation, (iv) a written order issued by the Owner for a minor change in the Work, or (v) a written amendment to the Contract signed by both parties.

pp) **"Notice of Award"** is the letter issued by the Owner notifying the CMAR of the award of the Project by the Clark County Board of Commissioners, authorizing the CMAR to proceed with the procurement of the bonds and insurance, and including the Contract for execution and return to the Owner.

qq) **"Notice to Proceed"** means the document issued by the Owner that (i) establishes the date the CMAR is allowed to begin construction activity at the site, and (ii) commences the running of the Contract Time.

rr) **"Owner"** means the County of Clark, a political subdivision of the State of Nevada.

ss) **"Owner's Designated Representative"** means Owner's employee identified in Section 3.01 (Designated Representative) of the Contract.

tt) **"Permits"** means all orders of approval, permits, licenses, authorizations, consents, certifications, exemptions, rulings, entitlements and approvals issued by a Governmental Body of whatever kind and however described which are required under Applicable Law to be obtained or maintained by any person with respect to the Construction of the Project.

uu) **"Product Data"** means the illustrations, standard schedules, performance charts, instructions brochures, diagrams and other information furnished by the CMAR to illustrate a material, product or system for some portion of the Work.

vv) **"Progress Record Documents"** means the set of documents maintained by the CMAR indicating the actual as-built revisions to the Work and Contract Documents, which are further described in Section 01700 of the Technical Specifications.

ww) **"Progress Schedule"** means a version of the schedule for the Work provided by the CMAR subsequent to the Baseline Project Schedule, pursuant to the requirements of the Contract related to issues such as time extensions, claims, payments, tardiness and recovery.

xx) **"Project"** means the total construction of which the Work performed provided under the Contract may be the whole or a part thereof and which may include construction by the Owner or by other contractor hired by the Owner.

yy) **"Promptly"** means without delay and on time.

zz) **"Reasonable Time"** means ten (10) business days, except where otherwise specified, or unless Clark County Board of Commission action is required.

aaa) **"Request for Information or RFI"** means a written request initiated by the CMAR to obtain clarification or information regarding the Project.

bbb) **"Samples"** mean the physical examples that illustrate the materials, equipment or workmanship, to be used by the CMAR and that establish standards for the judgment of the Work.

ccc) **"Shop Drawings"** mean the drawings, diagrams, schedules and other data specially prepared for the Work by the CMAR or any Subcontractor, manufacturer, Supplier or distributor to illustrate some portion of the Work.

ddd) **"Site"** means the location of the Project where the Work is to be performed.

eee) **"State"** means the State of Nevada.

fff) **"Subcontractor"** means any individual or entity who is sublet any part of the Work by the CMAR. There is no contractual relationship between the Owner and the Subcontractor who performs work or services for the CMAR.

ggg) **"Submittal"** means the item required by the Contract Documents to be provided to the Owner for information, review, or approval as indicated. Unless otherwise specifically indicated, Submittals are not a part of the construction and do not become part of the Contract Documents. Schedules, Shop Drawings, Product Data, and Samples are typical examples of a Submittal.

hhh) **"Substantial Completion"** means the point in time when, in the opinion of the Owner, construction is sufficiently complete, in accordance with the Contract Documents, that the Owner can occupy or utilize the Work, or designated portion thereof, for the intended use of the Project. This is not necessarily final acceptance of the Project or any portion thereof. A Certificate of Substantial Completion shall be issued by the Owner establishing the Date of Substantial Completion and noting any incomplete or unacceptable portions of the Work that must be completed or corrected prior to final acceptance of the Work. The date of such Certificate shall commence the running of the warranty periods required by the Contract Documents for the completed portions of the Work, except as otherwise provided in the Contract Documents or Certificate of Substantial Completion.

iii) **"Supplier"** means an entity selected by CMAR or Subcontractor of any tier for the supply of any materials or equipment for the Project.

jjj) **"Tax"** means any tax, fee, levy, duty, impost, charge, surcharge, assessment or withholding, or any payment-in-lieu thereof, and any related interest, penalty or addition-to tax.

kkk) **"Technical Specifications"** means the written descriptions of the requirements for the Work incorporated/attached as Exhibit "D" hereto as a part of the Contract.

SECTION 2. CMAR'S RIGHTS AND RESPONSIBILITIES

Section 2.01 Responsibility for the Security of the Work and Project Site

a) The CMAR is responsible at all times for the Work and for the Project site regardless of whether or not the Owner has required any insurance coverages (such as Builder Risk Insurance) which would have protected the interest of the CMAR and the Owner. The CMAR shall conduct its operations under the Contract in a manner as to avoid the risk of damage, injury, loss or theft by any means (including acts of God, vandalism or sabotage) to the Work or to the property of the CMAR, Owner or any other person. The CMAR shall promptly take such reasonable precautions, which are necessary and adequate against any and all conditions involving such risk of damage, injury, loss or theft. The CMAR shall continuously inspect the Work (including the materials and equipment used in connection therewith) to discover and determine if any such conditions exist and shall be solely responsible for correcting such conditions.

b) The CMAR shall cooperate with the Owner on all security matters and shall promptly comply with any security requirements established by the Owner. Such compliance with these security requirements shall not relieve the CMAR of its responsibility for maintaining proper security for the above-noted items, nor shall it be construed as limiting in any manner the CMAR's obligation to undertake such reasonable action as may be required to establish and maintain secure conditions at the Work site. The CMAR shall prepare and maintain accurate reports of incidents of loss, theft or vandalism and shall furnish these reports to the Owner in a timely manner.

Section 2.02 Responsibility for Protecting Adjacent Areas

a) Unless otherwise specifically provided in the Contract, the CMAR shall not perform the Work in a manner that would disrupt or otherwise interfere with the operation of any pipeline, telephone line, electric transmission line, ditch or other structure which may be on or adjacent to the Work site, or enter upon lands in their natural state until approved by the Owner. Thereafter, and before it begins the Work, the CMAR shall give due notice to the Owner of its intention to start the Work. The CMAR shall not be entitled to an increase in the Contract Time, or extra compensation on account of any postponement, interference or delay of the Work caused by such line, ditch or structure.

b) The CMAR shall preserve and protect cultivated areas and planted vegetation (such as trees, plants, shrubs and grass) on or adjacent to the Work site that the Owner has determined does not unreasonably interfere with the performance of the Work (including the operation of equipment or stockpiling of materials) and shall repair or restore any damage thereto.

Section 2.03 Responsibility for Construction Safety

a) The CMAR shall be solely responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the Work. The CMAR shall comply with all applicable laws, ordinances, rules, regulations and lawful orders of any public authority bearing on the safety of persons or property or their protection from damage, injury or loss.

b) The CMAR shall take all reasonable precautions for the safety of all employees on the Work and all other persons who may be affected thereby. The CMAR shall designate a responsible member of his organization whose duty shall be the prevention of accidents.

c) Except as otherwise stated in the Contract, if the CMAR encounters any materials reasonably believed to be asbestos, lead or polychlorinated biphenyl (PCB) on the Project site, the CMAR shall immediately stop work in the area affected and give notice of the condition to the Owner. The CMAR shall not resume the Work in the affected area without written direction by the Owner.

Section 2.04 Responsibility for Clean-Up of the Work Site

The CMAR shall, at all times, keep the work area in a neat, clean and safe condition. Upon completion of any portion of the Work, the CMAR shall promptly remove all of its equipment, temporary structures and surplus materials not to be used at or near the same location during later stages of work. Upon completion of the Work and before final payment is made, the CMAR shall, at its expense, dispose of all unnecessary vegetation, structures, rubbish, unused materials, and other equipment and materials belonging to it or used in the performance of the Work to the satisfaction of the Owner in accordance with all applicable federal, state, and local laws, ordinances and codes. The CMAR shall leave the premises and Work site in a neat, clean, and safe condition. In the event of the failure to comply with the foregoing, the Owner may satisfy the requirements of this Section at the CMAR's expense

Section 2.05 Responsibility for Construction Procedures

a) The CMAR shall supervise and direct the Work using its best skill and attention. The CMAR shall be solely responsible for all construction means, methods, techniques, sequences and procedures and for coordinating all portions of the Work under the Contract.

b) The CMAR shall not be relieved from its obligations to perform the Work in accordance with the Contract either by the activities or duties of the Owner in the administration of the Contract, or by inspections, tests or approvals required or performed by persons other than the CMAR.

Section 2.06 Responsibility for Employment of Competent Project Personnel

The CMAR shall employ competent project personnel that are acceptable to the Owner to oversee various aspects of the Project. Any substitution of the personnel defined in this section is prohibited and will be permitted only after a written request for such substitution has been made and approved by the Owner.

a) **Project Manager**. The Project Manager shall oversee all Work on the Project. The Project Manager shall have the authority to act on the CMAR's behalf on contract-specific issues. The Project Manager is to be present at progress meetings, and be involved in the chain of dispute resolution, Change Order negotiation, schedule development, public involvement, and other project specific activities where additional CMAR oversight is required to ensure full compliance with Contract requirements. The Project Manager shall continue in that capacity for the duration of the Project, unless the Project Manager ceases to be on the CMAR's payroll or the Owner otherwise agrees to a substitution in writing. Written approval by Owner of a Project Manager substitution request will not be unreasonably withheld.

b) **Superintendent.** The Superintendent shall manage all Work on the Project, including all subcontracted Work. The Superintendent shall represent the CMAR and all communications given to the Superintendent shall be as binding as if given to the CMAR. The Superintendent shall be available 24 hours a day and shall be on the construction site when there is any construction activity taking place on the Project. During day and night work schedules, the Superintendent may appoint additional deputy superintendents, as approved by the Owner.

The Superintendent is to be present at progress meetings and be available as needed to meet with the Owner regarding the progress of the Work and related activities. Failure to maintain a Superintendent on the Project site at all times work is in progress shall be considered a material breach of this Contract, entitling the Owner to terminate the Contract or, alternatively, issue a stop Work order until the Superintendent is on Project site.

The Superintendent shall continue in that capacity for the duration of the Project, unless the Superintendent ceases to be on the CMAR's payroll or the Owner otherwise agrees to a substitution in writing. Written approval shall not be unreasonably withheld.

Section 2.07 Responsibility for Uncovering and Correcting the Work

a) If any portion of the Work has been covered contrary to the request of the Owner or contrary to the requirements stated in the Contract, the CMAR shall, if requested by the Owner, uncover for observation and, if not in accordance with the Contract Documents, shall be replaced and recovered at the CMAR's expense without any adjustment to the Contract Time.

b) If any portion of the Work has been covered which the Owner has not specifically requested to observe prior to being covered, the CMAR shall, if requested by the Owner, uncover for observation and, if unacceptable, shall be replaced and recovered at the CMAR's expense without any adjustment to the Contract Time. If the uncovered Work is in compliance with the requirements of the Contract, the cost to recover shall be paid by the Owner.

Section 2.08 Responsibility for Permits and Fees

Unless otherwise provided in the Contract Documents to be the responsibility of the Owner, the CMAR shall secure all the necessary Permits and pay the required license and inspection fees associated therewith, which are necessary for the proper execution and completion of the Work.

Section 2.09 Responsibility for Record Documents

The CMAR shall keep a marked-up, up-to-date set of the Progress Record Documents subject to the provisions of Section 01700 of the Technical Specifications. The Progress Record Documents shall depict the as-built conditions of the Work as they occur during the course of construction as an accurate record of the deviations between the Work as designed and the Work as installed.

Section 2.10 Responsibility for Substitutions of Materials, Products or Services

a) **Criteria.** The CMAR may propose the substitution of any material, product or service in lieu of that required or specified by brand name or trade name under the Contract subject to the requirements set forth herein. Any material, product or service manufactured by a company other than the one specified, or is brand name, model number or generic species other than what is specified, will be considered a substitution.

Prior to proposing the substitution, the CMAR shall determine whether or not (i) the proposed material, product or service is, in fact, equal to that specified after considering the ease of operation, maintenance, repairs, appearance, longevity and any other pertinent factors and (ii) the substitution will result in a cost savings, reduced construction time or similar demonstrable benefit to the Owner. A substitution will not be permitted where the material or product is intended to match others in use, accommodate artistic design, specific function or economy of maintenance.

b) **Procedure.** In accordance with the Baseline Project Schedule, the CMAR shall submit to the Owner a written request for the substitution accompanied by drawings, samples, test data, certificates and any other pertinent documentation which will permit the Owner to make a fair and equitable decision concerning the proposed substitution. If the CMAR fails to submit the written request within the specified time, the substitution will not be allowed. If the substitution is acceptable to the Owner, a written authorization will be provided to the CMAR. No substitution will be allowed which will result in an increase in the Contract Amount.

c) **Burden of Proof.** The burden of proof in establishing the equality of the proposed substitution shall be upon the CMAR. Approval of a substitution shall not relieve the CMAR from responsibility for compliance with the other requirements of the Contract. The CMAR shall bear the expense for any changes in other parts of the Work caused by the substitution. The submission of a substitution incurs no obligation on the part of the Owner to accept or construe the proposed substitution to be an equal to that specified under the Contract. The Owner will be the sole judge of whether or not the substitution is equal in quality, utility and economy to that specified under the Contract. The Owner will have a reasonable amount of time to review each request for substitution.

d) **Required Certificates.** The substituted material, product or service shall be supported, by proper certification from the governmental agencies having jurisdiction over its use in the Work.

Section 2.11 Responsibility for the Delivery and Storage of Materials and Equipment

The CMAR shall receive, unload, store in a secure place, and deliver from storage to the Work site all materials and equipment required for the performance of the Contract. The storage facilities and methods of storing shall meet with the Owner's approval. Any materials and equipment subject to degradation by exposure shall be stored in a suitable enclosure provided by the CMAR.

Section 2.12 Responsibility for Emergencies

When emergencies affecting or threatening the safety of any person or property occur, the CMAR shall immediately act with diligence to prevent injury to such person, or damage or loss to such property. If the CMAR should fail to act, the Owner may, but is not obligated to, act immediately to prevent injury to such person, or damage or loss to property, whichever may be endangered by the emergency by whatever means or method the Owner deems appropriate, including, but not limited to, the use of other contractors, the Owner's own forces, and the CMAR's on-site equipment and materials, in which case, the CMAR shall pay the Owner for any such expenses incurred as provided in Section 10.05 (Owner's Right to Carry out the Work).

Section 2.13 Responsibility for Payment of Subcontractors and Other Parties

The CMAR is responsible for paying each Subcontractor constructing any portion of the Work, and other parties providing labor, material or supplies in connection with the Work pursuant to Nevada law.

Section 2.14 Responsibility for Schedule of Values

a) The CMAR, if so requested by the Owner, shall have provided to the Owner a schedule of values allocated to various portions of the Work. The schedule of values shall be formed and supported by such data and information, acceptable to the Owner.

b) Each line item of the schedule of values shall contain no more than reasonable and attributable costs applicable to the line item. The CMAR shall warrant the schedule of values to be reliable and accurate, and documents used in the preparation thereof shall be available for review by the Owner. Each line item on the schedule of values shall contain all costs attributable to that item with the exception of the CMAR Fee and CMAR General Conditions, which shall be

separately listed as a single line item at the bottom of the schedule of values as a lump sum total for the Project and payable as a percentage of overall work complete.

Section 2.15 Responsibility for Site Inspection

a) The CMAR acknowledges that it has taken steps reasonably necessary to ascertain the nature and location of the Work, and that it has investigated and satisfied itself as to the general and local conditions which can affect the Work or its cost, including but not limited to (i) conditions bearing upon transportation, disposal, handling, and storage of materials; (ii) the availability of labor, water, electric power, and roads; (iii) uncertainties of weather or similar physical conditions at the site; (iv) the conformation and conditions of the ground; and (v) the character of equipment and facilities needed preliminary to and during work performance.

b) The CMAR also acknowledges that it has satisfied itself as to the character, quality, and quantity of surface and subsurface materials or obstacles to be encountered insofar as this information is reasonably ascertainable from an inspection of the site, including all exploratory work done by the Owner, as well as from the drawings and specifications made a part of this contract. Any failure of the CMAR to take the actions described and acknowledged in this Section will not relieve the CMAR from responsibility for estimating properly the difficulty and cost of successfully performing the work, or for proceeding to successfully perform the work without additional expense to the Owner.

c) The Owner assumes no responsibility for any understanding reached or representation made concerning conditions which can affect the Work by any of the CMAR's officers or agents before the execution of the Contract, unless that understanding or representation is expressly stated in the Contract.

SECTION 3. OWNER'S RIGHTS AND RESPONSIBILITIES

Section 3.01 Owner's Designated Representative

a) The Owner shall appoint a Designated Representative with respect to the Contract. The Designated Representative shall have complete authority to transmit instructions, receive information, interpret and define the policies of the Owner and to make other decisions on the part of the Owner. Following the issuance of the Notice to Proceed, the Designated Representative may perform any review, communications, notices or other act required on the part of the Owner.

b) The Designated Representative shall not have any authority to change or interpret the Contract or Contract Documents, whether orally or in writing. Any ambiguity between the parties that require interpretation of the Contract or Contract Documents shall be resolved by written submission of a RFI by the CMAR. Any request for a change to the Contract or Contract Documents shall be resolved by written submission of a Change Order request by the CMAR. The Contract or Contract Documents shall not be changed without written confirmation from the Owner.

c) Communications from the Owner's Representative may be verbal or written. Any verbal instruction or directive by the Owner's Representative to the CMAR that changes either the Contract Amount or Contract Time or that changes either the Contract or the Contract Documents shall not be valid unless confirmed in writing and acknowledged and accepted by the Owner (i) within five working days or (ii) when the work that is subject to the verbal directive commences, whichever is earlier. Absent written confirmation of the Owner's Representative's verbal instruction to the CMAR, the parties agree that there is a strong presumption that no such verbal directive was ever given.

Section 3.02 Right to Perform or Award Separate Contracts for Portions of the Work

a) **Coordination.** The Owner reserves the right to perform portions of the Work related to the Project with its own forces or to award a separate contract or contracts for portions of the Work under the same or similar conditions of the Contract. The Owner will provide for the coordination of the activities by its own forces and that of each separate contractor with the Work of the CMAR. The CMAR shall participate with the Owner and the other separate contractors in reviewing their construction schedules when so directed by the Owner.

b) **Revisions to the Guaranteed Project Schedule.** The CMAR shall make the revisions to the Guaranteed Project Schedule deemed necessary after a joint review and mutual agreement. The Guaranteed Project Schedule as revised shall then constitute the schedule to be used by the CMAR. If the activities by the Owner or the other contractors are completed within the time reflected in the Guaranteed Project Schedule as revised or an extension is granted in the Contract Time, the CMAR shall be precluded from asserting any claim for delay or additional expenses resulting from the Owner exercising its rights granted herein.

c) **Storage of Equipment and Materials.** The CMAR shall afford the Owner and separate contractors' reasonable opportunity for introduction and storage of their materials and equipment and performance of their activities, and shall connect and coordinate the CMAR's construction and operations with theirs as required by the Contract.

d) **Reporting of Separate CMAR Deficiencies.** If part of the Work depends on the proper execution of construction or operations by the Owner or a separate contractor, the CMAR shall, prior to proceeding with the Work and each portion thereof, promptly report to the Owner the apparent discrepancies or defects such other construction or operations that would render the Work unsuitable for proper execution by the CMAR. The CMAR's failure to report such discrepancy or defect shall constitute an acknowledgment that the Owner's or separate contractor's completed or partially completed construction or operations is fit and proper for the CMAR to proceed with the Work, except as to defects not then reasonably discoverable.

e) **Delays and Damages to Separate CMARs.** The CMAR shall defend, indemnify and hold the Owner harmless pursuant to the provisions of Section 9.01 (General Indemnity) of the General Conditions for each claim asserted by a separate contractor for delay, improperly timed activity, defective construction or damage to the work of the separate contractor which is caused by the CMAR. The CMAR agrees to make no claim of cost or damages against the Owner for any delay, improperly timed activity, defective construction or damage to the Work of the CMAR which is caused (i) by the CMAR, or (ii) by a separate contractor unless such contractor is under contract to the Owner, or to a general contractor of the Owner.

The Owner shall pay each claim of cost incurred by the CMAR arising from the delay, improperly timed activity, defective construction or damage to the Work caused by a separate contractor acting under the direction or control of the Owner, or under the direction and control of a general contractor of the Owner, provided such claim meet the requirements contained in Section 01 29 76 (Application for Payment) of the Technical Specifications.

The failure of either party to pay the costs as required herein shall entitle the other party to file a claim pursuant to Section 12 (Disputes between the Parties) of the Contract.

f) **Repair of Damages.** The CMAR shall promptly repair any damage caused by the CMAR to the work of a separate contractor or to any property of the Owner or other property owner if so requested and permitted by the injured party. Such repair shall be in lieu of the payment of monetary damages to the injured party.

Section 3.03 Right to Perform Additional Work Within or Near the Project Site

a) The Owner reserves the right at any time to contract with other contractors whose work may occur within or near the site of the Project. In such event, the CMAR agrees not to interfere with or hinder the progress of work by the other contractors, and the Owner agrees to require such contractors to coordinate their work with that of the CMAR. The CMAR agrees to cooperate and coordinate with such contractors as directed by the Owner.

b) The CMAR shall arrange the Work and shall place and dispose of the materials being used so as not to interfere with the operations of other contractors within the limits of the same Project. The CMAR shall join the Work with that of the other contractors in an acceptable manner and shall perform it in proper sequence to that of the other contractors.

Section 3.04 Progress Meetings

The Owner shall chair the progress meetings between the parties to the Contract that shall include a representative from each major subcontractor if so requested by the Owner. The CMAR shall take notes of the progress meeting and shall distribute copies to each party within five (5) days after completion of the meeting. The meeting notes shall summarize decisions made at the meeting and reflect the weekly job progress in comparison to the Baseline Project Schedule. The attendees are responsible for remembering their own required action and the conference notes shall serve only as a reminder and record of the required action.

Section 3.05 Right of Suspension

The Owner may, without cause, order the CMAR in writing to suspend, delay or interrupt the Work, in whole or in part, for such period of time as determined by the Owner. An adjustment shall be made for the increase in the cost of performing the Contract but not to exceed 120 calendar days (excluding therefrom any profit to the CMAR Fee), on the increased cost of performance caused by the suspension, delay, or interruption. No adjustment shall be made to the extent that:

a) The performance is, was or would have been so suspended, delayed or interrupted by another cause for which the CMAR is responsible; or

b) An equitable adjustment is made or denied under another provision of the Contract Documents, or

c) The CMAR could have mitigated the increase in cost to perform the Contract.

If the Work is suspended beyond the 120-calendar day period, the provision of 3.06 shall apply and the CMAR will recover from the Owner payment for Work executed, including reasonable negotiated overhead and profit, and costs incurred by reason of such termination.

Section 3.06 Right of Termination for Convenience

a) Prior to, or during the performance of the Work, the Owner reserves the right to terminate the Contract in whole or in part, for any reason whatsoever (including, but not necessarily limited to, funding limitations). Upon such an occurrence the Owner will immediately notify the design professional and the CMAR in writing specifying the effective termination date of the Contract.

b) After receipt of the Notice of Termination, the CMAR shall immediately proceed with the following obligations, regardless of any delay in determining or adjusting any amounts due at the point in the Contract:

   i) Stop all construction;

   ii) Place no further orders for materials or services;

   iii) Terminate all subcontracts;

   iv) Cancel all material and equipment orders as applicable; and

   v) Take whatever action is necessary to protect and preserve all property related to this Contract, which is in the possession of the CMAR.

c) Within 180 days of the date of the Notice of Termination, the CMAR shall submit a final termination settlement proposal to the Owner based upon costs up to the date of termination, including reasonable profit as allowed by the Contract Documents on completed Work, and reasonable demobilization costs as allowed by the Contract Documents. If the CMAR fails to submit the proposal within the time allowed, the Owner may determine the amount due to the CMAR because of the termination and shall pay the determined amount to the CMAR.

d) The CMAR may terminate the Contract if through no act or fault of the CMAR or CMAR Subcontractor, their agents or employees or any other persons or entities, performing portions of the Work under direct or indirect contract with the CMAR, limited to either of the following reasons:

   i) Issuance of an order of a court or other public authority having jurisdiction that requires all Work to be terminated;

   ii) An act of government, such as a declaration of national emergency that requires all Work to be terminated.

Section 3.07 Right to Replace Subcontractor

The Owner shall have the right to require that the CMAR replace any Subcontractor at any time and for any reason by requesting such change in writing in accordance with the provisions of NRS 338.

SECTION 4. CONTRACT COMMENCEMENT, PROGRESS AND COMPLETION

Section 4.01 Notice to Proceed

a) After receipt of all required submittals, including insurance and bonds, the Owner will issue a Notice to Proceed. The CMAR shall not commence construction activities at the Work site prior to the date specified in the Notice to Proceed.

b) If deemed appropriate, the Owner may issue a Material Notice to Proceed to the CMAR authorizing the ordering of supplies, materials, equipment or other items related to the Work prior to issuance of the Notice to Proceed.

Section 4.02 Baseline Project Schedule

Within the time provided in Section 01 32 16 (Progress Schedules) of the Technical Specifications, the CMAR shall submit the Baseline Project Schedule for the Work, which shall contain the appropriate milestones by which the Owner can judge and determine the progress of the Work.

Section 4.03 Progress of the Work

a) The CMAR shall provide sufficient labor, materials, facilities, and equipment and shall work such hours, including night shifts, overtime operations, Saturdays, Sundays and holidays, as may be necessary to insure the prosecution and completion of the Work or separable portions thereof, in accordance with the Baseline Project Schedule.

b) If the progress of the Work falls behind or fails to proceed in accordance with the Baseline Project Schedule, or it becomes apparent to the Owner from the current schedule that the Work will not be substantially complete within the Contract Time (as adjusted by Owner approved Change Orders), in addition to the other requirements of the Contract and remedies available to the Owner, the CMAR agrees to take the following actions at no additional cost to the Owner to correct such tardiness:

   i) Increase manpower in such quantities and crafts as will substantially eliminate, in the judgment of the Owner, the backlog of Work;

   ii) Increase the number of working hours per shift, shifts per working day, working days per week, the amount of equipment, or any combination of the foregoing, sufficient to substantially eliminate, in the judgment of the Owner, the backlog of Work; and,

   iii) Reschedule activities to achieve maximum practical concurrence of accomplishment of activities.

c) The failure of the CMAR to comply with the requirements of this Section or to remedy the tardiness shall be grounds for a determination by the Owner that the CMAR is failing to diligently prosecute the Work, in which case the Owner may, after the notice of the breach has been provided to the CMAR pursuant to Section 10.01 (Definition of Breach) of the Contract, without prejudice to other remedies the Owner may have and regardless of whether the CMAR has taken or is taking corrective action, immediately correct the CMAR's failure at the CMAR's expense by exercising the right to perform and carry out the work as provided in Section 10.05 (Owner's Right to Carry Out the Work) including the use of the Owner's work forces, to award separate contracts, to supplement the CMAR's work forces, to prepare or have prepared schedules which shall be used to determine the provisions of the Contract to withhold actual and anticipated liquidated damages, and any other means the Owner deems appropriate.

Section 4.04 Payment Terms and Definitions

a) **Cost of the Work (and related terms)**

   i) The Cost of the Work includes wages paid, but not bonuses paid, for labor in the direct employ of the CMAR in the performance of the Work, exclusive of the labor that is to be included in the General Conditions. Labor rates, including fringe benefits, shall be in conformance with the applicable Prevailing Wage Rates as published by the Nevada State Labor Commission for this Project. This includes labor and management of CMAR self-performed construction work.

   ii) The Cost of the Work includes employees benefits and taxes for employees including, but not limited to, unemployment compensation, social security, health, welfare, retirement, and other fringe benefits as required by law, labor agreements, or paid under the CMAR's standard personnel policy, insofar as such costs are actually paid to employees of the CMAR detailed in subsection above who are engaged in the Work for employees.

   iii) The Cost of the Work includes the cost of all materials, supplies, and equipment incorporated in the cost of the Work, including costs of certificates of inspection and testing, transportation, storage, and handling, excluding testing and inspections required to be paid for directly by Owner.

   iv) The Cost of the Work includes all payments made by the CMAR to the Subcontractors and suppliers for the cost of the Work performed under the Contract.

   v) The Cost of the Work includes all costs directly incurred in the performance of the Work or in connection with the Project, and not included in the CMAR's Fee, which are reasonably inferable from the Contract Documents as necessary to produce the intended results and not already included in the General Conditions, CMAR Fee or CMAR Contingency.

   vi) Sales, use, gross receipts or other taxes, tariffs or duties related to the cost of the Work for which the CMAR is liable and not already included in the General Conditions, CMAR Fee or CMAR Contingency.

   vii) The CMAR's Cost of the Work includes the cost (including transportation and maintenance) of all supplies, equipment, temporary facilities, and hand tools (not owned by workers) that are used or consumed in the performance of the Work.

viii) The CMAR's Cost of the Work includes rental charges for all necessary machinery and equipment, exclusive of hand tools owned by workers, used for the Work, whether rented from the CMAR or others, including installation, repair and replacement, dismantling, removal, maintenance, transportation, and delivery costs at rates consistent with those prevailing in the area.

ix) CMAR's Cost of the Work includes all temporary water, power, and fuel costs necessary for the Work.

x) CMAR's Cost of the Work includes all cost for removal of all generated non-hazardous substances, debris, and waste materials.

b) **CMAR's General Conditions (and related terms)**

i) The CMAR's General Conditions includes salaries of CMAR's management and administrative employees when stationed at the field office, in whatever capacity employed, excluding construction labor and management of CMAR self-performed construction work, employees engaged on the road expediting the production or transportation of material and equipment, and employees from the principal or branch office performing jobsite functions while located at the principal office; including, by way of example and not limitation, the CMAR's Project manager, Project engineer, Project coordinator, Project estimator, Project scheduler and Project superintendent.

ii) The CMAR's General Conditions includes the cost of CMAR's management and administrative employees including, but not limited to, unemployment compensation, social security, health, welfare, retirement, and other fringe benefits as required by law, labor agreements, or paid under the CMAR's standard personnel policy, insofar as such costs are actually paid to employees of the CMAR detailed in subsection a above who are engaged in the Work for employees.

iii) The CMAR's General Conditions includes sales, use, gross receipts, or other taxes, tariffs, or duties related to the Work for which the CMAR is liable, as they specifically relate to the items included in the General Conditions cost line item.

iv) The CMAR's General Conditions includes all costs associated with establishing, equipping, operating, maintaining, and demobilizing the specified field office(s).

v) The CMAR's General Conditions includes all costs for reproduction, photographs, fax transmissions, long distance telephone calls, data processing services, postage, express delivery charges and on-site telephone service at the CMAR's field office.

vi) The CMAR's General Conditions include all costs related to management of the CMAR's safety program.

vii) The CMAR's General Conditions include the cost of CMAR bonding as stipulated herein.

viii) The CMAR's General Conditions include all required Permits, fees, licenses, and tests not paid by the Owner.

ix) The CMAR's General Conditions include the CMAR's cost of insurance as stipulated in Section 8 herein.

x) The CMAR's General Conditions shall not include transportation, travel, and hotel expenses for the CMAR's personnel incurred in connection with the Work unless specifically approved in writing by the Owner.

c) **CMAR's Fee (and related terms)**

i) The CMAR's Fee includes salaries and other mandatory or customary compensation of the CMAR's employees at its principal and branch offices, except employees assigned to the Project at the principal office. Specifically excluded are CMAR's personnel paid under CMAR's General Conditions.

ii) The CMAR's Fee includes general and administrative expenses of the CMAR's principal and branch offices other than the field office.

iii) The CMAR's Fee includes the CMAR's capital expenses, including interest on the CMAR's capital employed for the Work.

iv) The CMAR's Fee includes the CMAR's profit.

v) The CMAR's Fee excludes CMAR General Conditions (and related items) as listed above.

d) **CMAR's Contingency (and related terms)**

i) The CMAR's Contingency may be used to fund the following:

A) Increases in the Cost of the Work identified through the refinement, development and completion of the Contract Documents or procurement of the Work, including increases in subcontractor or supplier costs, after acceptance by the Owner of the GMP and execution of this Contract. Decreases in the Cost of the Work shall transfer to the CMAR Contingency.

B) Increases in the Cost of the Work for concealed conditions that can be reasonably inferred from the construction documents and/or the Work.

C) Rework by the CMAR that is not a result of the CMAR's or Subcontractor's negligence or lack of coordination or communication with the Consultant or trade Subcontractors.

D) Increase in the cost of the General Conditions. Decreases in the cost of the General Conditions shall transfer to the CMAR Contingency.

E) Any deductible incurred as a result of a Builder's Risk Insurance claim.

ii) The CMAR's Contingency shall not be used to fund the following:

A) Increases in the Cost of the Work as a result of an omission or correction in the Contract Documents that should have been identified through a reasonable constructability check and coordination review of the construction documents by the CMAR during the discharge of the CMAR's pre-construction duties. Design omissions or corrections which the CMAR could have reasonably identified through a reasonable constructability check and coordination review will be resolved on a case-by-case basis.

B) Increases in the Cost of the Work as a result of the CMAR's or subcontractor's negligence or lack of coordination or communication with the Consultant or trade Subcontractors.

iii) The Owner's Contingency shall be used to fund the following:

A) Increase in the Cost of the Work as a result of errors and omissions of the Consultant that could not have been reasonably discovered by the CMAR through a reasonable constructability check and coordination review of the construction documents by the CMAR during the discharge of the CMAR's pre-construction duties.

B) Increases in the Cost of the Work as a result of Building Code compliance or outside agency requirements identified through the refinement, development and completion of the Contract Documents after acceptance by the Owner of the GMP and execution of this Contract or during construction of the Work, including increases in Subcontractor or Supplier costs.

C) Increases in the Cost of the Work due to an unforeseen condition that could not be reasonably foreseeable from the Contract Documents.

D) Increases in the Cost of the Work due to an unavoidable event, including weather, that arises and that could not have been anticipated from the Contract Documents.

iv) For each use of the CMAR's Contingency, the CMAR shall:

A) Notify the Owner in writing no later than fourteen (14) days after the event or first knowledge of the cause that results in a request to use the CMAR Contingency;

B) Attempt to gain Owner approval of the use of the CMAR Contingency prior to the expenditure;

C) Owner approval must be obtained for use of expenditure(s) in excess of $100,000;

D) Provide backup documentation as requested by the Owner to justify the use and amount of the CMAR Contingency request; and

E) Document the approval of the expenditure of the CMAR Contingency though the use of a form acceptable to the Owner.

v) Reference Section 01 26 00 (Contract Modification Procedures) of the Technical Specifications for the allowable CMAR's Contingency mark-ups, including subcontractor mark-up, for overhead and profit.

Section 4.05 Progress Payments and Retainage

a) **Schedule of Values.** Within fourteen (14) days after the issuance of the Notice to Proceed, the CMAR shall submit to the Owner and the Consultant a schedule of values of the various portions of the Work, aggregating to the total Contract Sum, divided to facilitate payments to Subcontractors, prepared in a form acceptable to the Owner, and supported by such data to substantiate its correctness as the Owner may require. This schedule, when approved by the Owner and the Consultant, shall be the basis for each progress payment application. The scheduled costs shall be itemized in accordance with the breakdown listed in the CMAR GMP proposal and according to the list of defined components included in Subsection b below.

b) **Progress Bills and Payments.** The CMAR may submit a monthly progress bill requesting payment for the Work performed to-date after measuring the Work and estimating its value based upon the unit prices contained in the Contract or the approved schedule of values. The progress bill must be submitted and must be accompanied by photographs of the Work completed to date and other supporting documentation (such as material receipts and storage verifications). The quantities and value estimates must have the concurrence of the Owner. As permitted pursuant to Section 10.06 (Deduction from Progress Payments) of these General Conditions and NRS Chapter 338, the Owner may withhold from the progress payment an amount that is sufficient to protect the Owner for the CMAR's failure to comply with the requirements of the Contract or applicable building codes, laws or regulations.

c) **Certified Payroll Reports.** The CMAR must submit certified payroll records each month as required by NRS Chapter 338. If the certified payroll records for the previous month have not been received, the Owner may withhold funds from the progress payment in accordance with NRS Chapter 338. The Owner requires the use of LCP Tracker software for the submission of certified payrolls by the CMAR and all of its Subcontractors.

d) **Retainage.** From the progress payment to be made to the CMAR, the Owner shall deduct and retain an amount equal to five percent (5%) of the amount approved for payment through 50% completion of the work.

e) **Deposits.** CMAR shall notify Owner of any and all deposits made in furtherance of the performance of services under this Contract.

f) **Payment for Stored Material.** The Owner may at its discretion pay the CMAR the cost of the material that is to be used in the performance of the Work provided the material complies with the requirements of the Contract and the following conditions are satisfied:

i) The CMAR stores the material in a manner acceptable to the Owner at the Work site or other site that is acceptable to the Owner.

ii) The CMAR furnishes evidence of the quantity and quality of the stored material that is acceptable to the Owner.

iii) The CMAR furnishes legal title (free of liens or encumbrances of any kind) for the stored material that is acceptable to the Owner.

iv) The CMAR furnishes evidence the stored material is insured against loss, damage or disappearance thereof prior to use in the Work that is acceptable to the Owner.

The transfer of title to, or the payment for, the stored material by the Owner shall in no way relieve the CMAR of responsibility for placing the material in accordance with the requirements of the Contract.

If payment is being sought for material not specifically purchased for the Work, but taken from the CMAR's stock, then in lieu of an invoice, the CMAR shall submit to the Owner a statement and accompanying affidavit certifying that the material was taken from the CMAR's stock and that the claimed material and transportation costs represent the actual costs to the CMAR.

The progress bill requesting payment for the stored material shall not exceed the Contract price for such material or the price for the Contract item comprising the material used by the CMAR.

SECTION 5. COMPLETION OF PROJECT

Section 5.01 Substantial Completion

a) When the CMAR considers the Work or portion thereof has reached Substantial Completion, the CMAR shall so inform the Owner. The Owner shall schedule a walk-through to establish a punch list of items to be completed or corrected by the CMAR.

b) If the Work or any designated portion thereof has reached Substantial Completion, and all applicable governmental authorities have granted final approval of the Work, the Owner will issue a Certificate of Substantial Completion establishing the date of Substantial Completion identifying responsibilities of the Owner and CMAR for security, maintenance, utilities, damage to the work and insurance, and fixing the time for the CMAR to finish the items on the punch list accompanying the Certificate. The Certificate of Substantial Completion shall be submitted to the Owner and CMAR for their written acceptance of responsibilities assigned to them in such Certificate.

c) In the event the CMAR is unwilling to provide written acceptance of the Certificate of Substantial Completion, the Owner shall issue the Certificate without the CMAR's signature, and (i) the CMAR shall immediately comply with the provisions of the Certificate, and any dispute involving the CMAR's unwillingness to provide written acceptance shall be resolved in accordance with Section 12 (Disputes Between the Parties). In such event, the Owner may withhold Liquidated Damages based on the completion date shown on the issued Certificate of Substantial Completion until such time as the dispute is resolved between the parties.

Section 5.02 Punch List

a) The CMAR shall complete or correct the Work identified on the punch list within the time specified on the Certificate of Substantial Completion or as otherwise directed. If the CMAR fails to satisfactorily complete or correct the punch list items, such failure shall constitute a breach of this Contract and the Owner shall have the option to invoke any of the remedies provided for under Section 10.

b) The time stated for completion of punch list items shall include final clean-up of the Work site.

Section 5.03 Final Inspection and Final Acceptance of the Work

When the CMAR considers the Work is complete, the CMAR shall so notify the Owner in writing. If, after inspection and testing, the Owner determines that the Work has been completed as required by the Contract and the Contract otherwise fully performed, the Owner shall inform the CMAR that application for final payment may be made. The Contract shall not be considered to be fully performed until the CMAR provides the Owner with the certificates, guaranties, releases, certified payroll records, affidavits, record documents and other documents required under the Contract. Final acceptance of the Work shall be confirmed by the making of final payment unless otherwise stipulated at the time such payment is made.

Section 5.04 Final Payment

a) Provided the Contract has been fully performed pursuant to Section 5.03 (Final Inspection and Final Acceptance of the Work) of the Contract, the CMAR shall prepare and submit a final payment application for all Work performed under the Contract. The acceptance of final payment shall operate as a release to the Owner by the CMAR of all claims and liabilities for all things done or furnished in connection with the Work and for every act or omission, negligent or otherwise, of the Owner and others relating to or arising out of the Work.

b) No payment, final or otherwise, shall operate to release the CMAR from any obligations under the Contract or the Sureties from any obligations under the Performance Bond, Labor and Material Payment Bond or the Guaranty Bond.

Section 5.05 Non-Conforming Work Not Accepted

Neither final acceptance, the making of final payment, nor the entire or partial occupancy of the completed Work by the Owner, shall constitute an acceptance of the Work, or any portion thereof, not completed in accordance with the requirements of the Contract.

SECTION 6. LIQUIDATED AND DELAY DAMAGES

Section 6.01 Owner's Recovery of Liquidated Damages

a) The CMAR acknowledges that time is an essential element of this Contract and for that reason the Work needs to proceed and be prosecuted vigorously to completion. In the event that the Work is not completed within the Contract Time set forth in Section 5 (Commencement and Contract Time) of the Contract, the CMAR further acknowledges that the Owner will suffer damages which are difficult to ascertain, such as, but not necessarily limited to, the cost associated with additional architectural, engineering, inspection, supervision and contract administration.

b) Because it is difficult and impractical to fix the amount of actual damages which would be suffered by the Owner if the CMAR fails to meet the completion deadline, the parties have agreed that the amount of liquidated damages set forth in Section 6 of the Contract is a reasonable estimate of the damages to be suffered by the Owner.

c) The CMAR agrees to pay the Owner Liquidated Damages for each day that the Work exceeds the completion deadline until the CMAR reaches Substantial Completion of the Work. The Liquidated Damages provided for therein pertain only to the failure to complete the Work by the completion deadline, and does not preclude recovering any increased costs incurred by the Owner in completing the Work. Liquidated Damages shall be in addition to any other remedies resulting from delays that may be available to the Owner, which in the aggregate shall not exceed the CMAR's Fee as set forth in Section 3.C. By executing the Contract, the CMAR agrees that the amount of liquidated damages set forth therein is fair and reasonable.

d) If the Owner permits the CMAR to complete the Work, or any part thereof, after the completion deadline or any extensions thereto, such permission shall not be construed as a waiver on the part of the Owner of any of its rights or remedies under the Contract.

e) The Owner's right to withhold Liquidated Damages pursuant to the provisions of this Section, or any other section of the Contract, is self-executing, and is not subject to the notice of claim and dispute resolution procedures set forth in Section 12 (Disputes Between the Parties) of the Contract. If the CMAR disagrees with the assessment or withholding of any Liquidated Damages, such disagreement shall be treated as a dispute between parties subject to the notice of claim and alternative dispute resolution procedures set forth in that Section.

Section 6.02 Delay Damages

a) The CMAR shall not make any claim against the Owner for an increase in the Contract Amount, or for any damages, losses or additional expenses which the CMAR may suffer as a result of any delay in the completion of the Work (regardless of the circumstances giving rise to the delay), with the exception of the following:

   i) Delays so unreasonable in length as to amount to an abandonment of the Project,

   ii) Delays caused by fraud, misrepresentation, concealment or other bad faith by the Owner,

   iii) Delays caused by active interference by the Owner, or

   iv) Delays caused by a decision by the Owner to significantly add to the scope or duration of the public work.

b) If any of the exceptions set forth in (i) through (iv) above are determined by the Owner to be applicable, the Owner may grant a time extension commensurate with the delay, increase the Contract Amount and/or consider for payment a claim for damages, losses or additional expenses resulting from any delay in the completion of the Work provided such claim meets the requirements set forth in Section 12 (Disputes Between the Parties) of this Contract. The Owner shall determine the validity of the claim and the amount to be paid, and such consideration or payment shall not invalidate, limit or otherwise waive the prohibition provisions of this Section with respect to any future delay claims of the CMAR.

c) Without limiting the circumstances that may cause delays for which the CMAR is assuming the risk for CMAR's delay damages, the following possible delay circumstances for which a time extension may be considered within the contemplation of the parties:

   i) Unknown or uncertain conditions including, but not necessarily limited to, the discovery of caliche, ground water and all other subsurface conditions,

   ii) Weather conditions (including, but not limited to, precipitation, flood, mud slides, sink holes, ice and snow resulting from precipitation, wind, temperature or humidity) and the resultant effects thereof regardless of the nature, duration, severity or abnormality of such weather condition,

   iii) Unmarked utilities or utility interferences,

   iv) Events of war, labor disputes, transportation delays, freight embargos, earthquakes, floods, epidemics, terrorist threats or acts, workplace violence, theft, vandalism damage to the Work (including fire and explosion), disruptions in labor or materials resulting from a health crisis regardless of whether epidemic, pandemic or isolated to areas from which such labor and materials are supplied; acts of God and all other events, acts or omissions resulting in the unavailability of labor, materials, equipment or utilities,

v) Acts or omissions of the Owner and other governmental authorities acting in their role as code and regulation enforcement regulators,

vi) Acts or omissions of contractors, subcontractors, suppliers and material manufacturers involved in the Work,

vii) Acts, omissions and coordination of other contractors regardless of the event location or contractual relationship between the parties, unless such contractors are under the direction or control of the Owner, or under the direction or control of a general contractor of the Owner, and

viii) Discovery of hazardous substances or substances suspected of being hazardous,

d) This Section shall apply to any claim described as a "disruption," "acceleration," "suspension," "schedule change," "impact to the progress of the Work" or some other term avoiding use of the term "delay."

e) No CMAR claim for delay and impact damages shall be computed or determined on the basis of the Eichleay formula or a related formula to allocate unabsorbed overhead costs or expenses. Any claim and impact damages shall be computed or determined on the basis of actual damages incurred by the CMAR.

SECTION 7. BONDING REQUIREMENTS

Section 7.01 Required Bonds

The CMAR shall obtain and maintain throughout the term of this Contract the bonds required in Exhibit J, incorporated herein by this reference. CMAR shall comply with the terms and conditions set forth in Exhibit J.

Section 7.02 Acceptable Surety

Surety companies executing bonds must be licensed to issue surety by the State of Nevada Insurance Division pursuant to Nevada Revised Statute Chapter 683A and bonds must be issued by an appointed producer of insurance pursuant to Nevada Revised Statute Chapter 683A.

Section 7.03 Failure to Maintain Bonds

If, for any reason, the bonds are not maintained in effect as required herein, the surety files for protection under the federal bankruptcy laws or similar state laws or the surety rating decreases from that required under Section 7.2 (Acceptable Surety) of the Contract, the Owner may require the CMAR to procure bonds from another surety to be substituted in lieu of the bonds originally provided to the Owner, and the failure to procure the substitute bonds shall constitute a breach of the Contract entitling the Owner to any of the remedies set forth in Section 10 (Breach of Contract and Remedies) of the Contract.

SECTION 8. INSURANCE REQUIREMENTS

Section 8.01 Insurance

The CMAR shall obtain and maintain the insurance coverage required in Exhibit J incorporated herein by this reference. CMAR shall comply with the terms and conditions set forth in Exhibit J.

Section 8.02 Acceptable Insurance

Insurance companies issuing certificates of insurance must be licensed by the State of Nevada Insurance Division and certificates of insurance must be issued by an appointed producer of insurance pursuant to Nevada Revised Statute Chapter 683A.

Section 8.03 Failure to Maintain Insurance

The CMAR's failure to provide or maintain any of the insurance coverage required herein shall constitute a breach of the Contract. In addition to the remedies that the Owner may have pursuant to Section 10 (Breach of Contract and Remedies) of the General Conditions, the Owner may take whatever action is necessary to maintain the current policies in effect (including the payment of any premiums that may be due and owing by the CMAR) or procure substitute insurance. The CMAR is responsible for any costs incurred by the Owner in maintaining the current insurance coverage in effect, or providing substitute insurance, and such costs may be deducted from any sums due and owing the CMAR.

SECTION 9. INDEMNITY

Section 9.01 General Indemnity

a) The CMAR shall protect, indemnify and hold the Owner, its officers, employees, agents and consultants (collectively the "Indemnitees") harmless from any and all claims, liabilities, damages, losses, suits, actions, decrees, and judgments (including attorney fees, court costs) or other expenses of any and every kind or character (collectively the "Claims"), which may be recovered from or sought against the Indemnitees as a result of, by reason of, or as a consequence of, any act or omission, negligent or otherwise, on the part of the CMAR, its officers, employees, agents, Subcontractors or suppliers (i) in the manufacturing or supplying (including transportation) of any materials, supplies or other products used in the Work, or (ii) in the performance of the terms, conditions and covenants of the Contract, regardless of whether the Claims were caused in part by the Indemnitees. The Owner may retain for its protection any money due and owing the CMAR under this Contract. In the event no money is due and owing, the surety, if required, of the CMAR, may be held until all of the Claims have been settled and suitable evidence to that effect furnished to the Owner.

b) It is expressly agreed that the CMAR shall defend the Indemnitees against the Claims and in the event that the CMAR fails to do so, the Owner shall have the right, but not the obligation, to defend the same and to charge all direct and incidental costs, including attorney's fees and court costs to the CMAR. Nothing in the aforementioned Section 9.01 shall require the CMAR to indemnify the Indemnitees for the claims or damages arising out of the sole negligence of the Indemnitees.

Section 9.02 Patent Indemnity

a) The CMAR shall protect, defend and hold the Owner, its officers, employees, agents and consultants (collectively the "Patent Indemnitees") harmless from and against all claims, losses, costs, damages, and expenses, including attorney fees, court costs or other expenses (collectively the "Patent Claims"), incurred by the Patent Indemnitees, or any of them, respectively, as a result of or in connection with any claims or actions based upon infringement or alleged infringement of any patent and arising out of the use of the equipment or materials furnished under the Contract by the CMAR, or out of the processes or actions employed by, or on behalf of, the CMAR in connection with the performance of the Contract. The CMAR shall, at its sole expense, promptly defend against any such claim or action unless directed otherwise by the Patent Indemnitees; provided that the Patent Indemnitees shall have notified the CMAR upon becoming aware of such claims or actions, and provided further that the CMAR's aforementioned obligations shall not apply to equipment, materials or processes furnished or specified by the Patent Indemnitees.

b) In order to avoid such claims or actions, the CMAR shall have the right, at its expense, to substitute non-infringing equipment, materials or processes, or to modify such infringing equipment, materials and processes so they become non-infringing, or to obtain the necessary licenses authorizing the use of the infringing equipment, material or processes, provided that such substituted and modified equipment, materials and processes shall meet the requirements of this Contract.

SECTION 10. BREACH OF CONTRACT AND REMEDIES

Section 10.01 Definition of Breach

If, during the existence of the Contract, the CMAR:

a) Fails to properly pay any Subcontractor or other parties for labor, materials or supplies as required by Section 2.13 (Responsibility for Payment of Subcontractors and Other Parties) of the Contract;

b) Fails to begin the Work within the time specified in the Notice to Proceed as required by Section 4.01 (Notice to Proceed) of the Contract;

c) Fails to diligently prosecute the Work as required by Section 4.02 (Guaranteed Project Schedule) or Section 4.03 (Progress of the Work) of the Contract;

d) Fails to provide sufficient workmen, materials or equipment to assure the prompt completion of the Work as required by Section 4.03 (Progress of Work) of the Contract;

e) Fails to complete the Work within the Contract Time as required by Section 5 (Commencement and Contract Time) of the Contract;

f) Fails to complete the punch list within the time specified in the Certificate of Substantial Completion as required by Section 5.02 (Punch List) of the Contract;

g) Fails to maintain the bonds, industrial insurance coverage for his employees, general liability insurance or any of the other policies of insurance as required by Sections 7.01 (Required Bonds) and 8.01 (Required Insurance) of the Contract;

h) Fails to pay third party claims as required by Section 9.01 (General Indemnity) of the Contract;

i) Fails to maintain licensure by the Nevada State Contractors Board as required by Section 11.01 (General Warranty) of the Contract;

j) Fails to promptly remedy the Work not in conformance with the Contract as required by Section 11.03 (Warranty Work Conforms with Requirements of the Contract);

k) Fails to observe laws, ordinances, rules or regulations pertaining to the Project as required by Section 13.01 (General) of the Contract;

l) Fails to investigate, or cooperate in the investigation of, complaints concerning the payment of prevailing wage rates requested by the Owner or the State Labor Commissioner's Office as required by Section 13.02 (Compliance with Labor Laws) of the Contract;

m) Fails to maintain solvency, allows a judgment to stand against the CMAR for a period of five (5) days, files a petition with the United States Bankruptcy Court, is adjudged insolvent or bankrupt, makes a general assignment for the benefit of creditors, or commits an act of bankruptcy or insolvency; or

n) Fails to remedy any other material breach of the provisions of the Contract; then the occurrence of any of the above shall constitute a breach of the Contract which if unremedied may constitute an Event of Default as described in Section 10.02 (Event of Default).

Section 10.02 Event of Default

a) The CMAR and the Surety under the Performance Bond shall be entitled to seven (7) days' notice of each breach described in Section 10.01 (Definition of Breach) of the Contract and given the opportunity within such time to cure the breach, provided, however, such breach is capable of a cure. If such breach is capable of a cure but by its nature cannot be cured within the seven day period, the CMAR or Surety may be allowed such additional time as may be reasonably necessary to cure the breach provided the cure is commenced within the seven day period and is diligently pursued to completion.

b) If any breach is not subject to cure, or is not cured as provided herein, the Owner may declare that an "Event of Default" has occurred and the Owner may, in addition to any other remedies available in law or equity, invoke any of the remedies provided for under this Section 10 (Breach of Contract and Remedies) of the Contract.

Section 10.03 Damages

Except for those breaches which are subject to Liquidated Damages set forth in Section 6.01 (Owner's Recovery of Liquidated Damages), if the CMAR fails to cure any Event of Default under this Contract within the time provided in Section 10.02 (Event of Default), the Owner shall be entitled to damages resulting therefrom.

Section 10.04 Termination for Cause

a) Upon the occurrence of an Event of Default, the Owner may terminate the Contract which shall take effect immediately upon service of the notice on the CMAR and the Surety under the Performance Bond unless a different effective date is specified therein. In the event of such termination, the Surety shall have the right to take over and perform the Contract.

b) If the Surety does not commence performance of the Contract within ten (10) days of receipt of the notice, the Owner may do any and all of the following:

i) Take possession of the Project Site and the materials, equipment, tools, and construction equipment and machinery thereon owned by the CMAR;

ii) Accept the assignment of the CMAR's subcontracts pursuant to this Contract (Contingent assignment of subcontracts to Owner if Contract is terminated); and

iii) Finish the Work by whatever method deemed expedient by the Owner.

c) The CMAR shall not be entitled to any further payment under the Contract until the Work is completed and accepted by the Owner. If the unpaid balance of the Contract Amount exceeds the cost of completing the Work, including compensation for any damages or expenses incurred by the Owner through the default of the CMAR, the excess shall be paid to the CMAR. If, however, the damages and expenses exceed the unpaid balance of the Contract Amount, the CMAR and the Surety under the Performance Bond shall pay the difference to the Owner.

Section 10.05 Owner's Right to Perform the Work

a) If the CMAR fails to perform or proceed with the Work, or any part thereof, as required by the Contract, and fails within the seven (7) day notice required pursuant to Section 10.02 (Event of Default) of the Contract to remedy the breach, or to commence and continue correction of such breach with promptness and due diligence toward completion, the Owner may, without prejudice to any other right or remedy available to the Owner, and without terminating the Contract and relieving the CMAR from its obligations under the Contract, proceed to correct the breach, or applicable portion thereof, by any means or methods deemed appropriate (including use of the Owner's personnel).

b) If the Owner discovers during the course of the corrective action that the breach is greater or otherwise different from, but nevertheless related to, the breach described in the seven-day notice, then the greater or different breach shall be deemed to have been included in the original seven-day notice and the Owner may proceed with the corrective action without having to provide any additional notice to the CMAR.

c) If, after expiration of the seven-day notice period required pursuant to Section 10.02 (Event of Default) of the Contract, the CMAR proceeds to correct the breach and the Owner has already incurred certain expenses (such as, but not necessarily limited to, preparation of cost estimates or remedial plans and drawings, placement of material orders,

demolition costs, rental costs, storage costs, trash removal expenses, utility expenses, scheduled commitments from contractors which cannot be canceled without the Owner incurring costs to the contractor, transportation costs of personnel or materials, and incurred cost of hiring technical personnel whether licensed or not) as part of an effort to remedy the breach, then the CMAR shall pay the Owner for such incurred expenses as provided herein.

d) If, after issuance of the seven day notice of the breach required pursuant to Section 10.02 (Event of Default) of the Contract, the Owner decides not to take any action to correct the breach or fails in the effort to correct the breach, the CMAR remains responsible for the breach and any expenses incurred in any failed effort to correct the breach.

e) In the event of a correction and expense as provided herein, the Contract Amount shall be reduced by the amount of the incurred expenses which amount the Owner shall be entitled to deduct from any payments then or thereafter due the CMAR (including the direct and indirect costs of using the Owner's personnel). If payments then or thereafter due the CMAR are not sufficient to cover the incurred expenses, the CMAR shall pay the difference to the Owner.

Section 10.06 Deduction From Progress Payments

a) For each and every breach set forth in Section 10.01 (Definition of Breach) of the Contract, the Owner may decline to certify, in whole or in part, any pending application for payment which, in the opinion of the Owner, may be necessary to protect the Owner from the damages and expenses which are expected to be incurred, or which have been incurred, as a result of the breach. Based upon the opinion of the Owner, the Owner may withhold from any requested progress payment such sum as may be necessary to protect the Owner from such damages and expenses including, but not necessarily limited to, the Liquidated Damages permitted pursuant to Section 6.01 (Owner's Recovery of Liquidated Damages) of the Contract which the Owner anticipates will occur as a result in the delay in the Completion of the Project.

b) If an agreement can be reached between the Owner and the CMAR concerning the request for payment, the CMAR shall promptly submit a revised application for certification. The Owner shall have the right to deny in whole or in part, or to require an adjustment to, any pending application if, as a result of new evidence or observations subsequent to the issuance of a previous certification, the Owner has determined that the amount paid exceeds the percentage of completion of the Work, the Work cannot be completed for the unpaid balance of the Contract or any other such certification was improperly issued.

c) If the CMAR remedies the failure for which payment has been withheld, and the Owner verifies such correction, then the withheld money shall be included with the payment of the next application.

Section 10.07 Rights and Remedies are Cumulative

Except as otherwise expressly stated in the Contract, the rights and remedies of the parties are cumulative, and the exercise by any party of one or more of such rights or remedies shall not preclude the exercise by it, at the same or different times, of any other rights or remedies for the same default or any other default by the other party.

SECTION 11. REPRESENTATIONS AND WARRANTIES

Section 11.01 General Representations and Warranties

The CMAR hereby represents and warrants that it (a) is familiar with requirements of the Contract; (b) has investigated the site and is knowledgeable concerning the local conditions that may affect the performance of the Work; (c) is satisfied that the Work can be performed and completed as required in the Contract; (d) accepts all of the risks directly or indirectly connected with the performance of the Contract; (e) has not been influenced by any statement or promise other than those contained in the Contract Documents; (f) is experienced and competent to perform the Contract; (g) is familiar with all general and special laws, ordinances and regulations that may affect the Work, its performance, or those persons employed therein; (h) is familiar with tax and labor regulations and with rates of pay that will affect the Work, and (i) is properly licensed and will remain properly licensed by the CMARs Board of the State of Nevada in order to perform the Contract.

Section 11.02 Warranty of Merchantability and Fitness for Particular Purpose

The CMAR warrants that the equipment and materials used or provided as part of the Contract are of merchantable quality and fit for their particular purpose.

Section 11.03 Warranty Work Conforms with Requirements of the Contract

a) In addition to other warranties and longer time periods which may be provided in the Contract, and as a minimum, the CMAR warrants the Work performed under the Contract is in conformance with the requirements of the Contract, and that the Work is free of defects and deficiencies in design, materials and workmanship (unless furnished by the Owner) for a period of twelve (12) months from the date of the Certificate of Substantial Completion (or 12 months from the completion date of any portions of the Work first performed after Substantial Completion), regardless of whether the same were furnished or performed by the CMAR or by any of its Subcontractors of any tier. Upon receipt of written notice from the Owner of any non-conformance to the Contract during the applicable warranty period, the CMAR shall promptly correct the affected non-conformance at a time acceptable to the Owner.

b) The CMAR shall perform such tests as the Owner may require verifying that the Work is in compliance with the Contract. If such Work is not in accordance with the Contract, the costs of the correcting and testing, including the cost of removal necessary to gain access thereto and other related incidental costs, shall be borne by the CMAR. If such Work is found to be in accordance with the Contract, the costs of uncovering, replacement, and testing shall be charged to the Owner. The CMAR warrants any corrected Work to be in conformance with the Contract for a period of twelve (12) months from the date of acceptance thereof. If the CMAR fails to promptly make the necessary corrections and tests, the Owner may perform or cause to be performed the same at the CMAR's expense. The CMAR and its Surety shall be liable for the satisfaction and full performance of the warranties set forth in this Section.

c) Unless otherwise provided elsewhere in the Contract, the materials and equipment incorporated into the Work shall be new and of the most suitable grade of their respective kinds for their intended use, and all workmanship shall be in accordance with construction practices acceptable to the Owner.

d) Nothing contained in this Section shall be construed to establish a period of limitation with respect to the CMAR's obligations under the Contract other than specifically to correct the Work then known by the Owner to be in non- conformance with the Contract, including, but not limited to, defects and deficiencies in design, materials and workmanship (unless furnished by the Owner).

Section 11.04 Warranty Exclusions Prohibited

a) The Owner will not accept any warranty clause from the CMAR, Subcontractor or manufacturer that states:

   i) That the implied warranties of Merchantability or Fitness for a Particular Purpose are excluded from the Contract;

   ii) That the warranty clause is in lieu of all other warranties that are either expressed or implied.

b) In addition to the above restrictions, the warranty requirements of the Contract shall exist in a direct extension from the manufacturer to the Owner as well as from the CMAR to the Owner if the manufactured product is sold directly to the CMAR.

SECTION 12. DISPUTES BETWEEN THE PARTIES

Section 12.01 In General

Any claim, dispute or other controversy that may arise between the Owner and CMAR concerning any provision of this Contract shall be resolved through the good faith efforts of both parties. In accordance with NRS 338.150, if the claim, dispute or controversy cannot otherwise be settled, the parties shall use an alternate dispute resolution method before initiation of any judicial action. For purposes of this Contract, alternate dispute resolution shall mean non-binding mediation before an independent private mediator agreed to by the parties. If the parties cannot agree upon an independent private mediator within forty-five (45) days after notice of the claim is provided pursuant to Section 12.04 below, the party may proceed to file a judicial action with the Eighth Judicial District Court, Clark County, Nevada. The alternate dispute resolution proceedings shall take place in Clark County, Nevada, unless otherwise agreed to by the parties.

Section 12.02 Work to Proceed

While the alternate dispute resolution or judicial action is pending, the CMAR shall proceed with the Work and maintain progress in accordance with the requirements of the Contract, unless otherwise mutually agreed upon in writing.

Section 12.03 Alternate Dispute Resolution Costs and Fees

The fees and expenses of the alternate dispute resolution proceedings shall be equally shared by both parties. Each party is responsible for their own costs, expenses, consultant fees and attorney fees incurred in the presentation or defense of any claim, dispute or controversy that may arise between the parties.

Section 12.04 Notice of Disputes

In the event that a claim, dispute, or controversy arises between the parties which are related to the progress or construction of the Project, the party asserting the claim, dispute or controversy must provide written notice thereof to the other party within thirty (30) days after its occurrence. The written notice shall set forth with specificity the nature of the claim, dispute or controversy, the relief sought, and other matters properly relating thereto. The notification is important to the recipient of the notice so that proper measures can be taken to properly observe and record the progress of the Work, to properly document the impact that the claim, dispute or controversy may have thereon, and to enable that party to properly verify any costs incurred by the party asserting the claim, dispute or controversy in connection therewith. The failure of the party to provide proper notice to the other party as required herein shall forever bar that party from any remedy thereon, including seeking any alternate dispute resolution and/or judicial action. The notice and time requirements set forth herein shall not apply to warranty claims or other construction defect claims that the Owner may have against the CMAR relating to the construction of the Work.

Section 12.05 Right of Judicial Action

Any claim, dispute, or other matter in question between the parties concerning any provisions of this Contract that cannot otherwise be resolved between the parties through the use of the alternate dispute resolution required herein and, in the case of the CMAR, which has not been waived by the acceptance of final payment, may be submitted for judicial action. Prior to the exercise of this right, the party seeking judicial relief shall have provided the other party thirty (30) days prior written notice before filing such judicial action.

SECTION 13. COMPLIANCE WITH THE LAWS

Section 13.01 General

The CMAR shall comply with all federal, state and local laws and regulations applicable to construction of the Work including, but not necessarily limited to, licensing requirements, labor and health laws, and requirements for the payment of sales and use taxes on equipment, materials and supplies provided in connection with the Contract.

Section 13.02 Compliance with Labor Laws

a) **Prevailing Wage Rate Law**. The CMAR and each Subcontractor shall comply with all federal, state and local labor laws with regard to minimum wages, overtime work, hiring and discrimination including, without limitation, NRS Chapter 338.

b) **Prevailing Wage Rates.** For public work projects whose cost is one hundred thousand dollars ($100,000) or more, the CMAR hereby acknowledges that pursuant to the provisions of NRS 338.040 and 338.050, any person who is employed by the CMAR or Subcontractor at the Work Site, or who performs work on a public work project (regardless of any contractual relationship alleged to exist between the workman and his other employer), is subject to the prevailing wage rate provisions of NRS 338.010 to 338.090, inclusive.

   The CMAR is responsible for ensuring that the aforementioned persons are paid in accordance with the current prevailing wage rates approved by the State Labor Commissioner. Any Change Order causing a contract to equal or exceed one hundred thousand dollars ($100,000) will subject the Contract to the provisions of Prevailing Wage Rate Law and to audit by the State Labor Commissioner. Any work performed after regular working hours, or on Sunday or a legal holiday, shall be performed without additional expense to the Owner.

In accordance with NRS Chapter 338, the CMAR shall post the current prevailing wage rates and applicable addenda in a place generally visible to the workmen. The prevailing wage rates and applicable addenda are available from the office of the State Labor Commissioner (www.Labor.NV.gov). The CMAR agrees to investigate, or to assist in the investigation of, each claimed violation of the prevailing wage law as may be requested by the Owner or the State Labor Commissioner.

Should this project exceed 36 months from the bid opening, which is determined to be upon receipt of the final GMP, new prevailing wage rates shall apply. All labor rates shall remain firm from the date of the bid opening through 36 months. An updated Exhibit – Prevailing Wage Rates will be effective on the first day of the 37 month from the date of the bid opening and new prevailing wages shall apply. New prevailing wages will be obtained from the State of Nevada Labor Commissioner's Office prevailing wages at the time of the 37 month. Subject to the prevailing wage rate provisions of NRS 338.010 to 338.090 inclusive andAssembly Bill No. 190.

c) **Certified Payroll Reports.** Pursuant to NRS Chapter 338, any public work contract awarded for one hundred thousand dollars ($100,000) or more, the CMAR and each Subcontractor are required to:

i) Keep an accurate record showing the (A) name of worker, (B) occupation of the worker, (C) if the worker has a driver's license or identification card, an indication of the state or other jurisdiction that issued the license or card, and (D) the actual per diem wages and benefits paid to each worker employed by them in connection with the Work. These records are referred to as the Certified Payroll Reports.

ii) Keep an additional accurate record showing, for each worker employed by the CMAR or Subcontractor who has a driver's license or identification card (A) the name of the worker, (B) the driver's license or identification card number of the worker, and (C) the state or other jurisdiction that issued the license or card.

iii) The CMAR, and each Subcontractor through the CMAR, is required to submit a copy of the Certified Payroll Reports for each calendar month to the Owner no later than fifteen (15) calendar days after the end of the month. The CMAR shall be responsible for coordinating the submittal of all the Certified Payroll Reports for the Project, including the reports of each Subcontractor who is performing Work on the Project. The Owner requires the use of LCP Tracker software for the submission of certified payrolls by the CMAR and all of its Subcontractors.

The CMAR agrees to contact the Nevada State Labor Commissioner with any question concerning the payment of prevailing wage rates.

d) **Penalties.** In accordance with NRS 338.060, the CMAR shall forfeit the penalty provided herein to the Owner for each calendar day or portion thereof that each workman employed on the Project (i) is paid by the CMAR or Subcontractor less than the designated wage rate for the work on the Project, (ii) the CMAR or Subcontractor willfully included inaccurate or incomplete information in the monthly Certified Payroll Report submitted to the Owner, (iii) the CMAR or Subcontractor did not report to the Owner as required pursuant to NRS 338.070, and/or (iv) if a violation of more than one provision of subsection (i) through (iii) herein involves the same workman, the CMAR shall forfeit the penalty set forth in each violated subsection.

The CMAR hereby stipulates that the Owner may withhold not less than twenty dollars ($20.00), nor more than fifty ($50.00) for each and every violation of subparagraphs (i) through (iii) herein, the actual amount of which is according to a sliding scale based on the size of the CMAR's business which is adopted by the State Labor Commissioner, except that for violation of subparagraph (iii) the maximum penalty is limited to one thousand ($1,000) for the first violation and five thousand ($5,000) for each subsequent violation occurring during the term of the Contract.

In addition to any penalty imposed by the Labor Commissioner, if the CMAR or Subcontractor is determined by the Owner to have violated the provisions of this Section, the Owner may deduct from any payments due the CMAR, the costs of the proceedings associated with the investigation of each wage complaint including, but not limited to, employee salaries, investigator fees and attorney fees.

In addition to any monetary penalty imposed by the statute, the CMAR, or its Subcontractor, agent or representative, performing Work on the Project who neglects to comply with the prevailing wage rate requirements of NRS Chapter 338 is guilty of a misdemeanor.

e) **Copeland Anti-Kickback Law**. The CMAR shall comply with the Copeland Anti- Kick Back Act (19 U.S.C. 874) as supplemented in the Department of Labor Regulations (29 CFR Part 3). This Act provides that the CMAR or Subcontractor shall be prohibited from inducing by any means, any person employed in the construction, completion or repair of public work, to give up any part of the compensation to which that person is otherwise entitled.

f) **Fair Employment Law**. The CMAR shall comply with the fair employment provisions of NRS 338.125.

i) Discrimination:

The Owner is committed to promoting full and equal business opportunity for all persons doing business in Clark County, Nevada. The CMAR acknowledges that the Owner has an obligation to ensure that public funds are not used to subsidize private discrimination. CMAR recognizes that if the CMAR or their subcontractors are found guilty by an appropriate authority of refusing to hire or do business with an individual or company due to reasons of race, color, religion, sex, sexual orientation, gender identity or gender expression, age, disability, national origin, or any other legally protected status, the Owner may declare the CMAR in breach of contract and terminate the Contract.

ii) Fair Employment Practices

In connection with the performance of work under this Contract, the CMAR agrees not to discriminate against any employee or applicant for employment because of race, color, religion national origin, sex, sexual orientation, gender identity or gender expression, age, disability, or any other legally protected status. Such agreement shall include, but not be limited to, the following: employment; upgrading; demotion or transfer; recruitment or recruitment advertising; layoff or termination; rates of pay or other forms of compensation; and selection for training, including apprenticeship.
The CMAR further agrees to insert this provision in all subcontracts hereunder. Any violation of such provision by the CMAR or its subcontractors shall constitute a material breach of this Contract.

g) **Preferential Employment. (This Section IS___IS NOT___ Applicable to this Contract)** The CMAR shall comply with the preferential employment provisions of NRS Chapter 338.130. This law requires, in all cases where persons are employed in the construction of public works, preference must be given, when the qualifications of applicants are equal: First, to persons who have been honorably discharged from the Army, Navy, Air Force, Marine Corps or Coast Guard of the United States, a reserve component thereof or the National Guard, and are citizens of the State of Nevada; Second, to other citizens of the State of Nevada. If these provisions of NRS 338 are not complied with by the CMAR engaged on the public work, the contract shall be void, and any failure or refusal to comply with any of these provisions of this section renders any such contract void.

h) **Federal Wage Rates. (This Section IS___IS NOT___ Applicable to this Contract)** The CMAR shall comply that the Federal Wage Rates attached (*Attachment Exhibit*) and incorporated herein as a part hereof which are applicable to the Contract. The wages paid under the Contract shall conform to the Davis-Bacon Act of March 3, 1931, as amended (46 Stat. 1494, as amended, 40 U.S.C. 276a to 276a-7) as supplemented by Department of Labor Regulations (29- CFR, Part 5). If the State Wage Rates and Federal Wage Rates are not equal, the CMAR shall pay the higher prevailing rate.

i) **Special Requirements. (This Section IS___IS NOT___ Applicable to this Contract)** The CMAR shall comply with the requirements of Federal Requirements (*Attachment Exhibit I*), incorporated herein as a part hereof, which are applicable to the Contract.

Section 13.03 Compliance with Americans with Disabilities Act (ADA)

The Work shall comply with the ADA as amended to date. The CMAR shall construct the Work in compliance with the Americans with Disabilities Act and the rules and regulations promulgated thereunder and shall immediately notify the Owner of any conflicts between the Contract Documents and the Act or the rules and regulations promulgated thereunder.

Section 13.04 Compliance with Immigration Reform Control Act of 1986

In accordance with the Immigration Reform and Control Act of 1986, the CMAR shall not employ unauthorized aliens in the performance of the Contract.

Section 13.05 Air Pollution Control

a) Prior to commencing the Work, the CMAR shall obtain a permit from the Clark County Department of Air Quality and Environmental Management.

b) The CMAR shall perform the Work in a manner that does not discharge smoke, dust, or other air contaminants into the atmosphere from any source whatsoever, in violation of the laws, rules, and regulations of federal, state, and local government pertaining to air pollution including, but not necessarily limited to, the following:

i) Nevada Revised Statute 445: Air Quality Regulations.
ii) Title 40 Code of Federal Regulations (CFR) Part 82 Protection of Stratospheric Ozone – Refrigerant Regulations.
iii) Adhering to all Clark County Department of Air Quality and Environmental Management regulations.

c) The CMAR shall not be granted any time extensions for delays due to compliance with or violations of the aforementioned laws, rules, or regulations; and shall pay all compliance costs and violation fines and penalties. Such imposed fines and penalties shall not result in an increase in the Contract Amount, and are not subject to reimbursement by the Owner.

Section 13.06 Fire Prevention

a) The CMAR shall conform to all federal, state, and local laws and regulations pertaining to burning, fire prevention, and control within or adjacent to the Work Site. Necessary precautions to avoid and eliminate fire hazards shall be the responsibility of the CMAR.

b) All tarpaulins used for any purpose during construction of the Work shall be made of material resistant to fire, water, and weather and shall bear UL labels. Lighting of any fires on the Project Site is strictly forbidden.

c) The CMAR shall provide portable fire extinguishers compatible with the hazard of each work area and shall instruct its personnel in their location and use. Wherever welding or burning is conducted, inflammable materials shall be protected and a fire watch shall be provided by the CMAR to be present during the burning and welding operation to ensure that protective measures are taken and no fires result from such operation. The fire watch shall have fire extinguisher equipment readily available and know-how for proper use.

Section 13.07 Provisions Required by Law

Each and every provision of Nevada Revised Statutes Chapter 338 and 624 and any other laws required to be inserted in this Contract shall be deemed to be inserted herein and the Contract shall be read and enforced as though it were included herein, and if through mistake or otherwise any such provision is not inserted, or inserted incorrectly, then upon the application of either party, the Contract shall be amended to make such insertion or correction.

Section 13.08 Stormwater Pollution Control

a) Prior to commencing the Work, the CMAR shall obtain a National Pollutant Discharge Elimination System (NPDES) permit from Nevada Division of Environmental Protection (NDEP) for construction activities.

b) The CMAR shall perform the Work so as to not discharge stormwater runoff containing pollutants or sediment into the waters of the United States (including municipal separate storm sewer systems [MS4s]) in violation of federal and state laws, rules, and regulations.

c) The CMAR shall:

i) Comply with the provisions of Nevada Revised Statutes, Chapter 445A: Water Pollution Control.
ii) Adhere to all Federal regulations under 40 CFR 122.26(b)(14).
iii) Provide to the Owner, prior to commencing construction operations, copies of all associated Permits or waivers.

d) All information and forms pertaining to Nevada's Stormwater NPDES Permitting Program can be found on the following website: http://ndep.nv.gov/bwpc/storm01.htm.

e) The county, state, and federal regulations identified above are hereby incorporated by reference as preconditions of this Contract. The CMAR shall familiarize itself with these regulations and practices, and is advised that prior to engaging in any construction activities, the CMAR shall submit a Notice Of Intent (NOI) to the Nevada Division of Environmental Protection. A Storm Water Pollution Prevention Plan (SWPPP) must be completed prior to submission of the NOI and must remain on the Project site and be updated as necessary for the duration of the project. As applicant, the CMAR is responsible for insuring that all persons on the Project site, including contractor and subcontractor personnel, abide by the conditions of the permit. As the applicant, the CMAR is responsible for supplying complete copies of the NOI and SWPPP to all project subcontractors.

f) Upon completion of the Project, the CMAR must (at no additional cost to the Owner) permanently stabilize the construction area and file a Notice Of Termination (NOT) with NDEP to terminate the permit.

g) The CMAR shall not be granted any time extensions for delays due to compliance with or violations of the aforementioned laws, rules, regulations, and requirements and shall pay all compliance costs and violation fines and penalties. Such imposed fines and penalties shall not result in an increase in the Contract Amount, and are not subject to reimbursement by the Owner.

Section 13.09 Disposal of All Wastes (Hazardous, Toxic, and Non-Hazardous)

a) CMAR shall be responsible for disposal of all waste materials including non-hazardous, hazardous, or toxic materials. CMAR shall make its own arrangements for disposal or recycle of all waste materials and shall pay all costs associated with the proper disposal of all waste.

b) CMAR shall obtain written verification in terms of the landfill weight ticket, recycling certificate from the disposal site owner or operator with a written release from the disposal site owner or operator absolving the Owner of any and all responsibility in connection with the disposal of waste material on said property.

c) Unless otherwise provided, full compensation for all costs involved in disposing of materials as specified in this section, including all costs of hauling, shall be considered as included in the price paid for the Contract items of work involving such material and no additional compensation will be allowed therefore.

d) No waste material that is to be disposed shall be stockpiled on the Owner's property or the Project site longer than seven (7) days, unless otherwise approved by the Owner. Prior to initiating construction, the CMAR shall provide to the Owner a proposed temporary stockpile location. Construction debris and materials shall not be stockpiled in unapproved locations.

e) For hazardous or toxic materials waste, CMAR shall comply with all local, State, and federal regulations including but not limited to Resources Conservation and Recovery Act (RCRA), Toxic Substance Control Act (TSCA). CMAR must fill out the Waste Manifest and provide a copy of the Manifest to the Owner. CMAR (or its subcontractor) shall provide all necessary licenses or permits documentation for handling, transportation and disposal of hazardous or toxic materials as submittal information to the Owner. CMAR is responsible to identify/classify the hazardous waste, getting an EPA hazardous waste site number by filing the paperwork with NDEP as the hazardous waste generator, retaining certified RCRA hazardous waste transporter subcontractor, properly dispose the RCRA hazardous waste in certified hazardous waste treatment or landfill sites, deactivated the EPA hazardous waste site number when the job is done, and provide safe handling training to CMAR employees.

Section 13.10 Compliance with National Environmental Policy Act (NEPA)

If this contract is sponsored in whole or part through Federal funding, CMAR is required to comply with NEPA requirements including but not limited to, compliance with Clean Air Act, Clean Water Act, Endangered Species Act, National Historic Preservation Act, Migratory Bird Treaty Act, Resource Conservations and Recovery Act (RCRA), Toxic Substance Control Act (TSCA).

Section 13.11 Use of Apprentices

Contractor represents that it and its subcontractors will comply with Senate Bill 82 of the 82nd Legislative Session of the Nevada Legislature (2023) ("SB 82"), and NRS 338.01165 regarding the hiring of apprentices from a valid Apprenticeship Program (recognized by the State Apprenticeship Council) for the applicable type of public work (as defined in NRS 338.010).

A Contractor and/or Subcontractor engaged in a Vertical Construction who employs a worker pursuant to NRS 338.040 shall use one or more apprentices for at least 10 percent of total hours of labor in each apprenticed craft or type of work to be performed for which more than three workers are employed on a public work.

A Contractor and/or Subcontractor engaged in a Horizontal Construction who employs a worker pursuant to NRS 338.040 shall use one or more apprentices for at least 3 percent of total hours of labor in each apprenticed craft or type of work to be performed for which more than three workers are employed on a public work.

Contractor shall factor compliance with SB 82 into their pricing, including when a Contractor and/or Subcontractor, who is a signatory to a collective bargaining agreement with a union that sponsors an apprenticeship program for an apprenticed craft or type of work for which the term of apprenticeship is not more than three (3) years, requests an apprentice from that apprenticeship program, and an apprentice in the appropriate craft or type of work is not available, and that Contractor and/or Subcontractor then utilizes a person who graduated from the apprenticeship program in that craft or type of work within the three (3) years immediately preceding the request from that Contractor and/or Subcontractor. All change orders submitted to the County seeking the difference in cost for a Contractor and/or Subcontractor utilizing the option set forth in the previous sentence, and as more fully set forth in SB 82, will not be accepted by COUNTY.

SECTION 14. CONTRACT INTERPRETATION

Section 14.01 General

a) **Governing Law.** The Contract shall be construed and enforced in accordance with the laws of the State of Nevada. Any action for the enforcement of any provision of this Contract shall be instituted in the County of Clark, State of Nevada.

b) **References Hereto.** The terms "hereby," "hereof," "herein," "hereunder" and any similar terms refer to this Contract; and the term "hereafter" means after, and the term "heretofore" means before, the Contract Award Date.

c) **Gender and Plurality.** Words of the masculine gender mean and include correlative words of the feminine and neuter genders and words importing the singular number mean and include the plural number and vice versa.

d) **Persons.** Words importing persons include firms, companies, associations, joint ventures, general partnerships, limited partnerships, limited liability corporations, trusts, business trusts, corporations and other legal entities, including public bodies, as well as individuals.

e) **Headings.** The table of contents and any headings preceding the text of the Articles, Sections and subsections of this Contract shall be solely for convenience of reference and shall not affect its meaning, construction or effect.

f) **Entire Contract.** This Contract includes the requirements of the Plans and Specifications, the General Conditions and all appendices and clarifications thereto. Without limiting the generality of the foregoing, This Contract shall completely and fully supersede all other understandings and agreements among the Parties related to the execution of this Contract.

g) **Standards of Workmanship and Materials.** Any reference in this Contract to materials, equipment, systems or supplies (whether such references are in lists, notes, Specifications, schedules, or otherwise) shall be construed to require the CMAR to furnish the same in accordance with the grades and standards therefore indicated in this Contract. Where this Contract does not specify any explicit quality or standard for construction materials or workmanship, the CMAR shall use only workmanship and new materials of a quality consistent with that of construction, workmanship and materials specified elsewhere in the Specifications, and the Specifications are to be interpreted accordingly.

h) **Technical Standards and Codes.** References in this Contract to all professional and technical standards, codes and specifications are to the most recently published professional and technical standards, codes and specifications of the institute, organization, association, Owner or society specified, all as in effect as of the Contract Award Date. Unless otherwise specified to the contrary, (i) all such professional and technical standards, codes and specifications shall apply as if incorporated in the Specifications, and (ii) if any material revision occurs, to the CMAR's knowledge, after the Contract Date, and prior to completion of the applicable Work, the CMAR shall notify the Owner. If so directed in writing by the Owner, the CMAR shall perform the applicable Work in accordance with the revised professional and technical standard, code, or specification as long as the Guaranteed Maximum Price is adjusted, subject to cost substantiation, for any additional cost or expense attributable to any such revision.

i) **Causing Performance.** A Party shall itself perform, or shall cause to be performed, subject to any limitations specifically imposed hereby with respect to Subcontractors or otherwise, the obligations affirmatively undertaken by such Party under this Contract.

j) **Party Bearing Cost of Performance.** All obligations undertaken by each Party hereto shall be performed at the cost of the Party undertaking the obligation or responsibility, unless the other Party has explicitly agreed herein to bear all or a portion of the cost either directly, by reimbursement to the other Party or through an adjustment to the Guaranteed Maximum Price.

k) **Assistance.** The obligations of a Party to cooperate with, to assist or to provide assistance to the other Party hereunder shall be construed as an obligation to use the Party's personnel resources to the extent reasonably available in the context of performance of their normal duties, and not to incur material additional overtime or third party expense unless requested and reimbursed by the assisted Party.

l) **Good Construction Practice.** Good Construction Practice shall be utilized hereunder, among other things, to implement, and in no event displace or lessen the stringency of, the Contract Specifications or Contract Standards. In the event that, over the course of the performance of this Contract, Good Construction Practice evolves in a manner which in the aggregate materially and adversely affects the cost of compliance therewith by the CMAR, the CMAR shall be relieved of its obligation to comply with such evolved Good Construction Practice (but not the Good Construction Practice as of the Contract Award Date) unless the Owner agrees to adjust the Guaranteed Maximum Price on a cost- substantiated basis, as appropriate, to account for such additional costs. Except to the extent that the CMAR is relieved of its obligation to comply with such evolved Good Construction Practice, as provided above, in no event shall any evolution of Good Construction Practice, or any Owner election to pay or not pay any such additional costs, relieve the CMAR of its obligations hereunder.

m) **Applicability and Stringency of Contract Standards.** The CMAR shall be obligated to comply only with those Contract Standards which are applicable in any particular case. Where more than one Contract Standard applies to any particular performance obligation of the CMAR hereunder, each such applicable Contract Standard shall be complied with. In the event there are different levels of stringency among such applicable Contract Standards, the most stringent of the applicable Contract Standards shall govern.

n) **Delivery of Documents in Digital Format.** In this Contract, the CMAR is obligated to deliver reports, records, proposals and other documentary submittals in connection with the performance of its duties hereunder. The CMAR agrees that all such documents shall be submitted to the Owner both in printed form (in the number of copies indicated) and, at the Owner's request, in digital form. Digital copies shall consist of computer readable data submitted in Adobe PDF format which the Owner may reasonably request to facilitate the administration and enforcement of this Contract. If drawings, native AutoCAD files should be submitted unless an alternate format is requested by the Owner. In the event that a conflict exists between the signed or the signed and stamped hard copy of any document and the digital copy thereof, the signed or the signed and stamped hard copy shall govern. The Owner uses the Microsoft Office Suite of software and Primavera Expedition for contract administration

o) **Drafting Responsibility. Neither Party** shall be held to a higher standard than the other Party in the interpretation or enforcement of this Contract as a whole nor any portion hereof based on drafting responsibility.

p) **No Third-Party Rights.** This Contract is exclusively for the benefit of the Owner and the CMAR and shall not provide any third parties with any remedy, claim, liability, reimbursement, cause of action or other rights.

q) **References to Include.** All references to "include" or "including" herein shall be deemed to be followed by the words "but not be limited to" or "without limitation" or words of similar import.

Section 14.02 Intent and Correlation

The Contract is intended to include all items necessary for the proper execution and completion of the Work. The Contract Documents are complementary, and what is required by one portion or section of the Contract shall be as binding as if required by all. Any work not covered in the Contract will not be required unless it is consistent with the Contract Documents, and it is reasonably inferable or necessary to produce the intended results or provide a complete work. Words and abbreviations, which have well known technical or trade meanings, are used in the Contract Documents in accordance with such recognized meanings.

Section 14.03 Governing Order of Contract Documents

The Contract Documents include various divisions, sections, and conditions, which are essential parts for the work to be provided by the CMAR. In case of discrepancy, the lower number document will govern over the higher numbered document according to the following order of precedence, unless to do so would contravene the intent of the Contract Documents as determined by the Owner:

a) Change Orders
b) Addenda, with those of later date having precedence over those of an earlier date
c) CMAR Construction Contract
d) General Conditions
e) Special Provisions, Drawings and Referenced Standards (these documents are to be construed together in determining the intent of the Owner)

Section 14.04 Conflicting Conditions

In the event of inconsistencies within or between parts of the Contract Documents, or between the Contract Documents and applicable standards, codes and ordinances, the CMAR shall (a) provide the better quality or greater quantity of Work or (a) comply with the more stringent requirement; either or both in accordance with the Owner's interpretation.

Section 14.05 Graphic Enhancement

Graphic enhancement of any text of the Contract such as bolding, underlining, italics, etc. is added for ease of reference and shall not be interpreted as placing additional importance on the enhanced text or lessening the importance of text without such enhancement.

SECTION 15. MISCELLANEOUS PROVISIONS

Section 15.01 Regulatory Authorities

a) The CMAR does hereby acknowledge and agrees that Owner or Owner's Designated Representative for purposes of the Project, does not have any control, authority or influence over the decisions or requirements of regulatory authorities which are separate from the Owner, or which are departments of the Owner including, but not limited to, the Building Department, Fire Department, Planning Department or other divisions within the Department of Public Works acting in a regulatory manner. The CMAR is responsible for complying with the requirements imposed by the regulatory authorities (including the departments of the Owner acting in a regulatory manner) and any delays resulting to the CMAR in the performance of the Contract from having to comply with such requirements are solely the responsibility of the CMAR, and not attributable in any manner to the Owner.

b) The Owner's Designated Representative acts in a capacity similar to that of a representative working for a private property owner which is to ensure that the Owner receives a quality product, delivered on schedule, for a fair price. Furthermore, the Owner's Designated Representative does not speak or act for any regulatory authority, nor does any regulatory authority speak or act for the Owner's Designated Representative. The CMAR agrees that its relationship with the regulatory authorities having jurisdiction over the Project is separate from its relationship with the Owner's Designated Representative, and that the CMAR's interaction with each regulatory authority is to be conducted without assistance from the Owner's Designated Representative.

Section 15.02 Subcontracts

a) Any subcontract entered into by the CMAR and its Subcontractor or material Supplier shall not create any contractual relationship between the Owner and the Subcontractor or material Supplier. It is the CMAR's responsibility to ensure all subcontract agreements and material supply contracts comply with the term and conditions set forth in this Contract and applicable Statutes

b) The CMAR agrees to provide a copy of each subcontract (including contracts for the purchase of supplies) entered into by the CMAR in connection with the Project if so requested by the Owner for any of the reasons set forth in NRS 338.140 (1)(d).

c) The CMAR shall not substitute a Subcontractor for any portion of the Work which was previously indicated would be performed by the CMAR unless such substitution meets the requirements of NRS Chapter 338.

d) If the CMAR submitted with its proposal a signed and notarized Affidavit and received a preference in bidding, the contract between the CMAR and Subcontractor and each contract between a subcontractor and a lower-tier subcontractor must provide that;

(i) If a party to the contract causes the CMAR to fail to comply with the requirements of the Affidavit, the party is liable to the Owner for a penalty as defined by statute:

(ii) The right to recover the amount determined pursuant to paragraph (a) by the Owner may be enforced by the Owner directly against the party that causes the failure to comply; and

(iii) No other party to the contract is liable to the Owner for a penalty.

Section 15.03 Audit of Records

a) The CMAR agrees to maintain the financial books and records (including supporting documentation) pertaining to the performance of this Contract according to standard accounting principles and procedures. The books and records shall be maintained for a period of three (3) years after completion of this Contract, except that books and records which are the subject of an audit finding shall be retained for three (3) years after such finding has been resolved. If the CMAR goes out of business, the CMAR shall forward the books and records to the Owner to be retained by the Owner for the period of time required herein.

b) The Owner, or its Designated Representative(s), shall have the right to inspect and audit (including the right to copy and/or transcribe) the books and records of the CMAR pertaining to the performance this Contract during normal business hours. The Owner will provide prior written notice to the CMAR of the audit and inspection. If the books and records are not located within Clark County, the CMAR agrees to deliver them to the Owner, or to the address, designated by the Owner, within Clark County. In lieu of such delivery, the CMAR may elect to reimburse the Owner for the cost of travel (including transportation, lodging, meals and other related expenses) to inspect and audit the books and records at the CMAR's office. If the books and records provided to the Owner are incomplete, the CMAR agrees to remedy the deficiency after written notice thereof from the Owner, and to reimburse the Owner for any additional costs associated therewith including, without limitation, having to revisit the CMAR's office. The CMAR's failure to remedy the deficiency shall constitute a material breach of this Contract. The Owner shall be entitled to its costs and reasonable attorney fees in enforcing the provisions of this Section.

c) If, at any time during the term of this Contract, or at any time after the expiration or termination of the Contract, the Owner or the Owner's Designated Representative(s) finds the dollar liability is less than payments made by the Owner to the CMAR, the CMAR agrees that the difference shall be either: (i) repaid immediately by the CMAR to the Owner, or (ii) at the Owner's option, credited against any future billings due the CMAR.

Section 15.04 Independent Contractor

The CMAR represents that it is fully experienced and properly qualified to perform the class of Work provided for herein, and that it is properly licensed, equipped, organized and financed to perform such Work. The CMAR shall act as an independent contractor and not as an agent of the Owner in performing the Contract. The CMAR shall maintain complete control over its employees and all of its subcontractors. Nothing contained in the Contract or any subcontract awarded by the CMAR shall create any contractual relationship between any such subcontractor and the Owner. The CMAR shall perform the Work in accordance with its own methods subject to compliance with the Contract.

Section 15.05 Severability

The invalidity, illegality, or unenforceability of any provision of the Contract or the occurrence of any event rendering any portion or provision of the Contract void shall in no way affect the validity or enforceability of any other portion or provision of the Contract. Any void provision shall be deemed severed from the Contract, and the balance of the Contract shall be construed and enforced as if the Contract did not contain the particular portion of provision held to be void. The parties further agree to amend the Contract to replace any stricken provision with a valid provision that comes as close as possible to the intent of the stricken provision. The provisions of this clause shall not prevent the entire Contract from being void should a provision which is of the essence of the Contract to be determined void.

Section 15.06 Assignment of Contractual Rights

The CMAR shall not assign, transfer, convey or otherwise dispose of the Contract or its right, title or interest in or to the same, or any part thereto without prior written consent of Owner and any sureties. Any attempt by CMAR to assign or otherwise transfer any interest in this Contract without the prior written consent of Owner shall be void.

Section 15.07 Ownership and Use of Documents

The Drawings and Special Provisions are and shall remain the Owner's property unless a consultant is used in the preparation of the Contract Documents in which case ownership shall be according to the agreement between the Owner and the Consultant. They are to be used only with respect to the Project and are not to be used on any other project. Submission or distribution to meet official regulatory requirements for other purposes in connection with the Project is not to be construed as infringement of the copyright of the Owner's or Consultant's common law or other reserved rights.

Section 15.08 Prohibited Interests

No official of the Owner, who is authorized in such capacity and on behalf of the Owner to negotiate, make, accept or approve, or take part in negotiating, making, accepting, or approving any architectural, engineering, inspection, construction or material supply contract or any subcontract in connection with the construction of the Project, shall become directly or indirectly interested personally in the Contract or in any part hereof. No officer, employee, architect, attorney, engineer or inspector of, or for the Owner, who is authorized in such capacity and on behalf of the Owner to exercise any legislative, executive, supervisory or other similar functions in connection with the construction of the Project, shall become directly or indirectly interested personally in the Contract or in any part hereof, any material supply contract, subcontract, insurance contract, or any other contract pertaining to the Project.

Section 15.09 Waiver

No waiver of any breach or failure to enforce any of the terms, conditions or covenants of the Contract shall be construed to be a waiver of any succeeding breach of the same or similar provision of the Contract.

Section 15.10 No Personal Liability

No official, officer, employee or agent of the Owner shall in any way be personally liable or responsible for any covenant or agreement herein contained, whether expressed or implied, or for any statement, representation or warranty made in connection with the Contract.

Section 15.11 Contract Modification

The Contract represents the entire and integrated agreement between the Owner and the CMAR and supersedes prior negotiations, representations or agreements, either written or oral, made by either party. The Contract may only be amended by a Modification.

Section 15.12 Required Reporting for Bidder's Preference on Public Work Projects

a) In accordance with NRS 338.0117 for contracts awarded as the result of the bidders' preference being received, CMAR shall maintain, and submit as required, the reports as indicated in this Section 15.12. It is the CMAR's responsibility to maintain, documentation required to substantiate the information provided in the reports, including information for all Subcontractors on the Project.

b) At least 50 percent of the workers employed on the Project, including, without limitation, any employees of the CMAR and of any Subcontractor engaged on the Project, will hold a valid driver's license or identification card issued by the State of Nevada Department of Motor Vehicles ("DMV");

i) The CMAR shall keep or cause to be kept, for both the CMAR and all Subcontractors, an accurate record showing, for each worker employed by the CMAR or Subcontractor in connection with the Project:

A) The name of the worker;

B) The occupation of the worker;

C) If the worker has a driver's license or identification card, an indication of the state or other jurisdiction that issued the license or card; and

D) The actual per diem, wages and benefits paid to the worker.

ii) An additional accurate record showing, for each worker employed by the CMAR or Subcontractor in connection with the public work who has a driver's license or identification card;

A) The name of the worker;

B) The driver's license number or identification card number of the worker; and

C) The state or other jurisdiction that issued the license or card.

iii) The records maintained pursuant to paragraph (i) above must be must be open at all reasonable hours to the inspection by the Owner and the public as provided by NRS 239.010. The CMAR engaged on the Project shall ensure that a copy of each record for each calendar month is received by the Owner no later than fifteen 15 days after the end of the month. The copy of the record maintained pursuant to paragraph (ii) is confidential and **not open** to public inspection. The CMAR shall maintain the records for a minimum of two years after final payment is received from the Owner.

c) All vehicles used primarily for the Project will be:

i) Registered and partially apportioned to Nevada pursuant to the International Registration Plan, as adopted by the DMV pursuant to NRS 707.826; or

ii) Registered in the State of Nevada;

A) The CMAR shall keep or cause to be kept, for both the CMAR and all Subcontractor vehicles primarily used on the Project, an accurate record, updated monthly, showing a listing of vehicles being used on this Project. The list must include the Nevada State license plate number and registration information for both General CMAR and Subcontractors vehicles.

B) The records maintained pursuant to paragraph must be open at all reasonable hours to the inspection by the Owner and the public as provided in NRS 239.010. The CMAR shall maintain the records for a minimum of two years after final payment is received from the Owner.

d) If applying to receive a preference in bidding pursuant to subsection 3 of NRS 338.1727 or subsection 2 of NRS 408.3886, a t least 50 percent of the design professionals working on the Project, including, without limitation, employees of the Design-Build team and of any Subcontractor engaged on the Project, will have a valid driver's license or identification card issued by the State of Nevada DMV;

i) The CMAR shall keep or cause to be kept, for design professionals employed by either the CMAR and all Subcontractors, an accurate record, updated monthly, of the following information:

A) The name of the design professional;

B) The state or other jurisdiction that issued the license or card

C) The drivers' license number of identification card number of the design professional; and

ii) The records maintained pursuant to paragraph (i) subsection (A) and (B) must be open at all reasonable hours to the inspection by the Owner and the public as provided in NRS 239.010. The copy of the record maintained pursuant to paragraph (i) subsection (C) is confidential and not open to public inspection. The CMAR shall maintain the records for a minimum of two years after final payment is received from the Owner.

e) The CMAR and any Subcontractor engaged on the Project will maintain and make available for the inspection within this State his or her records concerning payroll relating to the Project.

Section 15.13 Owner's Recovery of Bidders Preference Penalties

a) If the Owner determines that the CMAR has failed to comply with a requirement certified in its Public Works Bidders Preference Affidavit the Owner may seek to recover by civil action penalties for failure to comply in the amount defined by statute.

b) If the CMAR submitted with its Proposal a signed and notarized Affidavit receives a preference in bidding and is awarded the construction contract, the contract between the CMAR and Owner must provide that;

i) If a party to the contract causes the CMAR to fail to comply with the requirements of the Affidavit, the party is liable to the Owner for a penalty as defined by statute:

ii) The right to recover the amount determined pursuant to paragraph (a) by the Owner may be enforced by the Owner directly against the party that causes the failure to comply; and

iii) No other party to the contract is liable to the Owner for a penalty.

Section 15.14 Counterpart Signatures

This Contract may be executed in counterparts. All such counterparts will constitute the same contract and the signature of any party to any counterpart will be deemed a signature to, and may be appended to, any other counterpart. Executed copies hereof may be delivered by facsimile or e-mail and upon receipt will be deemed originals and binding upon the parties hereto, regardless of whether originals are delivered thereafter.

The parties agree that this Contract may be signed electronically via the Owner's designated electronic signature platform, and that the electronic signatures appearing herein shall be considered the same as handwritten signatures for the purposes of validity, admissibility, and enforceability.

Section 15.15 Prison Rape Elimination Act Compliance

CMAR must comply with the Prison Rape Elimination Act (PREA) of 2003 (Federal Law 42 U.S.C. 15601 et.seq.), with all applicable PREA standards, with all applicable policies related to PREA and standards related to PREA for preventing, detecting, monitoring, investigating, and eradicating any form of sexual abuse within Clark County Detention Center (CCDC) or North Valley Complex (NVC) facilities/offices owned, operated, or contracted. CMAR acknowledges that, in addition to "self-monitoring requirements" Detention Services Division (DSD) will conduct announced or unannounced, compliance monitoring to include "on-site" monitoring. Failure to comply with PREA, including PREA standards and DSD policies may result in termination of this Contract.

Section 15.16 Detention Facilities

Nevada Revised Statute (NRS) 211.030 provides that the Sheriff is the custodian of the jails in his county and of the prisoners therein and that he shall keep the jails personally, or by his deputy or by a jailer or jailers appointed by him for that purpose, for whose acts he is responsible; LVMPD through its Detention Services Division (DSD) operates the Clark County Detention Center (CCDC) and the North Valley Complex (NVC). Accordingly, LVMPD DSD is COUNTY'S representative for all operations of the CCDC and NVC.

CMAR shall be fully and solely responsible for safety and health conditions for conducting all operations under this Contract and at all times in such a manner as to avoid the risk of endangerment to health, bodily harm to persons, and damage to property. CMAR shall continually and diligently inspect all equipment, materials and work to discover any conditions which might involve such risks and shall be solely responsible for discovery and correction of any such conditions CMAR shall furnish all safety equipment, supplies and instructions required for the work and enforce the proper use of such by its employees, agents, subcontractors and any and all sub-tier levels and suppliers. CMAR shall notify COUNTY in writing of the name of their assign employee responsible for safety and health including a twenty-four (24) hour telephone number prior to commencement of work. CMAR shall comply with all requirements of Nevada Revised Statute Chapter 618, Occupational Safety and Health, Nevada Administrative Code Chapter 618 and have established an active Safety Program in accordance therewith.

Section 15.17 Gratuities

a) Owner may, by written notice to CMAR, terminate this Contract if it is found after notice and hearing by Owner that gratuities (in the form of entertainment, gifts, or otherwise) were offered or given by CMAR or any agent or representative of CMAR to any officer or employee of Owner with a view toward securing a contract or securing favorable treatment with respect to the awarding or amending or making of any determinations with respect to the performance of this Contract.

b) In the event this Contract is terminated as provided in paragraph 1 hereof, Owner shall be entitled:

   i) to pursue the same remedies against CMAR as it could pursue in the event of a breach of this Contract by CMAR; and

   ii) as a penalty in addition to any other damages to which it may be entitled by law, to exemplary damages in an amount (as determined by Owner) which shall be not less than three (3) nor more than ten (10) times the costs incurred by CMAR in providing any such gratuities to any such officer or employee.

c) The rights and remedies of Owner provided in this clause shall not be exclusive and are in addition to any other rights and remedies provided by law or under this Contract.

Section 15.18 Covenant

CMAR covenants that it presently has no interest and that it will not acquire any interest, direct or indirect, which would conflict in any manner or degree with the performance of services required to be performed under this Contract. CMAR further covenants, to its knowledge and ability, that in the performance of said services no person having any such interest shall be employed.

Section 15.19 Disclosure of Ownership Form

CMAR agrees to provide the information on the attached Disclosure of Ownership/Principals form prior to any contract and/or contract amendment to be awarded by the Board of County Commissioners.

Section 15.20 Authority

Owner is bound only by Owner's agents acting within the actual scope of their authority. Owner is not bound by actions of one who has apparent authority to act for Owner. The acts of Owner's agents which exceed their contracting authority do not bind Owner.

Section 15.21 Non-Endorsement

As a result of the selection of CMAR to supply goods or services, Owner is neither endorsing nor suggesting that CMAR'S service is the best or only solution. CMAR agrees to make no reference to Owner in any literature, promotional material, brochures, sales presentations, or the like, without the express written consent of Owner.

Section 15.22 Public Records

Owner is a public agency as defined by state law, and as such, is subject to the Nevada Public Records Law (Chapter 239 of the Nevada Revised Statutes). Under the law, all of Owner's records are public records (unless otherwise declared by law to be confidential) and are subject to inspection and copying by any person. All Contract documents are available for review following the award of the Contract.

Section 15.23 Companies that Boycott Israel

CMAR certifies that, at the time it signed this Contract, it was not engaged in, and agrees for the duration of the Contract, not to engage in, a boycott of Israel. Boycott of Israel means, refusing to deal or conduct business with, abstaining from dealing or conducting business with, terminating business or business activities with or performing any other action that is intended to limit commercial relations with Israel; or a person or entity doing business in Israel or in territories controlled by Israel, if such an action is taken in a manner that discriminates on the basis of nationality, national origin or religion. It does not include an action which is based on a bona fide business or economic reason; is taken pursuant to a boycott against a public entity of Israel if the boycott is applied in a nondiscriminatory manner; or is taken in compliance with or adherence to calls for a boycott of Israel if that action is authorized in 50 U.S.C. § 4607 or any other federal or state law.

Section 15.24 State of Nevada Legal Holidays

CMAR is advised that below there are 10 firm legal holidays and 11 when December 31st falls on Friday.

Martin Luther King's Birthday
Presidents' Day
Memorial Day
Juneteenth
Independence Day
Labor Day
Nevada Admission Day
Veteran's Day
Thanksgiving Day and the Friday After
Christmas Day
New Year's Day

Section 15.25 Close-out Documentation

As a part of the required Contract close-out documentation, CMAR shall submit a Summary Report of Material Suppliers and Subcontractors listing the name of the Subcontractor, work performed, the Business Enterprise Group (BEG), Ethnicity Status, and Value of the contracts. The close-out document shall be submitted in a manner that substantially meets the format and content of the form attached hereto as Close-out Documentation Summary Report of Subcontractors. See **Exhibit**

The Business Enterprise Categories are defined as follows:

a) MINORITY OWNED BUSINESS ENTERPRISE (MBE):
An independent and continuing business for profit, which performs a commercially useful function and is at least 51 percent owned and controlled by one or more minority persons of African American (AA), Hispanic American (HA), Asian-Pacific American (AX) or Native American (NA) ethnicity.

b) WOMEN OWNED BUSINESS ENTERPRISE (WBE):
An independent and continuing business for profit, which performs a commercially useful function and is at least 51 percent owned and controlled by one or more women.

c) PHYSICALLY CHALLENGED BUSINESS ENTERPRISE (PBE):
An independent and continuing business for profit, which performs a commercially useful function and is at least 51 percent owned and controlled by one or more disabled individuals pursuant to the federal Americans with Disabilities Act.

d) SMALL BUSINESS ENTERPRISE (SBE):
An independent and continuing business for profit which performs a commercially useful function, is not owned and controlled by individuals designated as minority, women, or physically challenged, and where gross annual sales does not exceed $2,000,000.

e) VETERAN OWNED ENTERPRISE (VET):
A Nevada business at least 51% owned/controlled by a veteran.

f) DISABLED VETERAN OWNED ENTERPRISE (DVET):
A Nevada business at least 51% owned/controlled by a disabled veteran.

g) EMERGING SMALL BUSINESS (ESB):
Certified by the Nevada Governor's Office of Economic Development effective January 2014. Approved into Nevada Law during the 77th Legislative session as a result of AB294.

The information provided by CMAR is for Owner's information only, as requested by the Board of County Commissioners.

Section 15.26 Utilities

CMAR shall, at its expense, arrange for, develop and maintain all utilities in work areas to meet the requirements of the Contract. Such utilities shall be furnished by CMAR at no additional cost to Owner.

Section 15.27 Taxes

CMAR shall pay all taxes, levies, duties and assessments of any nature that may be applicable to any work under this Contract. The Contract amount and any approved change orders amounts shall include all taxes imposed by law. CMAR shall make any and all payroll deductions required by law. CMAR herein indemnifies and holds Owner harmless from any liability regarding any and all such taxes, levies, duties, assessments and deductions.

Section 15.28 Labor Strife

CMAR shall not cause or condone labor strife that may jeopardize the timely and efficient completion of public construction projects.

Section 15.29 Change Orders

CMAR shall comply with all provisions and conditions which are required by an approved change order between Owner and CMAR. In the event a change order adjusts the GMP Price and/or the Contract term, associated costs and fees as outlined in this Contract shall apply.

Section 15.30 Uniform Standard Specifications for Public Works Construction Off-Site Improvements Does Not Apply to Section 105.17(C)

Section 105.17(c) of the Uniform Standard Specifications for Public Works Construction Off-Site Improvements, Clark County Area, Nevada, current edition and all revisions through date of advertisement, does not apply to this Contract.

RFP 607319-24
EXHIBIT B - GMP SCHEDULE OF VALUES

THE WHITING-TURNER CONTRACTING COMPANY

Clark County Fire Training Center
GMP - Permit Set Construction Documents - 03/20/2026

MASTERFORMAT SUMMARY

DIVISION	FIRE STATION 7,666 GSF 1 S			TRAINING BUILDING 8,000 GSF 1 E			GARAGE 30,000 GSF 2 APP			MAINTENANCE BUILDING 20,000 GSF 1 BE			BURN TOWER 0,000 GSF 0			SITE DEVELOPMENT 4.5 ACRES SITE			PROJECT TOTAL 191,537 GSF		
	COST	$/SF	% COW	COST	$/SF	% COW	COST	$/SF	% COW	COST	$/SF	% COW	COST	$/SF	% COW	COST	$/ACRE	% COW	COST	$/SF	% COW
1 General Requirements	$	$	0.00%	$ 280,000	$ 11.16	2.32%	$ 95,000	$ 1.01	0.83%	$	$	0.00%	$	$	0.00%	$ 120,000	$ 26,310.61	1.62%	$ 1,056,000	$ 5.51	1.43%
2 Existing Conditions	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$ 176,119	$ 69,895.77	2.42%	$ 476,119	$ 2.49	0.64%
3 Concrete	$ 263,000	$ 30.35	3.54%	$	$	0.00%	$ 10,155,500	$ 110.20	29.76%	$ 801,000	$ 11.54	4.43%	$ 15,000	$ 18.18	1.26%	$	$	0.00%	$ 10,873,800	$ 56.77	14.68%
4 Masonry	$ 450,000	$ 51.92	6.51%	$	$	0.00%	$ 418,000	$ 5.35	2.80%	$ 182,956	$ 8.29	3.00%	$	$	0.00%	$	$	0.00%	$ 950,096	$ 4.96	1.28%
5 Metals	$ 443,500	$ 51.30	6.36%	$ 2,991,679	$ 47.79	9.50%	$ 210,000	$ 2.28	1.87%	$ 587,620	$ 23.84	6.67%	$ 1,030,918	$ 104.01	8.61%	$	$	0.00%	$ 5,281,105	$ 27.57	7.13%
6 Wood, Plastics and Composites	$ 187,500	$ 50.27	2.72%	$ 240,095	$ 10.75	3.41%	$	$	0.00%	$ 23,000	$ 0.12	0.03%	$	$	0.00%	$	$	0.00%	$ 1,239,795	$ 6.47	1.67%
7 Thermal & Moisture Protection	$ 892,166	$ 102.99	13.07%	$ 6,917,417	$ 99.53	19.47%	$	$	0.00%	$ 67,931	$ 1.89	1.07%	$	$	0.00%	$	$	0.00%	$ 7,943,057	$ 41.47	10.73%
8 Openings	$ 416,135	$ 48.05	6.08%	$ 1,292,011	$ 72.14	5.31%	$	$	0.00%	$ 328,118	$ 15.91	1.40%	$	$	0.00%	$	$	0.00%	$ 2,641,564	$ 13.79	3.57%
9 Finishes	$ 823,310	$ 101.92	12.06%	$ 8,231,261	$ 128.91	25.86%	$ 193,913	$ 2.10	1.70%	$ 1,562,638	$ 23.46	16.91%	$	$	0.00%	$	$	0.00%	$ 10,934,694	$ 57.09	14.77%
10 Specialties	$ 91,348	$ 10.61	1.33%	$ 682,909	$ 9.81	1.97%	$ 527,765	$ 5.72	3.56%	$ 111,111	$ 5.67	1.20%	$	$	0.00%	$	$	0.00%	$ 1,154,064	$ 6.03	1.56%
11 Equipment	$ 96,961	$ 11.15	1.41%	$ 537,733	$ 7.69	1.54%	$ 10,000	$ 0.11	0.08%	$ 863,281	$ 39.71	8.89%	$	$	0.00%	$	$	0.00%	$ 1,447,097	$ 7.56	1.95%
12 Furnishings	$ 23,561	$ 2.70	0.34%	$ 715,150	$ 10.23	2.06%	$	$	0.00%	$ 111,111	$ 0.71	0.16%	$	$	0.00%	$	$	0.00%	$ 758,604	$ 3.96	1.02%
13 Special Construction	$	$	0.00%	$	$	0.00%	$	$	0.00%	$ 2,382,450	$ 110.20	26.17%	$	$	0.00%	$	$	0.00%	$ 2,382,450	$ 12.44	3.22%
14 Conveying Systems	$	$	0.00%	$ 390,000	$ 5.90	1.20%	$ 146,134	$ 1.58	1.20%	$ 135,000	$ 6.56	1.99%	$	$	0.00%	$	$	0.00%	$ 419,000	$ 2.19	0.57%
21 Fire Suppression	$ 43,000	$ 5.61	1.22%	$ 836,806	$ 12.13	2.47%	$	$	0.00%	$ 139,815	$ 1.96	2.13%	$	$	0.00%	$	$	0.00%	$ 1,201,800	$ 6.28	1.63%
22 Plumbing	$ 508,860	$ 63.03	7.71%	$ 1,810,375	$ 26.26	5.37%	$	$	0.00%	$ 839,185	$ 30.98	9.22%	$	$	0.00%	$	$	0.00%	$ 2,979,550	$ 15.56	4.02%
23 HVAC	$ 727,177	$ 83.91	10.62%	$ 2,382,099	$ 35.51	7.13%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$ 4,058,721	$ 21.19	5.48%
25 Integrated Automation	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%
26 Electrical	$ 1,111,000	$ 135.47	20.13%	$ 5,670,661	$ 80.32	16.74%	$	$	0.00%	$ 1,105,000	$ 53.31	12.11%	$	$	0.00%	$ 747,471	$ 300,677.01	9.79%	$ 8,946,454	$ 46.66	12.07%
27 Communications	$	$	0.00%	$ 8,500	$ 0.12	0.02%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$ 8,500	$ 0.04	0.01%
28 Electronic Safety & Security	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%
31 Earthwork	$ 8,666	$ 1.06	0.13%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$ 1,501,847	$ 590,865.83	11.46%	$ 1,510,548	$ 7.89	2.06%
32 Exterior Improvements	$ 10,000	$ 1.25	0.15%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$ 1,067,084	$ 239,961.63	16.12%	$ 4,872,001	$ 25.96	6.71%
33 Site Utilities	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$ 543,845	$ 113,183.33	26.11%	$ 2,822,815	$ 14.74	3.81%
SUBTOTAL - COST OF WORK	$ 6,845,756	$ 789.96	100.00%	$ 34,841,134	$ 498.37	100.00%	$ 11,377,280	$ 123.34	100.00%	$ 9,104,515	$ 439.41	100.00%	$ 1,190,918	$ 119.46	100.00%	$ 10,690,260	$ 1,568,554.48	100.00%	$ 74,049,823	$ 386.61	100.00%
Subcontractor Default Insurance (SDI)	$ 82,149	$ 9.48	1.20%	$ 113,093	$ 9.98	1.30%	$ 159,227	$ 1.38	1.40%	$ 101,261	$ 4.27	1.10%	$ 11,741	$ 1.18	1.00%	$ 139,284	$ 18,922.65	1.30%	$ 888,598	$ 4.64	
General Requirements	$ 153,649	$ 17.73	2.24%	$ 221,177	$ 11.18	3.90%	$ 218,353	$ 2.00	3.50%	$ 190,408	$ 8.02	3.00%	$ 49,098	$ 4.92	4.00%	$ 181,276	$ 24,611.05	3.40%	$ 1,655,606	$ 8.64	
Estimating Contingency	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	
Construction CM Contingency	$ 485,113	$ 55.97	7.09%	$ 1,094,206	$ 15.66	3.00%	$ 357,500	$ 3.88	3.00%	$ 286,098	$ 13.01	3.00%	$	$	0.00%	$ 159,618	$ 40,298.16	3.00%	$ 2,326,838	$ 12.15	
Escalation Contingency	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	0.00%	$	$	
General Conditions	$ 627,910	$ 100.73	9.17%	$ 3,327,622	$ 63.55	9.55%	$ 1,156,776	$ 15.75	9.17%	$ 1,010,922	$ 50.03	9.15%	$ 111,295	$ 10.22	9.34%	$ 1,564,172	$ 360,048.15	9.15%	$ 9,442,177	$ 49.30	
Liability Insurance	$ 93,586	$ 10.70	1.15%	$ 374,815	$ 6.25	1.15%	$ 151,020	$ 1.67	1.15%	$ 122,200	$ 5.98	1.15%	$ 16,127	$ 1.63	1.15%	$ 144,760	$ 21,711.71	1.15%	$ 1,002,725	$ 5.24	
Mining Impact Fund	$ 71,356	$ 8.47	0.00%	$ 273,393	$ 4.51	0.00%	$ 123,963	$ 1.37	0.00%	$ 93,000	$ 4.71	0.00%	$ 12,707	$ 1.29	0.00%	$ 111,568	$ 16,811.77	0.00%	$ 793,806	$ 4.14	
Mining Impact Fee	$ 286,271	$ 33.48	3.68%	$ 1,096,162	$ 17.97	3.60%	$ 130,000	$ 1.15	3.00%	$ 328,000	$ 15.81	3.60%	$ 42,028	$ 4.31	3.60%	$ 281,422	$ 42,210.53	3.60%	$ 2,669,834	$ 13.94	
Builder's Risk Insurance	$ 50,935	$ 5.97	0.66%	$ 61,093	$ 0.93	0.15%	$ 21,125	$ 0.24	0.19%	$ 18,900	$ 0.92	0.19%	$ 2,211	$ 0.22	0.19%	$ 19,510	$ 2,311.51	0.18%	$ 175,630	$ 0.92	
PROJECT TOTALS	$ 8,835,551	$ 1,019.22 / GSF		$ 45,741,020	$ 729.88 / GSF		$ 14,277,708	$ 154.75 / GSF		$ 11,455,304	$ 551.42 / GSF		$ 1,517,564	$ 151.83 / GSF		$ 14,141,032	$ 1,964,208.35 / ACRE		$ 93,003,177	$ 485.57 / GSF	

Exhibit C - CCFTC GMP Allowances, Qualifications & Clarifications

The intent of this document is to provide a written narrative to accompany the GMP proposal dated March 20th, 2026. The Clark County Fire Training Center GMP is based on the documents listed in the attached Document Log dated 2/23/2026.

GENERAL EXCLUSIONS & QUALIFICATIONS

1. This GMP is based on Carpenter Sellers Del Gato Bid Set drawings and specifications dated 01/07/2026, addendum A dated 02/06/2026, and Addendum B dated 02/19/2026. All Costs for Plan Check Comments and any future revisions are excluded.
2. General contractor payment & performance bond is included.
3. We have excluded security guards. GMP currently includes monitored site security cameras.
4. Project is bid on a normal working schedule Monday – Friday between the hours of 6am and 5pm. Weekend and Night/overtime work are excluded. However, the contractor reserves the right to work any time, 7 days a week, without prior approval as allowed by local authorities having jurisdiction.
5. Noise mitigation for construction activities is not included in this proposal.
6. This proposal is based on the use of 2025-2026 Clark County prevailing wage labor.
7. GMP includes cost of NV Energy power usage bills throughout construction duration, power billing to be transferred to the Owner at substantial completion.
8. Dewatering has been excluded for all site excavating activities, including underground water affecting construction, uncontrolled discharge of water by others, and excessive rains.
9. Any LEED or Green Globes IAQ and accreditation testing has been excluded in this proposal.
10. Third party/QAA testing and inspection fees are not included and shall be the responsibility of the Owner. Reinspections for failed inspections are covered in GMP proposal.
11. All design consultant fees, third party fire life safety testing and energy testing have been excluded.
12. This proposal does not include any commissioning services or fees. Excludes third-party commissioning agent.
13. All material/equipment included in this proposal as an "or equal" assumption as approved by design team and Owner meaning that alternate materials/equipment may be used on this project, but they will meet and/or exceed the required specifications. All alternates or substitution requests will be submitted to Owner and Architect for approval.
14. GMP excludes all utility fees. Cost includes temporary utility usage for construction purposes only up until meter set and/or established utility service. Owner shall take over utility usage fees upon meter set/ established utility service.
15. The following permit fees are excluded:
    a. Building Permit
    b. Site Electrical Permit
    c. Building Electrical Permit

d. Building Plumbing Permit
e. Building Mechanical Permit
f. Building Signage Permit
g. Building Stairwell and Elevator Shaft
h. Wrought Iron Steel Fence
i. Engineering required for CMU/Concrete Site Walls
j. Site Underground Utilities Permit
k. Cost of Connection Fees for Utilities
l. Commercial Grading Permit
m. FAA Permit (If required)
n. Building TCO
o. Building Certificate of Occupancy
p. Health Department review fees and or permit fees for all food service.
q. Any permit required for the execution of the work or completion of the project not specifically listed above is Excluded.

16. Cost for added work requested by Clark County above and beyond what is shown on the contract documents, not reasonably inferred, is excluded.
17. Includes all cost associated with Whiting-Turner Constructability log responses dated 02/20/2026, any open questions not responded to or required additional clarification will be reviewed for cost impacts.

DIVISION 01 – GENERAL CONDITIONS & REQUIREMENTS

1. This proposal includes the rental and maintenance of a jobsite office trailer located on-site of Clark County Fire Training Center for the duration of project for project laydown and parking only. Owner trailer office is excluded; however, space can be reserved for Owner's use onsite if desired.

DIVISION 02 – EARTHWORK, UTILITIES, SITE

1. Excludes any added costs for grade modifications due to improper slope or drainage required for ADA compliant path of travel; includes grade per project documents.
2. Excludes containment, treatment, grid excavation and/or disposal of any contaminated soils encountered as none are identified within SGS North America Final Soils Report dated 01/28/2026.
3. Excludes removal of underground obstructions not identified in Geotech report dated 08/07/2023. Items excluded are consistent with debris, concrete structures, etc. encountered during excavation.
4. Excludes conflicts with unforeseen or unmarked existing utilities.
5. Adjustments of existing utilities due to conflict with new utility install is excluded.
6. WT GMP assumes over excavation of undocumented fill material onsite per Geotech report. All over excavated material is assumed to be acceptable structural fill material and reused as base material once tested.

7. Excludes augured chimney drains at tree and palm locations as these may only be required if Caliche is encountered. If required, these can be priced accordingly.
8. Soil sterilization, treatments, & insecticides are excluded.
9. Warranty requirements for Plants and Landscaping noted within Specification 32 93 00 section 1.8 are included in base pricing.

DIVISION 03 – CONCRETE

1. Excludes 1/8" in 10ft floor flatness requirement for elevated decks per Specification 03 30 00 Section 3.8. WT will meet Concrete Industry Standards of ¼" in 10ft floor flatness at elevated SOMD.
2. Excludes any deck shoring for Composite deck. Assumes metal deck will support pour activity unless otherwise noted on the project drawings.
3. Excludes fluid applied waterproofing.
4. GMP includes termite spraying at Fire Station 88 only.
5. Excludes repair of cracking, curling, deflection or other naturally occurring effects borne by concrete construction.

DIVISION 04 - MASONRY

1. Cost and schedule based on the ability to top out CMU without bracing and/or tying in building structure.
2. Includes cost for standard mortar color for all masonry (CMU) block units.
3. Excludes CMU Expansion joints, none shown.
4. Excludes integral water repellants in CMU block and mortar.

DIVISION 05 – METALS & STRUCTURAL STEEL

1. AESS (Architecturally Exposed Structural Steel) tolerances and requirements are excluded.
2. Includes HSS tube steel to support roof parapet walls at the Training Center, none shown in contract documents.
3. All interior stair rails are included as painted steel rail as finish is not identified.
4. Excludes aluminum ships ladder per detail 13 & 5 on A4.12. Includes cost for Steel Ships ladders in lieu of aluminum.
5. Excludes painting of exposed steel unless otherwise noted within the contract documents.
6. Excludes high performance primers and coatings of interior steel.
7. Includes structural supports for MTL-06, MTL-05, & MTL-01 at the Training Center as none are shown in contract documents. Exlcudes supplemental steel for the rest of MTL (Metal Panel) system. Assumes structure has been designed to withstand all decorative skin load impact.

DIVISION 06 – WOODS, AND PLASTICS

1. Excludes LEED, AWI, FSC, QCP & fire retardant treated wood & lumber.
2. Any structural plastics, plastic fabrications, and structural composites have been excluded.

3. Includes matte black hardware at millwork as identified per Q/A1.30, excludes bronze hardware per specifications at all millwork per specification 06 41 16.

DIVISION 07 - THERMAL & MOISTURE PROTECTION

1. Coping shall be prefinished metal in standard color.
2. A roof manufacturer's 20-year NDL material and labor warranty is included.
3. Excludes traffic coating at exposed vertical foundation walls.
4. Pricing excludes all Spray Applied Fireproofing and Intumescent Fireproofing on Structural Steel on all buildings. Based on the FPR, Structural Steel Fireproofing is not required for this project.
5. Price based on standard colors for all exterior metal finishes including flashing.
6. Pricing assumes batt insulation in lieu of mineral wool where aloud by code. Includes mineral wool as identified at the Fire Station only.
7. Pricing excludes roof davits on all buildings.
8. EIFS ceiling on Level 2 at the Training Center Parking Garage, included as sand pebble fine texture and does not include the air-weather barrier as manufacturer rep stated not required for deck underside horizontal application.

DIVISION 08 - OPENINGS

1. Individual keying of all unit doors will be by property management. Whiting-Turner will provide a general construction key, and common area doors will have their own keys that Whiting-Turner will turn over to Ownership at project completion.
2. Pricing includes card reader hardware as identified within the Contract Documents; all other access control hardware, pathway, cabling and/or programming is excluded.
3. Smoke curtains have been excluded at the elevator doors located in the Training Center. None-identified within FPR.
4. Included Fire Station #88 Four-Fold Apparatus Bay Doors Model FF300 per specifications.
5. Pricing includes (12) AMARR Model #2742 Steel Insulated Sectional Doors per the Maintenance Building Plans. No Specifications provided.
6. Excludes glass guardrail shown on note 530 on A5.10 at the Training Center. Guardrail included as MTL-06 per Architectural elevations.
7. Excludes all heat soaking of glass.

DIVISION 9 - FINISHES

1. Assumes ACT ceiling can be pinned and or attached to deck/ composite slab in lieu of spanning structural beams.
2. Proposal includes a $10/SF cost to furnish the WC-01 Digital Custom Vinyl Wallcovering @ the Training Center. Install included in base GMP proposal.

3. This proposal excludes any high-performance coatings, intumescent coatings, custom plaster, and murals of any kind.
4. GMP includes GSS graffiti coating per Clark County request in lieu of products per spec 09 96 23.
5. Full height wall conditions with adjacent ceilings shall only be finished and painted to 6" above ceiling elevations. Partial height walls shall be contemplated where no fire rated assemblies or sound rated walls are required.
6. Proposal excludes any restocking fees due to a material change after product has been ordered.
7. Waxing and/or polishing of Vinyl flooring is not included in this proposal.
8. Cost based on 2CM Solid Surface per Contract Documents

DIVISION 10 – SPECIALTIES

1. Pricing includes cost for exterior and interior building signage/way finding signage per Contract Documents.
2. Any safety specialties such as defibrillator cabinets and first aid cabinets have been excluded. None identified in plans.
3. Excludes time clocks in the Maintenance Building.
4. Excludes all digital media players, computers, content, data cabling and connections unless specifically included above.
5. Excludes name plates and padlocks at all lockers.
6. Pricing excludes any MEP infrastructure to the Burn Tower. Pricing includes raceways and pull string only for power distribution to the Burn Tower from the SH1 Site Service Switchboard.
7. Excludes furnish and install of all Fire Blast props and infrastructure.
8. Burn Tower scope included as electrical raceway and pull string, concrete foundation and slab on grade and burn tower install by WHP only.

Division 11 – EQUIPMENT

1. Includes Maintenance Building Equipment as identified in Contract Documents and coordinated with the Fire Department & Automotive Equipment of Nevada. Includes the following:
    a. Service Pit
        i. 25,000lb Rolling Jack
        ii. Rolling Oil Drain
        iii. 48" Wide Pit Covers
    b. Waste Product Pumps
        i. Waste Oil Pump
        ii. Waste Coolant Pump
        iii. Filter/Regulator/Lubricator
        iv. Shut Off Kit
    c. Reel Banks

i. 3/8" Air Hose Reel
ii. ½" Air Hose Reel
iii. Transmission Fluid Reel
iv. Gear Oil Reel
v. Coolant Reel
vi. Low/Medium Pressure Hose Inlet Kit
vii. High Pressure Inlet Kit
viii. 4 Reel Mounting Channel (2 per Bank)
ix. LP/MP Fluid Shut Off
x. Grease Shut Off Valve for Reels
xi. Grease Dispense Valve
xii. ATF/Oil Meters – Preset, 8gpm, rigid tip
xiii. Gear Lube Meter – Preset, 8gpm, rigid tip
xiv. Coolant Meter – Preset, 8gpm, rigid tip

d. Wall Mounted Air Reels
   i. 1" NPT Regulator
   ii. 1" NPT Filter
   iii. Gauge for regulator
   iv. 1" Quick Connect + ½" Quick Connect
   v. 3/8" Air Hose Reels
   vi. 1 Reel Mounting Channel
   vii. Low/Medium Pressure Hose Inlet Kit
   viii. LP/MP Fluid Shut Off Valves for Reels
e. Compressed Air Equipment
   i. HQR15F-12 15hp Revolution quite enclosed compressor
   ii. Alternator Panel
   iii. 200 SCFM flow control left to right
   iv. CH7 oil water separator – 50 CFM
   v. CHWS-250 oil water separator – 250 CFM
f. Storage Tanks
   i. 280 Gallon UL-142 Steel Tank (w/ fresh tank trim kit)
   ii. 280 Gallon UL-142 Steel Tank (w/ waste tank trim kit)
   iii. 1000 Gallon UL-142 Steel Tank (w/ waste tank trim kit)
   iv. Waste product overflow shut off
   v. Waste product tank full alarm
g. Fresh Product Pumps
   i. 5:1 Oil Pump Kit
   ii. Thermal Relief Valve Kit

iii. LP/MP Fluid Shut Off Valve
iv. Downtube
v. Filter/Regulator/Lubricator
vi. Premixed Coolant Pump Kit
vii. Grease Pump Kit w/ Topper Inductor
viii. Adjustable Grease Air Regulator
ix. Tamper Resistant Air Regulator

h. Waste Oil/Coolant Drains
   i. Big Hauler Truck Drain (for bays without service pit)
   ii. Receiver Evacuation Kit

Division 12 – FURNISHINGS

1. FF&E listed as landscape amenities on the landscape plans have been included. All other interior and exterior FF&E items are excluded.
2. Excludes Furnish and Install of all gym equipment within the Training Center and the Fire Station.
3. Furnish of any wall art has been excluded. Install only is included for the graduating class plaques as shown per contract documents. Plaques to the delivered FOB by the Owner.
4. Window treatments have been priced as manual operation.
5. Pricing includes Irwin Telescopic Bleachers, VersaTract with VersaDeck Seating Requirements in the Training Center Auditorium in lieu of the basis of design Jezet "PLAZA" chair per specification 12 66 23.

DIVISION 14 – CONVEYING EQUIPMENT

1. Schindler elevator is the carried elevator subcontractor as it is listed as basis of design within project specifications. Cost includes the Schindler 5000 model in lieu of the Schindler 3300XL MRL specified within the Contract Documents. Schindler 3300XL model has been discontinued.
2. Excludes custom elevator cab build-out; cost assumes standard (non-premium) finishes per A7.30 & A7.31.
3. Elevator has been priced as machine room-less with machine at top of hoist way and the controller at the top of the hoist ways.

DIVISION 21 – FIRE PROTECTION

1. Includes furnish and install of (1) 1,000-gpm electric fire pump system.
2. Includes semi-recessed sprinkler heads in front of house spaces. Includes six (6) custom colors for front-of-house spaces.
3. Excludes fireproofing, labeling, and insulating of fire sprinkler piping.
4. Excludes Fire Alarm or Fire Sprinkler Monitoring System.
5. Excludes overtime plan review and/or inspection fees through the AHJ.
6. Excludes concrete work or pads required for fire pumps.

7. Includes furnish and install of standpipe and fire pump. Includes pipe to be Schedule 10 for all grooved pipe and Schedule 30 for all threaded piping.
8. Includes design and install of Sprinkler Riser per local AHJ and NFPA 13.
9. Includes furnish and install of FDC Knox Caps, FDC Knox plugs, and Standpipe Knox Caps.
10. Includes Dry Sprinkler system at exterior balconies ceilings and exterior canopies.

DIVISION 22 –PLUMBING

1. Includes the use of ProPress fittings for domestic water plumbing and mechanical hydronic systems.
2. Off-site Southwest Gas Scope is excluded in base pricing.

DIVISION 23 – MECHANICAL

1. Cost excludes screening of mechanical units; assumes units were placed as such to meet any AHJ requirements for line of site and or visibility requirements.
2. Duct leakage testing is excluded.
3. Door Blower test is excluded.
4. MQAA testing is excluded and assumed owner will be hiring MQAA Special Inspection Agency if required.
5. Any seismic engineering, or certification of the MEP system has been excluded. Includes bracing where shown on plans.
6. Includes Sunbelt Controls Automatic Logic Systems for the Building Automation System.
7. Excludes the scope of work to remove/salvage the existing RTUs. Removal by Owner.

DIVISION 26 – ELECTRICAL

1. Excludes any cost and or delay associated with Nevada Energy review comments regarding permanent power process.
2. Furnish and install of all Router and switches for all buildings, programming, and integrations is by owner.
3. Excludes furnish and install of a UPS system.
4. Excludes furnish and install of submeters.
5. Fire alarm system design/build is based on electrical subcontractor's interpretation of the code based on similar local projects. Any changes to the code or interpretations by the Fire Marshall/Inspector, or the Life Safety consultant are not being accounted for. Pricing for this is subject to revision upon receipt of the approved Fire Protection Report.
6. WT includes the electrical scope to be installed per the following codes: 2018 IBC, 2017 NEC, 2018 IECC, 2010 ADA Standards, and 2018 International Fire Code.
7. Scope is based on electrical plans provided, subject to change pending NVE drawings.
8. WT assumes available power capacity as indicated; modifications to the existing services beyond what is shown are excluded.

9. Base pricing excludes EV parking infrastructure or "Future Use" Raceways for potential EV parking spots within the parking garage. Includes EV parking infrastructure on the site only.
10. Base pricing excludes parking availability indication system or Parking Guidance Systems within the parking garage.

Division 27 – Low Voltage

1. WT assumes security VLAN will be set in place by the customer to communicate between this site and the main site for management purposes prior to configuration.
2. Internet connection and/or IT network connection to customer IT network is not included, to be provided by Clark County.
3. WT excludes unless otherwise noted; software licenses, subscriptions, renewals, and ongoing service agreements.
4. WT excludes integration with owner furnished, third party systems unless explicitly shown within the contract documents.
5. Low voltage connections to owner-furnished FF&E, AV equipment or other specialty devices are excluded.
6. Excludes furnish of WAP devices, to be provided by Owner IT department. Installation included in base GMP.
7. Excludes routers, switches and programing of network. To be performed by Owner IT department.

Division 28 – Fire Alarm

1. Temporary fire alarm systems or interim life safety systems are excluded by WT.
2. WT excludes modifications or device relocation requested after initial acceptance as per contract documents.
3. WT excludes training beyond initial turnover, on-call services, and post-occupancy testing.

DIVISION 31 – Earthwork (Earthwork & Striping)

1. Over-excavations will be limited to depths recommended by the geotechnical report. Additional over-excavation will be excluded by WT.
2. Erosion control and dust control are included for normal construction duration only; WT excludes extended durations.
3. WT includes permanent striping and signage. WT excludes temporary striping, phased striping, or re-striping due to sequencing changes.

DIVISION 32 – Site Improvements (Site Concrete, Landscape, & Fencing)

1. WT excludes off-site or right of way work not explicitly shown or noted in contract documents. WT includes on-site exterior improvements within the property boundary as shown within the contract documents.

DIVISION 33 – Utilities (Dry & Wet)

1. WT excludes repair or replacement of unlocated existing utilities.
2. WT shall not be responsible for the relocation, adjustment or removal of existing utilities and unknown structures not shown in the drawings.
3. WT will not provide fiber optic cable or interconnect cable.
4. Earthwork quantities are based on the Geotechnical reports and drawings issued.
5. WT excludes allowance for unsuitable soils beyond those identified in the Geotechnical report.
6. WT excludes the removal of Biocide Tank. Assumes owner to coordinate with CCWRD for Biocide Tank removal prior to start of construction.

Exhibit C: Contract Allowances

1) **Caliche/Hard Dig Allowance ($250,000)**
    a. This proposal includes $250,000 Caliche/Hard Dig allowance.

2) **Future Expansion Room 347 Buildout Allowance ($250,000)**
    a. This proposal includes $250,000 Room 347 TI buildout allowance called out as "Future Office Expansion", roughly 2,000 square feet.

Exhibit C - Whiting-Turner Salaried and Billable Rates

1. Whiting-Turner shall furnish yearly labor rates. Labor rates shall be applied by year and level of employees working on the project. If an employee receives a promotion, their class may change on January 1 of the year following the promotion. Whiting-Turner shall notify Owner of any promotions at the end of the year and approval by Owner shall not be unreasonably withheld.

Payroll Charge Rates as of January 1, 2026

Title	Southwest w. Burden	EHS W. Burden	VDC W. Burden	Mech/Elec W. Burden	Cost/Sched W. Burden
Intern *	$ 32.82	$ 32.82	$ -	$ 32.82	$ 32.82
Assistant/ Receptionist/ Administrative Assistant	$ 48.51	$ -	$ -	$ -	$ -
Project Accountant	$ 72.96	$ -	$ -	$ -	$ -
Asst. Field Engineer/Asst. Project Engineer	$ 75.15	$ -	$ -	$ -	$ -
Field Engineer/Project Engineer/Asst. Supt 1	$ 100.56	$ -	$ -	$ 103.47	$ -
Sr. Field Engineer/Asst. Project Manager/Asst. Supt 2	$ 109.17	$ 89.23	$ -	$ 120.07	$ 112.39
Project Manager 1/Superintendent 1	$ 120.73	$ 99.67	$ -	$ 151.66	$ 130.09
Project Manager 2/Superintendent 2	$ 134.42	$ 104.21	$ -	$ 174.57	$ 153.55
Project Manager 3/Superintendent 3	$ 145.72	$ 118.28	$ -	$ 177.94	$ 158.85
Project Manager 4/Superintendent 4	$ 167.16	$ 136.43	$ -	$ 202.39	$ 165.68
Project Manager 5/Superintendent 5	$ 188.57	$ 144.05	$ -	$ 249.55	$ 199.33
Senior Project Manager/ Senior Superintendent	$ 226.66	$ 204.29	$ -	$ 276.55	$ 231.97
Regional Superintendent	$ 349.58	$ -	$ -	$ 349.26	$ -
Vice President/ Vice President of Projects	$ 285.16	$ -	$ -	$ 309.75	$ 268.88
Regional Superintendent	$ 388.63	$ -	$ -	$ -	$ -

Payroll Charge Rates as of January 1, 2027

Title	Southwest w. Burden	EHS W. Burden	VDC W. Burden	Mech/Elec W. Burden	Cost/Sched W. Burden
Intern *	$ 34.46	$ 34.46	$ -	$ 34.46	$ 34.46
Assistant/ Receptionist/ Administrative Assistant	$ 50.94	$ -	$ -	$ -	$ -
Project Accountant	$ 76.48	$ -	$ -	$ -	$ -
Asst. Field Engineer/Asst. Project Engineer	$ 78.78	$ -	$ -	$ -	$ -
Field Engineer/Project Engineer/Asst. Supt 1	$ 105.46	$ -	$ -	$ 108.64	$ -
Sr. Field Engineer/Asst. Project Manager/Asst. Supt 2	$ 114.51	$ 93.69	$ -	$ 126.07	$ 118.01
Project Manager 1/Superintendent 1	$ 126.53	$ 104.66	$ -	$ 159.25	$ 136.59
Project Manager 2/Superintendent 2	$ 140.85	$ 109.42	$ -	$ 183.30	$ 161.23
Project Manager 3/Superintendent 3	$ 152.67	$ 124.19	$ -	$ 186.84	$ 166.79
Project Manager 4/Superintendent 4	$ 175.15	$ 143.25	$ -	$ 212.50	$ 173.96
Project Manager 5/Superintendent 5	$ 197.62	$ 151.26	$ -	$ 262.03	$ 209.30
Senior Project Manager/ Senior Superintendent	$ 237.59	$ 214.51	$ -	$ 290.38	$ 243.57
Regional Superintendent	$ 366.66	$ -	$ -	$ 366.72	$ -
Vice President/ Vice President of Projects	$ 299.02	$ -	$ -	$ 325.24	$ 282.32
Regional Superintendent	$ 407.66	$ -	$ -	$ -	$ -

Payroll Charge Rates as of January 1, 2028

Title	Southwest w. Burden	EHS W. Burden	VDC W. Burden	Mech/Elec W. Burden	Cost/Sched W. Burden
Intern *	$ 36.19	$ 36.19	$ -	$ 36.19	$ 36.19
Assistant/ Receptionist/ Administrative Assistant	$ 53.49	$ -	$ -	$ -	$ -
Project Accountant	$ 80.18	$ -	$ -	$ -	$ -
Asst. Field Engineer/Asst. Project Engineer	$ 82.60	$ -	$ -	$ -	$ -
Field Engineer/Project Engineer/Asst. Supt 1	$ 110.61	$ -	$ -	$ 114.08	$ -
Sr. Field Engineer/Asst. Project Manager/Asst. Supt 2	$ 120.11	$ 98.38	$ -	$ 132.38	$ 123.91
Project Manager 1/Superintendent 1	$ 132.63	$ 109.89	$ -	$ 167.21	$ 143.42
Project Manager 2/Superintendent 2	$ 147.61	$ 114.89	$ -	$ 192.46	$ 169.29
Project Manager 3/Superintendent 3	$ 159.96	$ 130.40	$ -	$ 196.18	$ 175.13
Project Manager 4/Superintendent 4	$ 183.53	$ 150.41	$ -	$ 223.13	$ 182.66
Project Manager 5/Superintendent 5	$ 207.13	$ 158.82	$ -	$ 275.13	$ 219.76
Senior Project Manager/ Senior Superintendent	$ 249.07	$ 225.23	$ -	$ 304.90	$ 255.75
Regional Superintendent	$ 384.59	$ -	$ -	$ 385.06	$ -
Vice President/ Vice President of Projects	$ 313.57	$ -	$ -	$ 341.50	$ 296.44
Regional Superintendent	$ 427.65	$ -	$ -	$ -	$ -

EXHIBIT C-1
NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE
EXHIBIT "C-1" OWNER CONTINGENCY

Left intentionally blank

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
FIRE TRAINING CENTER									
DRAWINGS									
		General							
G0.00	09.15.2025 60% CDs	COVER SHEET							
G0.02	09.15.2025 60% CDs	SHEET INDEX	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
G0.03	09.15.2025 60% CDs	GENERAL INFORMATION/CODE ANALYSIS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
G0.04	09.15.2025 60% CDs	TYPICAL ACCESSIBILITY DETAILS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
G1.01	09.15.2025 60% CDs	LIFE SAFETY PLAN - LEVEL ONE	9/15/2025	12/15/2025	1/7/2026				
G1.02	09.15.2025 60% CDs	LIFE SAFETY PLAN - LEVEL TWO	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
G1.03	09.15.2025 60% CDs	LIFE SAFETY PLAN - LEVEL THREE	9/15/2025	12/15/2025	1/7/2026				
G1.04	09.15.2025 60% CDs	LIFE SAFETY PLAN - LEVEL FOUR	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
G1.30	01.07.2026 Build PS	TRAINING CENTER - IECC ENVELOPE COMPLIANCE	9/15/2025	12/15/2025	1/7/2026				
		Civil Drawings			1/7/2026				
C1.01	09.15.2025 60% CDs	COVER SHEET							
C1.02	09.15.2025 60% CDs	GENERAL NOTES SHEET	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C1.03	09.15.2025 60% CDs	PROJECT DATA	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.01	09.15.2025 60% CDs	DEMOLITION PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.02	09.15.2025 60% CDs	DEMOLITION PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C2.03	09.15.2025 60% CDs	DEMOLITION PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.04	09.15.2025 60% CDs	DEMOLITION PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.05	09.15.2025 60% CDs	DEMOLITION PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C3.01	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.02	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.03	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.04	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.05	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C4.01	09.15.2025 60% CDs	TRAFFIC SIGNAL PLAN AT TROPICANA AND ARVILLE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C4.02	09.15.2025 60% CDs	TRAFFIC SIGNAL SCHEDULE AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C4.03	09.15.2025 60% CDs	EMERGENCY SIGNAL PLAN SCHEDULE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C4.04	09.15.2025 60% CDs	GENERAL TRAFFIC NOTES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C5.01	09.15.2025 60% CDs	MASTER GRADING PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C5.02	09.15.2025 60% CDs	GRADING PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C5.03	09.15.2025 60% CDs	GRADING PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.04	09.15.2025 60% CDs	GRADING PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.05	09.15.2025 60% CDs	GRADING PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.06	09.15.2025 60% CDs	GRADING PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.01	09.15.2025 60% CDs	TROPICANA AVE & PROFILE	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.02	12.15.2025 95% CDs	TROPICANA AVE - UTILITY PLAN AND PROFILE		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.03	12.15.2025 95% CDs	ARVILLE ST - UTILITY PLAN AND PROFILE 1		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.04	12.15.2025 95% CDs	ARVILLE ST - UTILITY PLAN AND PROFILE 2		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.05	12.15.2025 95% CDs	ARVILLE ST - UTILITY PLAN AND PROFILE 3		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.06	01.07.2026 Build PS	SEWER LATERAL PLAN AND PROFILES		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.01	09.15.2025 60% CDs	MASTER UTILITY SHEET			1/7/2026	2/6/2026	2/19/2026		
C7.02	09.15.2025 60% CDs	UTILITY PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.03	09.15.2025 60% CDs	UTILITY PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.04	09.15.2025 60% CDs	UTILITY PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.05	09.15.2025 60% CDs	UTILITY PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.06	09.15.2025 60% CDs	UTILITY PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C8.01	09.15.2025 60% CDs	GENERAL STRUCTURAL NOTES & TYPICAL DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C8.02	09.15.2025 60% CDs	JUCTION STRUCTURES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C8.03	09.15.2025 60% CDs	RETAINING WALL	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C9.01	09.15.2025 60% CDs	DETAIL SHEET 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C9.02	09.15.2025 60% CDs	DETAIL SHEET 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C9.03	09.15.2025 60% CDs	DETAIL SHEET 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C9.04	12.15.2025 95% CDs	DETAIL SHEET 4		12/15/2025	1/7/2026				
		Landscape Drawings							
L1.01	09.15.2025 60% CDs	OVERALL LANDSCAPE PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L1.02	09.15.2025 60% CDs	LANDSCAPE PLAN ENLARGEMENT "A"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L1.03	09.15.2025 60% CDs	LANDSCAPE PLAN ENLARGEMENT "B"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L1.04	12.15.2025 95% CDs	LEVEL 3 PLAZA PLANTING PLAN		12/15/2025	1/7/2026				
L2.01	09.15.2025 60% CDs	OVERALL IRRIGATION PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L2.02	09.15.2025 60% CDs	IRRIGATION PLAN ENLARGEMENT "A"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L2.03	09.15.2025 60% CDs	IRRIGATION PLAN ENLARGEMENT "B"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L3.01	09.15.2025 60% CDs	PROJECT DETAILS	9/15/2025	12/15/2025	1/7/2026				
L3.02	12.15.2025 95% CDs	PROJECT DETAILS		12/15/2025	1/7/2026				
		Architectural Site Drawings							
AS1.01	09.15.2025 60% CDs	OVERALL ARCHITECTURAL SITE PLAN	9/15/2025	12/15/2025	1/7/2026				

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company
02/24/26

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
AS1.10	09.15.2025 60% CDs	ENLARGED ARCHITECTURAL SITE PLAN - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.11	09.15.2025 60% CDs	ENLARGED ARCHITECTURAL SITE PLAN - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.12	09.15.2025 60% CDs	ENLARGED ARCHITECTURAL SITE PLAN - AREA C	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.20	09.15.2025 60% CDs	ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.21	09.15.2025 60% CDs	ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS3.00	09.15.2025 60% CDs	SITE GATE SCHEDULE AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS3.10	09.15.2025 60% CDs	ARCHITECTURAL SITE DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
		Architectural Drawings							
A0.10	09.15.2025 60% CDs	PARTITION TYPES	9/15/2025	12/15/2025	1/7/2026				
A0.20	09.15.2025 60% CDs	PARTITION TYPES	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.01	09.15.2025 60% CDs	OVERALL FLOOR PLAN - LEVEL ONE	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.01A	09.15.2025 60% CDs	FLOOR PLAN - LEVEL ONE - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.01B	09.15.2025 60% CDs	FLOOR PLAN - LEVEL ONE - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.01.1	09.15.2025 60% CDs	OVERALL DIMENSIONAL PLAN - LEVEL ONE	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.01.1A	09.15.2025 60% CDs	DIMENSIONAL PLAN - LEVEL ONE - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.01.1B	09.15.2025 60% CDs	DIMENSIONAL PLAN - LEVEL ONE - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.02	09.15.2025 60% CDs	OVERALL FLOOR PLAN - LEVEL TWO	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.02A	09.15.2025 60% CDs	FLOOR PLAN - LEVEL TWO - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.02B	09.15.2025 60% CDs	FLOOR PLAN - LEVEL TWO - AREA B	9/15/2025	12/15/2025	1/7/2026				
A1.02.1	09.15.2025 60% CDs	OVERALL DIMENSIONAL PLAN - LEVEL TWO	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.02.1A	09.15.2025 60% CDs	DIMENSIONAL PLAN - LEVEL TWO - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.02.1B	09.15.2025 60% CDs	DIMENSIONAL PLAN - LEVEL TWO - AREA B	9/15/2025	12/15/2025	1/7/2026				
A1.03	09.15.2025 60% CDs	OVERALL FLOOR PLAN - LEVEL THREE	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.03A	09.15.2025 60% CDs	FLOOR PLAN - LEVEL THREE - AREA A	9/15/2025	12/15/2025	1/7/2026				
A1.03B	09.15.2025 60% CDs	FLOOR PLAN - LEVEL THREE - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A1.03.1	09.15.2025 60% CDs	OVERALL DIMENSIONAL PLAN - LEVEL THREE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A1.03.1A	09.15.2025 60% CDs	DIMENSIONAL PLAN - LEVEL THREE - AREA A	9/15/2025	12/15/2025	1/7/2026				
A1.03.1B	09.15.2025 60% CDs	DIMENSIONAL PLAN - LEVEL THREE - AREA B	9/15/2025	12/15/2025	1/7/2026				
A1.04	09.15.2025 60% CDs	OVERALL FLOOR PLAN - LEVEL FOUR	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A1.04A	09.15.2025 60% CDs	FLOOR PLAN - LEVEL FOUR - AREA A	9/15/2025	12/15/2025	1/7/2026				
A1.04B	09.15.2025 60% CDs	FLOOR PLAN - LEVEL FOUR - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.04.1	09.15.2025 60% CDs	OVERALL DIMENSIONAL PLAN - LEVEL FOUR	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.04.1A	09.15.2025 60% CDs	DIMENSIONAL PLAN - LEVEL FOUR - AREA A	9/15/2025	12/15/2025	1/7/2026				
A1.04.1B	09.15.2025 60% CDs	DIMENSIONAL PLAN - LEVEL FOUR - AREA B	9/15/2025	12/15/2025	1/7/2026				
A1.02.00	12.15.2025 95% CDs	SLAB PLAN - LEVEL ONE		12/15/2025	1/7/2026				
A1.02.01	12.15.2025 95% CDs	SLAB PLAN - LEVEL TWO		12/15/2025	1/7/2026				
A1.02.2A	12.15.2025 95% CDs	SLAB PLAN - LEVEL THREE - AREA A		12/15/2025	1/7/2026				
A1.02.2B	02.06.2026 Add A #5	SLAB PLAN - LEVEL THREE - AREA B		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.02.3B	12.15.2025 95% CDs	SLAB PLAN - LEVEL THREE - AREA B				2/6/2026	2/19/2026		
A1.02.4A	12.15.2025 95% CDs	SLAB PLAN - LEVEL FOUR - AREA A		12/15/2025	1/7/2026				
A1.02.4B	12.15.2025 95% CDs	SLAB PLAN - LEVEL FOUR - AREA B		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.11	09.15.2025 60% CDs	SIGNAGE SCHEDULE		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.12	09.15.2025 60% CDs	SIGNAGE PLAN - LEVEL ONE	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.13	09.15.2025 60% CDs	SIGNAGE PLAN - LEVEL TWO	9/15/2025	12/15/2025	1/7/2026				
A1.14	09.15.2025 60% CDs	SIGNAGE PLAN - LEVEL THREE	9/15/2025	12/15/2025	1/7/2026				
A1.15	09.15.2025 60% CDs	SIGNAGE PLAN - LEVEL FOUR	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.21	09.15.2025 60% CDs	OVERALL FF&E PLAN - LEVEL ONE	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.22	09.15.2025 60% CDs	OVERALL FF&E PLAN - LEVEL TWO	9/15/2025	12/15/2025	1/7/2026				
A1.23	09.15.2025 60% CDs	OVERALL FF&E PLAN - LEVEL THREE	9/15/2025	12/15/2025	1/7/2026				
A1.23A	09.15.2025 60% CDs	FF&E PLAN FLOOR THREE - AREA A	9/15/2025	12/15/2025	1/7/2026				
A1.23B	09.15.2025 60% CDs	FF&E PLAN FLOOR THREE - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.24	09.15.2025 60% CDs	OVERALL FF&E PLAN - LEVEL FOUR	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.24A	09.15.2025 60% CDs	FF&E PLAN LEVEL FOUR - AREA A	9/15/2025	12/15/2025	1/7/2026				
A1.24B	09.15.2025 60% CDs	FF&E PLAN FLOOR FOUR - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A1.30	09.15.2025 60% CDs	FINISH INDEX - TRAINING BUILDING	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.41	09.15.2025 60% CDs	OVERALL FINISH PLAN - LEVEL ONE	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A1.42	09.15.2025 60% CDs	OVERALL FINISH PLAN - LEVEL TWO	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.43	09.15.2025 60% CDs	OVERALL FINISH PLAN - LEVEL THREE	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.43A	09.15.2025 60% CDs	FINISH PLAN - LEVEL THREE - AREA A	9/15/2025	12/15/2025	1/7/2026				
A1.43B	09.15.2025 60% CDs	FINISH PLAN - LEVEL THREE - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.44	09.15.2025 60% CDs	OVERALL FINISH PLAN - LEVEL FOUR	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.44A	09.15.2025 60% CDs	FINISH PLAN - LEVEL FOUR - AREA A	9/15/2025	12/15/2025	1/7/2026				
A1.44B	09.15.2025 60% CDs	FINISH PLAN - LEVEL FOUR - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A2.01	09.15.2025 60% CDs	TRAINING CENTER - ENLARGED PLANS & ELEVATIONS - MEN RECRUIT SHOWER/LOCKERS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A2.02	09.15.2025 60% CDs	TRAINING CENTER - ENLARGED PLANS & ELEVATIONS - WOMEN CADRE SHOWER/LOCKERS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.03	09.15.2025 60% CDs	TRAINING CENTER - ENLARGED PLANS - MEN CADRE SHOWER/LOCKERS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A2.04	09.15.2025 60% CDs	TRAINING CENTER - ELEVATIONS - MEN CADRE SHOWER/LOCKERS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A2.05	09.15.2025 60% CDs	TRAINING CENTER - ENLARGED PLANS & ELEVATIONS - WOMEN RECRUIT SHOWER/LOCKERS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		

RFP 607319-24
EXHIBIT D - TECHNICAL SPECIFICATIONS AND DRAWINGS

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company
2/19/2026

Item #	Design Issue	Title	09.15.2025 60% Construction Drawings	12.15.2025 95% Construction Drawings	01.07.2026 Building Permit Set	02.06.2026 Addendum A Bid Set	02.20.2026 Addendum B Issuance	Current Date	Notes
A2.06	09.15.2025 60% CDs	TRAINING CENTER - ENLARGED PLANS & ELEVATIONS - THIRD LEVEL RESTROOMS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A2.07	09.15.2025 60% CDs	TRAINING CENTER - ELEVATIONS - THIRD LEVEL RESTROOMS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.08	09.15.2025 60% CDs	TRAINING CENTER - ENLARGED PLANS & ELEVATIONS - FOURTH LEVEL RESTROOMS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.09	12.15.2025 95% CDs	TRAINING CENTER - ENLARGED PLANS & RENDERINGS - LOBBY, HALLWAY AND PRE FUNCTION AREA		12/15/2025	1/7/2026				
A2.10	12.15.2025 95% CDs	TRAINING CENTER - ELEVATIONS - LOBBY, HALLWAY AND PRE FUNCTION AREA		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.11	12.15.2025 95% CDs	TRAINING CENTER - ENLARGED PLANS & RENDERINGS - CLASS PLAQUE CORRIDOR & WORKOUT ROOM		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.12	12.15.2025 95% CDs	TRAINING CENTER - ELEVATIONS - CLASS PLAQUE CORRIDOR & WORKOUT ROOM RENDERINGS		12/15/2025	1/7/2026	2/6/2026			
A2.13	09.15.2025 60% CDs	TRAINING CENTER - ENLARGED PLANS - AUDITORIUM	9/15/2025	12/15/2025	1/7/2026				
A2.14	09.15.2025 60% CDs	TRAINING CENTER - ELEVATIONS - AUDITORIUM	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A2.15	12.15.2025 95% CDs	TRAINING CENTER - ENLARGED PLANS & ELEVATIONS - KITCHEN AND COPY/COFFEE ROOM		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.16	12.15.2025 95% CDs	TRAINING CENTER - ENLARGED PLANS, ELEVATIONS, & RENDERINGS - EMS CLASSROOM		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.17	12.15.2025 95% CDs	TRAINING CENTER - ENLARGED PLAN, ELEVATIONS, & RENDERINGS - EMS LARGE BREAK OUT AND NARCOTICS ROOM		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.18	12.15.2025 95% CDs	TRAINING CENTER - ENLARGED PLAN, ELEVATIONS, & RENDERINGS - WEST CLASSROOMS		12/15/2025	1/7/2026	2/6/2026			
A2.19	12.15.2025 95% CDs	TRAINING CENTER - ENLARGED PLAN, ELEVATIONS, & RENDERINGS - EAST CLASSROOMS		12/15/2025	1/7/2026	2/6/2026			
A2.20	12.15.2025 95% CDs	TRAINING CENTER - ENLARGED PLANS, ELEVATIONS, & RENDERINGS - TYPICAL BREAK OUT AND CONFERENCE ROOMS		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.21	09.15.2025 60% CDs	TRAINING CENTER - ENLARGED PLANS & ELEVATIONS - FOURTH LEVEL CASEWORK	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A2.22	09.15.2025 60% CDs	TRAINING CENTER - ELEVATIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A3.01	09.15.2025 60% CDs	OVERALL REFLECTED CEILING PLAN - LEVEL ONE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A3.01	01.07.2026 Build PS	REFLECTED CEILING PLAN - LEVEL ONE			1/7/2026	2/6/2026	2/19/2026		
A3.01A	09.15.2025 60% CDs	REFLECTED CEILING PLAN - LEVEL ONE - AREA A	9/15/2025	12/15/2025					
A3.01B	09.15.2025 60% CDs	REFLECTED CEILING PLAN - LEVEL ONE - AREA B	9/15/2025	12/15/2025					
A3.02	09.15.2025 60% CDs	OVERALL REFLECTED CEILING PLAN - LEVEL TWO	9/15/2025	12/15/2025	1/7/2026				
A3.02	02.06.2026 Add A BS	REFLECTED CEILING PLAN - LEVEL TWO				2/6/2026	2/19/2026		
A3.02A	09.15.2025 60% CDs	REFLECTED CEILING PLAN - LEVEL TWO - AREA A	9/15/2025	12/15/2025					
A3.02B	09.15.2025 60% CDs	REFLECTED CEILING PLAN - LEVEL TWO - AREA B	9/15/2025	12/15/2025					
A3.03	09.15.2025 60% CDs	OVERALL REFLECTED CEILING PLAN - LEVEL THREE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A3.03A	09.15.2025 60% CDs	REFLECTED CEILING PLAN - LEVEL THREE - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A3.03B	09.15.2025 60% CDs	REFLECTED CEILING PLAN - LEVEL THREE - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A3.04	09.15.2025 60% CDs	OVERALL REFLECTED CEILING PLAN - LEVEL FOUR	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A3.04A	09.15.2025 60% CDs	REFLECTED CEILING PLAN - LEVEL FOUR - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A3.04B	09.15.2025 60% CDs	REFLECTED CEILING PLAN - LEVEL FOUR - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A3.10	09.15.2025 60% CDs	CEILING DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A3.11	09.15.2025 60% CDs	CEILING DETAILS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A3.12	01.07.2026 Build PS	CEILING DETAILS			1/7/2026	2/6/2026	2/19/2026		
A4.01	09.15.2025 60% CDs	OVERALL ROOF PLAN	9/15/2025	12/15/2025	1/7/2026				
A4.01A	09.15.2025 60% CDs	ROOF PLAN - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A4.01B	09.15.2025 60% CDs	ROOF PLAN - AREA B	9/15/2025	12/15/2025	1/7/2026				
A4.11	09.15.2025 60% CDs	ROOF DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A4.12	09.15.2025 60% CDs	ROOF DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A5.01	09.15.2025 60% CDs	AXON VIEWS	9/15/2025	12/15/2025	1/7/2026				
A5.02	09.15.2025 60% CDs	EXTERIOR ELEVATIONS - SOUTH	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A5.03	09.15.2025 60% CDs	EXTERIOR ELEVATIONS - EAST	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A5.04	09.15.2025 60% CDs	EXTERIOR ELEVATIONS - NORTH	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A5.05	09.15.2025 60% CDs	EXTERIOR ELEVATIONS - WEST	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A5.06	09.15.2025 60% CDs	ENLARGED GROUND LVL LOBBY	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A5.10	09.15.2025 60% CDs	DECK LEVEL THREE - ENLARGED ELEVATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A5.12	09.15.2025 60% CDs	ELEVATION RENDERINGS	9/15/2025	12/15/2025	1/7/2026				
A5.13	09.15.2025 60% CDs	EXTERIOR RENDERING VIEWS	9/15/2025	12/15/2025	1/7/2026				
A5.14	09.15.2025 60% CDs	EXTERIOR MATERIALS	9/15/2025	12/15/2025	1/7/2026				
A6.01	09.15.2025 60% CDs	BUILDING SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A6.02	09.15.2025 60% CDs	BUILDING SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A6.03	09.15.2025 60% CDs	BUILDING SECTIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A6.04	09.15.2025 60% CDs	BUILDING SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A7.01	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A7.02	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A7.03	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A7.04	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A7.10	09.15.2025 60% CDs	STAIR 01 - PLANS	9/15/2025	12/15/2025	1/7/2026				
A7.11	09.15.2025 60% CDs	STAIR 01 - SECTIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A7.12	09.15.2025 60% CDs	STAIR 02 - PLANS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A7.13	09.15.2025 60% CDs	STAIR 02 - SECTIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A7.14	09.15.2025 60% CDs	STAIR 03 - PLANS AND SECTIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A7.15	09.15.2025 60% CDs	STAIR 04 - PLANS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A7.16	09.15.2025 60% CDs	STAIR 04 - SECTIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A7.17	02.19.2026 Add B Issue	STAIR 04 - SECTIONS					2/19/2026		
A7.20	09.15.2025 60% CDs	STAIR DETAILS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		

RFP 607319-24
EXHIBIT D - TECHNICAL SPECIFICATIONS AND DRAWINGS

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company
2/19/2026

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
A7.21	01.07.2026 Build PS	STAIR DETAILS			1/7/2026		2/19/2026		
A7.30	09.15.2025 60% CDs	ELEVATION A - PLANS AND SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A7.31	09.15.2025 60% CDs	ELEVATION B - PLANS AND SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A7.32	01.07.2026 Build PS	ELEVATOR DETAILS			1/7/2026				
A8.01	09.15.2025 60% CDs	TRAINING CENTER - DOOR SCHEDULE AND TYPES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A8.02	09.15.2025 60% CDs	TRAINING CENTER - WINDOW TYPES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A8.03	09.15.2025 60% CDs	TRAINING CENTER - WINDOW TYPES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A8.04	09.15.2025 60% CDs	TRAINING CENTER - WINDOW TYPES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A8.10	09.15.2025 60% CDs	TRAINING CENTER - DOOR DETAILS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A8.11	09.15.2025 60% CDs	TRAINING CENTER - DOOR DETAILS	9/15/2025	12/15/2025	1/7/2026				
A8.12	09.15.2025 60% CDs	TRAINING CENTER - WINDOW DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A8.13	09.15.2025 60% CDs	TRAINING CENTER - WINDOW DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A8.14	01.07.2026 Build PS	TRAINING CENTER - WINDOW DETAILS			1/7/2026	2/6/2026	2/19/2026		
A9.01	09.15.2025 60% CDs	TRAINING CENTER - CASEWORK DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A9.02	09.15.2025 60% CDs	TRAINING CENTER - EXTERIOR DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A9.03	09.15.2025 60% CDs	TRAINING CENTER - MISC DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A9.07	01.07.2026 Build PS	TRAINING CENTER - MISC DETAILS			1/7/2026	2/6/2026	2/19/2026		
		Structural Drawings							
SG0.01	09.15.2025 60% CDs	COVER SHEET	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
SG0.02	09.15.2025 60% CDs	GENERAL NOTES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
SG0.03	09.15.2025 60% CDs	GENERAL NOTES	9/15/2025	12/15/2025	1/7/2026				
SG0.04	09.15.2025 60% CDs	GENERAL NOTES	9/15/2025	12/15/2025	1/7/2026				
SG0.05	09.15.2025 60% CDs	GENERAL NOTES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S1.01	09.15.2025 60% CDs	TRAINING CENTER OVERALL FOUNDATION PLAN	9/15/2025	12/15/2025	1/7/2026				
S1.01A	09.15.2025 60% CDs	TRAINING CENTER FOUNDATION PLAN - A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
S1.01B	09.15.2025 60% CDs	TRAINING CENTER FOUNDATION PLAN - B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
S1.02	09.15.2025 60% CDs	TRAINING CENTER LEVEL 2 PLAN	9/15/2025	12/15/2025	1/7/2026				
S1.02A	09.15.2025 60% CDs	TRAINING CENTER LEVEL 2 FRAMING PLAN - A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
S1.02B	09.15.2025 60% CDs	TRAINING CENTER LEVEL 2 FRAMING PLAN - B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S1.03	09.15.2025 60% CDs	TRAINING CENTER LEVEL 3 PLAN	9/15/2025	12/15/2025	1/7/2026				
S1.03A	09.15.2025 60% CDs	TRAINING CENTER LEVEL 3 FRAMING PLAN - A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S1.03B	09.15.2025 60% CDs	TRAINING CENTER LEVEL 3 FRAMING PLAN - B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S1.04	09.15.2025 60% CDs	TRAINING CENTER LEVEL 4 PLAN	9/15/2025	12/15/2025	1/7/2026				
S1.04A	09.15.2025 60% CDs	TRAINING CENTER LEVEL 4 FRAMING PLAN - A	9/15/2025	12/15/2025	1/7/2026				
S1.04B	09.15.2025 60% CDs	TRAINING CENTER LEVEL 4 FRAMING PLAN - B	9/15/2025	12/15/2025	1/7/2026				
S4.01	09.15.2025 60% CDs	TRAINING CENTER ROOF PLAN	9/15/2025	12/15/2025	1/7/2026				
S4.01A	09.15.2025 60% CDs	TRAINING CENTER ROOF FRAMING PLAN - A	9/15/2025	12/15/2025	1/7/2026				
S4.01B	09.15.2025 60% CDs	TRAINING CENTER ROOF FRAMING PLAN - B	9/15/2025	12/15/2025	1/7/2026				
S5.02A	09.15.2025 60% CDs	CONCRETE BEAM ELEVATIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S5.02B	09.15.2025 60% CDs	CONCRETE BEAM ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
S5.02C	09.15.2025 60% CDs	CONCRETE BEAM ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
S5.03A	09.15.2025 60% CDs	CONCRETE BEAM ELEVATIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S5.03B	09.15.2025 60% CDs	CONCRETE BEAM ELEVATIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S5.03C	09.15.2025 60% CDs	CONCRETE BEAM ELEVATIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S6.01	09.15.2025 60% CDs	BRACE ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
S7.01	09.15.2025 60% CDs	ENLARGED SHEAR WALL PLANS	9/15/2025	12/15/2025	1/7/2026				
S7.02	09.15.2025 60% CDs	ENLARGED SHEAR WALL PLANS	9/15/2025	12/15/2025	1/7/2026				
S7.03	09.15.2025 60% CDs	ENLARGED SHEAR WALL PLANS	9/15/2025	12/15/2025	1/7/2026				
S7.04	09.15.2025 60% CDs	ENLARGED SHEAR WALL PLANS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S7.05	12.15.2025 95% CDs	CHORD REINFORCING PLANS		12/15/2025	1/7/2026				
S7.10	09.15.2025 60% CDs	ENLARGED STAIR PLANS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S7.11	09.15.2025 60% CDs	ENLARGED STAIR PLANS	9/15/2025	12/15/2025	1/7/2026				
S7.12	09.15.2025 60% CDs	ENLARGED STAIR PLANS	9/15/2025	12/15/2025	1/7/2026				
S7.13	09.15.2025 60% CDs	ENLARGED STAIR PLANS	9/15/2025	12/15/2025	1/7/2026				
S7.21	12.15.2025 95% CDs	ENLARGED FOOTING PLANS		12/15/2025	1/7/2026				
S7.51	09.15.2025 60% CDs	WALL ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
S7.52	09.15.2025 60% CDs	WALL ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
S7.53	09.15.2025 60% CDs	WALL ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
S9.01	09.15.2025 60% CDs	FOUNDATION SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S9.02	09.15.2025 60% CDs	FOUNDATION SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S9.04	09.15.2025 60% CDs	CONCRETE SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.05	09.15.2025 60% CDs	CONCRETE SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.06	09.15.2025 60% CDs	CONCRETE SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S9.07	09.15.2025 60% CDs	CONCRETE SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.08	09.15.2025 60% CDs	CONCRETE SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.09	09.15.2025 60% CDs	CONCRETE SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
S9.30	09.15.2025 60% CDs	SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S9.31	09.15.2025 60% CDs	SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
S9.45	09.15.2025 60% CDs	MASONRY SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S9.40	09.15.2025 60% CDs	STEEL FRAMING SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.41	09.15.2025 60% CDs	STEEL FRAMING SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.42	09.15.2025 60% CDs	STEEL FRAMING SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.43	09.15.2025 60% CDs	STEEL SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.50	09.15.2025 60% CDs	STAIR SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S9.51	02.19.2026 Add'l B Issue	STAIR SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S9.60	09.15.2025 60% CDs	STEEL SECTIONS AND DETAILS					2/19/2026		
		Food Service Drawings	9/15/2025	12/15/2025	1/7/2026				
FS1.02	09.15.2025 60% CDs	FOOD SERVICE EQUIPMENT FLOOR PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS2.01	09.15.2025 60% CDs	FOOD SERVICE EQUIPMENT SCHEDULE	9/15/2025	12/15/2025	1/7/2026				
FS3.01	09.15.2025 60% CDs	FOOD SERVICE ELECTRICAL PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS4.01	09.15.2025 60% CDs	FOOD SERVICE PLUMBING PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS4.01.1	09.15.2025 60% CDs	FOOD SERVICE PLUMBING FLOOR SINK & FLOOR DRAIN PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS5.01	09.15.2025 60% CDs	FOOD SERVICE REFRIGERATION / EXHAUST HOOD PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS6.01	09.15.2025 60% CDs	FOOD SERVICE BUILDING CONDITIONS PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS7.01	12.15.2025 95% CDs	FOOD SERVICE ELEVATION		12/15/2025	1/7/2026		2/19/2026		
FS1.04	09.15.2025 60% CDs	FOOD SERVICE EQUIPMENT PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS2.04	09.15.2025 60% CDs	FOOD SERVICE EQUIPMENT SCHEDULE	9/15/2025	12/15/2025	1/7/2026				
FS3.04	09.15.2025 60% CDs	FOOD SERVICE ELECTRICAL PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS4.04	09.15.2025 60% CDs	FOOD SERVICE PLUMBING PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS4.04.1	09.15.2025 60% CDs	FOOD SERVICE PLUMBING FLOOR SINK & FLOOR DRAIN PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS5.04	09.15.2025 60% CDs	FOOD SERVICE REFRIGERATION / EXHAUST HOOD PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS6.04	09.15.2025 60% CDs	FOOD SERVICE BUILDING CONDITIONS PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
FS7.04	12.15.2025 95% CDs	FOOD SERVICE ELEVATION		12/15/2025	1/7/2026		2/19/2026		
FS8.04	09.15.2025 60% CDs	FOOD SERVICE WALK IN COOLER SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS8.04.1	09.15.2025 60% CDs	FOOD SERVICE WALK IN COOLER SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS9.04	09.15.2025 60% CDs	FOOD SERVICE REFRIGERATION SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS10.04	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS10.04.1	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS10.04.2	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS10.04.3	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS10.04.4	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS10.04.5	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS10.04.6	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS10.04.7	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWING	9/15/2025	12/15/2025	1/7/2026				
FS1.05	09.15.2025 60% CDs	FOOD SERVICE EQUIPMENT PLAN	9/15/2025	12/15/2025	1/7/2026				
FS2.05	09.15.2025 60% CDs	FOOD SERVICE ELECTRICAL SCHEDULE	9/15/2025	12/15/2025	1/7/2026				
FS3.05	09.15.2025 60% CDs	FOOD SERVICE ELECTRICAL PLAN	9/15/2025	12/15/2025	1/7/2026				
FS4.05	09.15.2025 60% CDs	FOOD SERVICE PLUMBING PLAN	9/15/2025	12/15/2025	1/7/2026				
FS4.05.1	09.15.2025 60% CDs	FOOD SERVICE PLUMBING FLOOR SINK & FLOOR DRAIN PLAN	9/15/2025	12/15/2025	1/7/2026				
FS6.05	09.15.2025 60% CDs	FOOD SERVICE BUILDING CONDITIONS PLAN	9/15/2025	12/15/2025	1/7/2026				
FS7.05	12.15.2025 95% CDs	FOOD SERVICE ELEVATION		12/15/2025	1/7/2026				
		Mechanical Drawings							
M0.00	09.15.2025 60% CDs	MECHANICAL LEGEND, NOTES AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M0.01	01.07.2026 Build PS	MECHANICAL COMISSIONING			1/7/2026				
M0.03	12.15.2025 95% CDs	MECHANICAL ZONING PLAN - LEVEL 3		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M0.04	12.15.2025 95% CDs	MECHANICAL ZONING PLAN - LEVEL 4		12/15/2025	1/7/2026				
M1.01	09.15.2025 60% CDs	OVERALL MECHANICAL PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026				
M1.01.1	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - LEVEL 1 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M1.01.2	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - LEVEL 1 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M1.02	09.15.2025 60% CDs	OVERALL MECHANICAL PLAN - LEVEL 2	9/15/2025	12/15/2025	1/7/2026				
M1.02.1	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - LEVEL 2 - AREA A	9/15/2025	12/15/2025	1/7/2026				
M1.02.2	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - LEVEL 2 - AREA B	9/15/2025	12/15/2025	1/7/2026				
M1.03	09.15.2025 60% CDs	OVERALL MECHANICAL PLAN - LEVEL 3	9/15/2025	12/15/2025	1/7/2026				
M1.03.1	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - LEVEL 3 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M1.03.2	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - LEVEL 3 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M1.04	09.15.2025 60% CDs	OVERALL MECHANICAL PLAN - LEVEL 4	9/15/2025	12/15/2025	1/7/2026				
M1.04.1	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - LEVEL 4 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M1.04.2	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - LEVEL 4 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M1.05	09.15.2025 60% CDs	OVERALL MECHANICAL PLAN - ROOF	9/15/2025	12/15/2025	1/7/2026				
M1.05.1	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - ROOF - AREA A	9/15/2025	12/15/2025	1/7/2026				
M1.05.2	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - ROOF - AREA B	9/15/2025	12/15/2025	1/7/2026				
M5.00	09.15.2025 60% CDs	MECHANICAL DETAILS	9/15/2025	12/15/2025	1/7/2026				
M6.00	09.15.2025 60% CDs	MECHANICAL SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M6.01	09.15.2025 60% CDs	MECHANICAL SCHEDULES	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
M7.00	01.07.2026 Build PS	MECHANICAL CONTROLS			1/7/2026				
M7.01	01.07.2026 Build PS	MECHANICAL CONTROLS			1/7/2026				

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
M7.02	01.07.2026 Build PS	MECHANICAL CONTROLS			1/7/2026				
M8.00	09.15.2025 60% CDs	AXONOMETRIC VIEW - ROOF	9/15/2025	12/15/2025	1/7/2026				
M9.00	01.07.2026 Build PS	KITCHEN HOOD DRAWINGS			1/7/2026				
M9.01	01.07.2026 Build PS	KITCHEN HOOD DRAWINGS			1/7/2026				
M9.02	01.07.2026 Build PS	KITCHEN HOOD DRAWINGS			1/7/2026				
M9.03	01.07.2026 Build PS	KITCHEN HOOD DRAWINGS			1/7/2026				
M9.04	01.07.2026 Build PS	KITCHEN HOOD DRAWINGS			1/7/2026				
M9.05	01.07.2026 Build PS	KITCHEN HOOD DRAWINGS			1/7/2026				
M9.06	01.07.2026 Build PS	KITCHEN HOOD DRAWINGS			1/7/2026				
M9.07	01.07.2026 Build PS	KITCHEN HOOD DRAWINGS			1/7/2026				
		Plumbing Site Drawings							
P0.00	09.15.2025 60% CDs	PLUMBING GENERAL NOTES, AND LEGENDS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
P0.01	09.15.2025 60% CDs	PLUMBING SPECIFICATIONS	9/15/2025	12/15/2025	1/7/2026				
P1.00	09.15.2025 60% CDs	PLUMBING SITE PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
		Plumbing Drawings							
P0.00	09.15.2025 60% CDs	PLUMBING INDEX, GENERAL NOTES, LEGEND, AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026				
P0.01_	09.15.2025 60% CDs	PLUMBING SPECIFICATIONS	9/15/2025	12/15/2025	1/7/2026				
P1.01	09.15.2025 60% CDs	PLUMBING PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P1.02	09.15.2025 60% CDs	PLUMBING PLAN - LEVEL 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P1.03	09.15.2025 60% CDs	PLUMBING PLAN - LEVEL 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P1.04	09.15.2025 60% CDs	PLUMBING PLAN - LEVEL 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P1.06	09.15.2025 60% CDs	PLUMBING PLAN - ROOF	9/15/2025	12/15/2025	1/7/2026	2/5/2026			
P2.01.1	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 1 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P2.01.2	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 1 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P2.02.1	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 2 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P2.02.2	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 2 - AREA B	9/15/2025	12/15/2025	1/7/2026				
P2.03.1	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 3 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P2.03.2	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 3 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P2.04.1	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 4 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P2.04.2	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 4 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/5/2026			
P2.06.1	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - ROOF - AREA A	9/15/2025	12/15/2025	1/7/2026				
P2.06.2	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - ROOF - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P3.01.1	09.15.2025 60% CDs	PLUMBING WATER SYSTEMS PLAN - LEVEL 1 - AREA A	9/15/2025	12/15/2025	1/7/2026				
P3.01.2	09.15.2025 60% CDs	PLUMBING WATER SYSTEMS PLAN - LEVEL 1 - AREA B	9/15/2025	12/15/2025	1/7/2026				
P3.02.1	09.15.2025 60% CDs	PLUMBING WATER SYSTEMS PLAN - LEVEL 2 - AREA A	9/15/2025	12/15/2025	1/7/2026				
P3.02.2	09.15.2025 60% CDs	PLUMBING WATER SYSTEMS PLAN - LEVEL 2 - AREA B	9/15/2025	12/15/2025	1/7/2026				
P3.03.1	09.15.2025 60% CDs	PLUMBING WATER SYSTEMS PLAN - LEVEL 3 - AREA A	9/15/2025	12/15/2025	1/7/2026				
P3.03.2	09.15.2025 60% CDs	PLUMBING WATER SYSTEMS PLAN - LEVEL 3 - AREA B	9/15/2025	12/15/2025	1/7/2026				
P3.04.1	09.15.2025 60% CDs	PLUMBING WATER SYSTEMS PLAN - LEVEL 4 - AREA A	9/15/2025	12/15/2025	1/7/2026				
P3.04.2	09.15.2025 60% CDs	PLUMBING WATER SYSTEMS PLAN - LEVEL 4 - AREA B	9/15/2025	12/15/2025	1/7/2026				
P4.01.1	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - LEVEL 1 - AREA A	9/15/2025	12/15/2025	1/7/2026				
P4.01.2	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - LEVEL 1 - AREA B	9/15/2025	12/15/2025	1/7/2026				
P4.02.1	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - LEVEL 2 - AREA A	9/15/2025	12/15/2025	1/7/2026				
P4.02.2	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - LEVEL 2 - AREA B	9/15/2025	12/15/2025	1/7/2026				
P4.03.1	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - LEVEL 3 - AREA A	9/15/2025	12/15/2025	1/7/2026				
P4.03.2	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - LEVEL 3 - AREA B	9/15/2025	12/15/2025	1/7/2026				
P4.04.1	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - LEVEL 4 - AREA A	9/15/2025	12/15/2025	1/7/2026				
P4.04.2	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - LEVEL 4 - AREA B	9/15/2025	12/15/2025	1/7/2026				
P4.06.1	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - ROOF - AREA A	9/15/2025	12/15/2025	1/7/2026				
P4.06.2	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - ROOF - AREA B	9/15/2025	12/15/2025	1/7/2026				
P5.00	09.15.2025 60% CDs	PLUMBING DIAGRAMS - WASTE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P5.01	09.15.2025 60% CDs	PLUMBING DIAGRAMS - WATER	9/15/2025	12/15/2025	1/7/2026				
P5.02	12.15.2025 95% CDs	PLUMBING DIAGRAMS - TYPICAL FIXTURES		12/15/2025	1/7/2026				
P6.00	09.15.2025 60% CDs	PLUMBING SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P6.50	12.15.2025 95% CDs	PLUMBING CALCULATIONS		12/15/2025	1/7/2026				
P7.00	09.15.2025 60% CDs	PLUMBING RISER DIAGRAMS - WASTE LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P7.01	09.15.2025 60% CDs	PLUMBING RISER DIAGRAMS - WASTE LEVEL 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P7.02	12.15.2025 95% CDs	PLUMBING RISER DIAGRAMS - WASTE RESTROOMS		12/15/2025	1/7/2026				
P7.03	12.15.2025 95% CDs	PLUMBING RISER DIAGRAMS - WATER		12/15/2025	1/7/2026				
P8.00	12.15.2025 95% CDs	ENLARGED FLOOR PLANS - WASTE & VENT		12/15/2025	1/7/2026				
P8.01	12.15.2025 95% CDs	ENLARGED FLOOR PLANS - WASTE & VENT		12/15/2025	1/7/2026				
P9.00	12.15.2025 95% CDs	ENLARGED FLOOR PLANS - WATER & GAS		12/15/2025	1/7/2026				
P9.01	12.15.2025 95% CDs	ENLARGED FLOOR PLANS - WATER & GAS		12/15/2025	1/7/2026				
		Electrical Site Drawings							
ES0.00	09.15.2025 60% CDs	ELECTRICAL LEGEND, NOTES, AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES0.01	09.15.2025 60% CDs	IECC, LIGHT FIXTURE SCHEDULE, AND ELECTRICAL DIAGRAMS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES1.00	09.15.2025 60% CDs	ELECTRICAL SITE PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES1.00P	09.15.2025 60% CDs	ELECTRICAL SITE PHOTOMETRIC	9/15/2025	12/15/2025	1/7/2026	2/6/2026			

RFP 607319-24
EXHIBIT D - TECHNICAL SPECIFICATIONS AND DRAWINGS

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company
2/19/2026

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
ES1.00PE	12.15.2025 95% CDs	ELECTRICAL SITE PHOTOMETRIC - EMERGENCY		12/15/2025	1/7/2026	2/6/2026			
ES1.10	09.15.2025 60% CDs	ELECTRICAL ENLARGED SITE PLAN - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES1.11	09.15.2025 60% CDs	ELECTRICAL ENLARGED SITE PLAN - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES1.12	09.15.2025 60% CDs	ELECTRICAL ENLARGED SITE PLAN - AREA C	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES5.00	09.15.2025 60% CDs	SINGLE LINE DIAGRAM & SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES6.00	12.15.2025 95% CDs	ELECTRICAL SITE SCHEDULES		12/15/2025	1/7/2026	2/6/2026			
		Electrical Drawings							
E0.00	09.15.2025 60% CDs	ELECTRICAL LEGEND, NOTES, AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E0.01	09.15.2025 60% CDs	IECC AND LIGHT FIXTURE SCHEDULE	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E0.02	12.15.2025 95% CDs	IECC LIGHTING COMPLIANCE		12/15/2025	1/7/2026		2/19/2026		
E1.01	09.15.2025 60% CDs	OVERALL ELECTRICAL PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E1.01A	09.15.2025 60% CDs	ELECTRICAL PLAN - LEVEL 1 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E1.01B	09.15.2025 60% CDs	ELECTRICAL PLAN - LEVEL 1 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E1.02	09.15.2025 60% CDs	OVERALL ELECTRICAL PLAN - LEVEL 2	9/15/2025	12/15/2025	1/7/2026				
E1.02A	09.15.2025 60% CDs	ELECTRICAL PLAN - LEVEL 2 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E1.02B	09.15.2025 60% CDs	ELECTRICAL PLAN - LEVEL 2 - AREA B	9/15/2025	12/15/2025	1/7/2026				
E1.03	09.15.2025 60% CDs	OVERALL ELECTRICAL PLAN - LEVEL 3	9/15/2025	12/15/2025	1/7/2026				
E1.03A	09.15.2025 60% CDs	POWER PLAN - LEVEL 3 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E1.03B	09.15.2025 60% CDs	POWER PLAN - LEVEL 3 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E1.04	09.15.2025 60% CDs	OVERALL ELECTRICAL PLAN - LEVEL 4	9/15/2025	12/15/2025	1/7/2026				
E1.04A	09.15.2025 60% CDs	POWER PLAN - LEVEL 4 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E1.04B	09.15.2025 60% CDs	POWER PLAN - LEVEL 4 - AREA B	9/15/2025	12/15/2025	1/7/2026				
E1.05	12.15.2025 95% CDs	OVERALL ELECTRICAL PLAN - ROOF		12/15/2025	1/7/2026		2/19/2026		
E2.01	09.15.2025 60% CDs	SECTION PLANS - STAIRS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E2.02	09.15.2025 60% CDs	ENLARGED PLANS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E2.03	12.15.2025 95% CDs	SECTION PLANS - ELEVATORS		12/15/2025	1/7/2026				
E2.04	12.15.2025 95% CDs	ENLARGED PLANS		12/15/2025	1/7/2026				
E3.03A	09.15.2025 60% CDs	LIGHTING PLAN - LEVEL 3 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E3.03B	09.15.2025 60% CDs	LIGHTING PLAN - LEVEL 3 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E3.01A	09.15.2025 60% CDs	LIGHTING PLAN - LEVEL 1 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E3.01B	09.15.2025 60% CDs	LIGHTING PLAN - LEVEL 1 - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E5.00	09.15.2025 60% CDs	SINGLE LINE DIAGRAM & SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E5.01	12.15.2025 95% CDs	SCHEDULES		12/15/2025	1/7/2026	2/6/2026			
E6.00	09.15.2025 60% CDs	ELECTRICAL SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
E6.01	09.15.2025 60% CDs	ELECTRICAL SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
		Telecom Drawings							
T001	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE LEGENDS AND NOTES	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T002	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE LEGENDS AND LEGEND NOTES	9/15/2025	12/15/2025	1/7/2026				
T003	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE LEGENDS AND SCHEDULES	9/15/2025	12/15/2025	1/7/2026				
T101A	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL ONE - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T101B	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL ONE - AREA B	9/15/2025	12/15/2025	1/7/2026				
T102A	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL TWO - AREA A	9/15/2025	12/15/2025	1/7/2026				
T102B	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL TWO - AREA B	9/15/2025	12/15/2025	1/7/2026				
T103A	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL THREE - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T103B	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL THREE - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T104A	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL FOUR - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T104B	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL FOUR - AREA B	9/15/2025	12/15/2025	1/7/2026				
T106A	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL ROOF - AREA A	9/15/2025	12/15/2025	1/7/2026				
T106B	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL ROOF - AREA B	9/15/2025	12/15/2025	1/7/2026				
T301A	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL ONE - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T301B	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL ONE - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T302A	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL TWO - AREA A	9/15/2025	12/15/2025	1/7/2026				
T302B	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL TWO - AREA B	9/15/2025	12/15/2025	1/7/2026				
T303A	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL THREE - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T303B	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL THREE - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T304A	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL FOUR - AREA A	9/15/2025	12/15/2025	1/7/2026				
T304B	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL FOUR - AREA B	9/15/2025	12/15/2025	1/7/2026				
T400	09.15.2025 60% CDs	TELECOM SITE PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T401A	09.15.2025 60% CDs	TELECOM PLAN LEVEL ONE - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T401B	09.15.2025 60% CDs	TELECOM PLAN LEVEL ONE - AREA B	9/15/2025	12/15/2025	1/7/2026				
T402A	09.15.2025 60% CDs	TELECOM PLAN LEVEL TWO - AREA A	9/15/2025	12/15/2025	1/7/2026				
T402B	09.15.2025 60% CDs	TELECOM PLAN LEVEL TWO - AREA B	9/15/2025	12/15/2025	1/7/2026				
T403A	09.15.2025 60% CDs	TELECOM PLAN LEVEL THREE - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T403B	09.15.2025 60% CDs	TELECOM PLAN LEVEL THREE - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T404A	09.15.2025 60% CDs	TELECOM PLAN LEVEL FOUR - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T404B	09.15.2025 60% CDs	TELECOM PLAN LEVEL FOUR - AREA B	9/15/2025	12/15/2025	1/7/2026				
T406A	09.15.2025 60% CDs	TELECOM PLAN ROOF - AREA A	9/15/2025	12/15/2025	1/7/2026				
T406B	09.15.2025 60% CDs	TELECOM PLAN ROOF - AREA B	9/15/2025	12/15/2025	1/7/2026				

RFP 607319-24
EXHIBIT D - TECHNICAL SPECIFICATIONS AND DRAWINGS

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
T501	09.15.2025 60% CDs	TELECOM ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T502	09.15.2025 60% CDs	TELECOM ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T601	09.15.2025 60% CDs	AUDIOVISUAL INFRASTRUCTURE ROOM RISERS	9/15/2025	12/15/2025	1/7/2026				
T652	09.15.2025 60% CDs	TELECOM BUILDING RISER	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T701	09.15.2025 60% CDs	TYPICAL TELECOM RISER	9/15/2025	12/15/2025	1/7/2026				
T702	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
T801	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
T802	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE DETAILS	9/15/2025	12/15/2025	1/7/2026				
		TECHNOLOGY INFRASTRUCTURE DETAILS	9/15/2025	12/15/2025	1/7/2026				
		Fire Alarm Drawings							
FA0.10	09.15.2025 60% CDs	FIRE ALARM GENERAL NOTES, ABBREVIATIONS AND LEGENDS	9/15/2025	12/15/2025	1/7/2026				
FA1.01	09.15.2025 60% CDs	OVERALL FIRE ALARM PLAN - LEVEL ONE	9/15/2025	12/15/2025	1/7/2026				
FA1.02	09.15.2025 60% CDs	OVERALL FIRE ALARM PLAN - LEVEL TWO	9/15/2025	12/15/2025	1/7/2026				
FA1.03	09.15.2025 60% CDs	OVERALL FIRE ALARM PLAN - LEVEL THREE	9/15/2025	12/15/2025	1/7/2026				
FA1.04	09.15.2025 60% CDs	OVERALL FIRE ALARM PLAN - LEVEL FOUR	9/15/2025	12/15/2025	1/7/2026				
		Security Drawings							
Y001	09.15.2025 60% CDs	SECURITY SYMBOLS LEGEND NOTES, AND SCHEDULES	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y100	09.15.2025 60% CDs	SECURITY SITE PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y101A	09.15.2025 60% CDs	SECURITY PLAN LEVEL ONE - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y101B	09.15.2025 60% CDs	SECURITY PLAN LEVEL ONE - AREA B	9/15/2025	12/15/2025	1/7/2026				
Y102A	09.15.2025 60% CDs	SECURITY PLAN LEVEL TWO - AREA A	9/15/2025	12/15/2025	1/7/2026				
Y102B	09.15.2025 60% CDs	SECURITY PLAN LEVEL TWO - AREA B	9/15/2025	12/15/2025	1/7/2026				
Y103A	09.15.2025 60% CDs	SECURITY PLAN LEVEL THREE - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y103B	09.15.2025 60% CDs	SECURITY PLAN LEVEL THREE - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y104A	09.15.2025 60% CDs	SECURITY PLAN LEVEL FOUR - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y104B	09.15.2025 60% CDs	SECURITY PLAN LEVEL FOUR - AREA B	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y106A	09.15.2025 60% CDs	SECURITY PLAN ROOF - AREA A	9/15/2025	12/15/2025	1/7/2026				
Y106B	09.15.2025 60% CDs	SECURITY PLAN ROOF - AREA B	9/15/2025	12/15/2025	1/7/2026				
Y801	09.15.2025 60% CDs	SECURITY DETAILS	9/15/2025	12/15/2025	1/7/2026				
Y802	01.07.2026 Build PS	SECURITY DETAILS			1/7/2026				
		FIRE STATION 88							
		DRAWINGS							
		General							
G0.00	09.15.2025 60% CDs	COVER SHEET	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
G0.04	09.15.2025 60% CDs	GENERAL INFORMATION/CODE ANALYSIS - FIRE STATION	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
G0.20	09.15.2025 60% CDs	ACCESIBILITY SHEET	9/15/2025	12/15/2025	1/7/2026				
G1.20	09.15.2025 60% CDs	LIFE SAFETY PLAN - FIRE STATION	9/15/2025	12/15/2025	1/7/2026				
G1.32	12.15.2025 95% CDs	IBCC ENVELOPE COMPLIANCE - FIRE STATION		12/15/2025	1/7/2026				
		Civil Drawings							
C1.01	09.15.2025 60% CDs	COVER SHEET	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C1.02	09.15.2025 60% CDs	GENERAL NOTES SHEET	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C1.03	09.15.2025 60% CDs	PROJECT DATA	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.01	09.15.2025 60% CDs	DEMOLITION PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C2.02	09.15.2025 60% CDs	DEMOLITION PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.03	09.15.2025 60% CDs	DEMOLITION PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.04	09.15.2025 60% CDs	DEMOLITION PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.05	09.15.2025 60% CDs	DEMOLITION PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C3.01	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.02	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.03	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.04	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.05	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C4.01	09.15.2025 60% CDs	TRAFFIC SIGNAL PLAN AT TROPICANA AND ARVILLE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C4.02	09.15.2025 60% CDs	TRAFFIC SIGNAL SCHEDULE AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C4.03	09.15.2025 60% CDs	EMERGENCY SIGNAL PLAN SCHEDULE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C4.04	09.15.2025 60% CDs	GENERAL TRAFFIC NOTES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C5.01	09.15.2025 60% CDs	MASTER GRADING PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C5.02	09.15.2025 60% CDs	GRADING PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.03	09.15.2025 60% CDs	GRADING PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.04	09.15.2025 60% CDs	GRADING PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.05	09.15.2025 60% CDs	GRADING PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.06	09.15.2025 60% CDs	GRADING PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.01	09.15.2025 60% CDs	TROPICANA AVE & PROFILE	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.02	12.15.2025 95% CDs	TROPICANA AVE - UTILITY PLAN AND PROFILE		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.03	12.15.2025 95% CDs	ARVILLE ST - UTILITY PLAN AND PROFILE 1		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.04	12.15.2025 95% CDs	ARVILLE ST - UTILITY PLAN AND PROFILE 2		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.05	12.15.2025 95% CDs	ARVILLE ST - UTILITY PLAN AND PROFILE 3		12/15/2025	1/7/2026	2/6/2026	2/19/2026		

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
C6.06	01.07.2026 Build PS	SEWER LATERAL PLAN AND PROFILES			1/7/2026	2/6/2026	2/19/2026		
C7.01	09.15.2025 60% CDs	MASTER UTILITY SHEET	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.02	09.15.2025 60% CDs	UTILITY PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.03	09.15.2025 60% CDs	UTILITY PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.04	09.15.2025 60% CDs	UTILITY PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.05	09.15.2025 60% CDs	UTILITY PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.06	09.15.2025 60% CDs	UTILITY PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C8.01	09.15.2025 60% CDs	GENERAL STRUCTURAL NOTES & TYPICAL DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C8.02	09.15.2025 60% CDs	JUCTION STRUCTURES	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C8.03	09.15.2025 60% CDs	RETAINING WALL	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C9.01	09.15.2025 60% CDs	DETAIL SHEET 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C9.02	09.15.2025 60% CDs	DETAIL SHEET 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C9.03	09.15.2025 60% CDs	DETAIL SHEET 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C9.04	12.15.2025 95% CDs	DETAIL SHEET 4		12/15/2025	1/7/2026				
		Landscape Drawings							
L1.01	09.15.2025 60% CDs	OVERALL LANDSCAPE PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L1.02	09.15.2025 60% CDs	LANDSCAPE PLAN ENLARGEMENT "A"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L1.03	09.15.2025 60% CDs	LANDSCAPE PLAN ENLARGEMENT "B"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L1.04	12.15.2025 95% CDs	LEVEL 3 PLAZA PLANTING PLAN		12/15/2025	1/7/2026				
L2.01	09.15.2025 60% CDs	OVERALL IRRIGATION PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L2.02	09.15.2025 60% CDs	IRRIGATION PLAN ENLARGEMENT "A"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L2.03	09.15.2025 60% CDs	IRRIGATION PLAN ENLARGEMENT "B"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L3.01	09.15.2025 60% CDs	PROJECT DETAILS	9/15/2025	12/15/2025	1/7/2026				
L3.02	12.15.2025 95% CDs	PROJECT DETAILS		12/15/2025	1/7/2026				
		Architectural Site Drawings							
AS1.01	09.15.2025 60% CDs	OVERALL ARCHITECTURAL SITE PLAN	9/15/2025	12/15/2025	1/7/2026				
AS1.10	09.15.2025 60% CDs	ENLARGED ARCHITECTURAL SITE PLAN - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.11	09.15.2025 60% CDs	ENLARGED ARCHITECTURAL SITE PLAN - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.12	09.15.2025 60% CDs	ENLARGED ARCHITECTURAL SITE PLAN - AREA C	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.20	09.15.2025 60% CDs	ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.21	09.15.2025 60% CDs	ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS3.00	09.15.2025 60% CDs	SITE GATE SCHEDULE AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS3.10	09.15.2025 60% CDs	ARCHITECTURAL SITE DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
		Architectural Drawings							
A0.20	09.15.2025 60% CDs	PARTITION TYPES	9/15/2025	12/15/2025	1/7/2026				
A1.20	09.15.2025 60% CDs	FLOOR PLAN / DIMENSION PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A1.21	09.15.2025 60% CDs	SIGNAGE PLAN	9/15/2025	12/15/2025	1/7/2026				
A1.60	09.15.2025 60% CDs	FINISH INDEX	9/15/2025	12/15/2025	1/7/2026				
A1.61	09.15.2025 60% CDs	FINISH AND REFF PLANS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.20	09.15.2025 60% CDs	FIRE STATION - ENLARGED PLANS & ELEVATIONS - CAPTAIN'S AND PUBLIC RESTROOMS	9/15/2025	12/15/2025	1/7/2026				
A2.21	09.15.2025 60% CDs	FIRE STATION - ENLARGED PLANS & ELEVATIONS - CREW RESTROOMS & SHOWER	9/15/2025	12/15/2025	1/7/2026				
A2.22	09.15.2025 60% CDs	FIRE STATION - ENLARGED PLANS & ELEVATIONS - DISPATCH, FITNESS, KITCHEN	9/15/2025	12/15/2025	1/7/2026				
A3.20	09.15.2025 60% CDs	REFLECTED CEILING PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A3.21	09.15.2025 60% CDs	CEILING DETAILS	9/15/2025	12/15/2025	1/7/2026				
A3.22	09.15.2025 60% CDs	CEILING DETAILS	9/15/2025	12/15/2025	1/7/2026				
A4.20	09.15.2025 60% CDs	ROOF PLAN	9/15/2025	12/15/2025	1/7/2026				
A4.21	09.15.2025 60% CDs	ROOF DETAILS	9/15/2025	12/15/2025	1/7/2026				
A4.22	09.15.2025 60% CDs	ROOF DETAILS	9/15/2025	12/15/2025	1/7/2026				
A5.20	09.15.2025 60% CDs	EXTERIOR ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
A5.21	09.15.2025 60% CDs	EXTERIOR ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
A5.24	09.15.2025 60% CDs	EXTERIOR AXONS	9/15/2025	12/15/2025	1/7/2026				
A5.25	09.15.2025 60% CDs	EXTERIOR RENDERINGS	9/15/2025	12/15/2025	1/7/2026				
A5.26	09.15.2025 60% CDs	EXTERIOR MATERIALS	9/15/2025	12/15/2025	1/7/2026				
A6.20	09.15.2025 60% CDs	BUILDING SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A7.20	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A7.21	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A7.22	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A7.23	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025	1/7/2026				
A8.20	09.15.2025 60% CDs	DOOR SCHEDULE, TYPES, AND WINDOW TYPES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A8.21	09.15.2025 60% CDs	DOOR AND WINDOW DETAILS	9/15/2025	12/15/2025	1/7/2026				
A8.22	09.15.2025 60% CDs	DOOR AND WINDOW DETAILS	9/15/2025	12/15/2025	1/7/2026				
A9.20	09.15.2025 60% CDs	CASEWORK DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A9.30	09.15.2025 60% CDs	MISC. DETAILS	9/15/2025	12/15/2025	1/7/2026				
A9.30	01.07.2026 Build PS	MISC. DETAILS			1/7/2026				
		Structural Drawings							
SG0.20	09.15.2025 60% CDs	COVER SHEET	9/15/2025	12/15/2025	1/7/2026				
SG1.21	09.15.2025 60% CDs	GENERAL NOTES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
SG1.22	09.15.2025 60% CDs	GENERAL NOTES	9/15/2025	12/15/2025	1/7/2026				

RFP 607319-24
EXHIBIT D - TECHNICAL SPECIFICATIONS AND DRAWINGS

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company
2/19/2026

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
SG1.23	09.15.2025 60% CDs	GENERAL NOTES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S1.20	09.15.2025 60% CDs	FIRE STATION FOUNDATION PLAN	9/15/2025	12/15/2025	1/7/2026				
S4.20	09.15.2025 60% CDs	FIRE STATION ROOF FRAMING PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S4.21	09.15.2025 60% CDs	FIRE STATION HIGH ROOF FRAMING PLAN	9/15/2025	12/15/2025	1/7/2026				
S8.01	01.07.2026 Build PS	TRASH ENCLOSURE PLAN			1/7/2026				
S9.20	09.15.2025 60% CDs	FOUNDATION SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.21	09.15.2025 60% CDs	FOUNDATION SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S9.23	09.15.2025 60% CDs	CONCRETE SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
S9.24	09.15.2025 60% CDs	MASONRY SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S9.25	09.15.2025 60% CDs	MASONRY SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
S9.27	09.15.2025 60% CDs	FRAMING SECTION AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
		Food Service Drawings							
FS1.20	09.15.2025 60% CDs	FOOD SERVICE EQUIPMENT FLOOR PLAN	9/15/2025	12/15/2025	1/7/2026				
FS2.20	09.15.2025 60% CDs	FOOD SERVICE EQUIPMENT SCHEDULE	9/15/2025	12/15/2025	1/7/2026				
FS3.20	09.15.2025 60% CDs	FOOD SERVICE ELECTRICAL PLAN	9/15/2025	12/15/2025	1/7/2026				
FS1.20	09.15.2025 60% CDs	FOOD SERVICE PLUMBING PLAN	9/15/2025	12/15/2025	1/7/2026				
FS4.20.1	09.15.2025 60% CDs	FOOD SERVICE PLUMBING FLOOR SINK & FLOOR DRAIN PLAN	9/15/2025	12/15/2025	1/7/2026				
FS5.20	09.15.2025 60% CDs	FOOD SERVICE REFRIGERATION PLAN	9/15/2025	12/15/2025	1/7/2026				
FS6.20	09.15.2025 60% CDs	FOOD SERVICE BUILDING CONDITIONS PLAN	9/15/2025	12/15/2025	1/7/2026				
FS7.20	12.15.2025 95% CDs	FOOD SERVICE ELEVATION PLAN		12/15/2025	1/7/2026				
FS8.20	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWINGS	9/15/2025	12/15/2025	1/7/2026				
FS8.20.1	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWINGS	9/15/2025	12/15/2025	1/7/2026				
FS8.20.2	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWINGS	9/15/2025	12/15/2025	1/7/2026				
FS8.20.3	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWINGS	9/15/2025	12/15/2025	1/7/2026				
FS8.20.4	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWINGS	9/15/2025	12/15/2025	1/7/2026				
FS8.20.5	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWINGS	9/15/2025	12/15/2025	1/7/2026				
FS8.20.6	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWINGS	9/15/2025	12/15/2025	1/7/2026				
FS8.20.7	09.15.2025 60% CDs	FOOD SERVICE EXHAUST HOOD SHOP DRAWINGS	9/15/2025	12/15/2025	1/7/2026				
		Mechanical Drawings							
M0.20	09.15.2025 60% CDs	MECHANICAL LEGEND, NOTES AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
M1.21	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026				
M1.22	09.15.2025 60% CDs	MECHANICAL DUCTWORK PLAN - ROOF	9/15/2025	12/15/2025	1/7/2026				
M1.23	12.15.2025 95% CDs	MECHANICAL PIPING PLAN - LEVEL 1		12/15/2025	1/7/2026				
M3.20	09.15.2025 60% CDs	MECHANICAL HVAC ISOMETRIC	9/15/2025	12/15/2025	1/7/2026				
M5.21	09.15.2025 60% CDs	MECHANICAL DIAGRAMS	9/15/2025	12/15/2025	1/7/2026				
M5.22	12.15.2025 95% CDs	MECHANICAL DIAGRAMS		12/15/2025	1/7/2026				
M5.23	12.15.2025 95% CDs	MECHANICAL DIAGRAMS		12/15/2025	1/7/2026				
M5.24	12.15.2025 95% CDs	MECHANICAL DIAGRAMS		12/15/2025	1/7/2026				
M5.25	12.15.2025 95% CDs	MECHANICAL DIAGRAMS		12/15/2025	1/7/2026				
M5.26	12.15.2025 95% CDs	MECHANICAL DIAGRAMS		12/15/2025	1/7/2026				
M6.20	09.15.2025 60% CDs	MECHANICAL SCHEDULES		12/15/2025	1/7/2026				
M6.21	09.15.2025 60% CDs	MECHANICAL VENTILATION CALCS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
		Plumbing Site Drawings	9/15/2025	12/15/2025	1/7/2026				
P0.00	09.15.2025 60% CDs	PLUMBING GENERAL NOTES, AND LEGENDS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
P0.01	09.15.2025 60% CDs	PLUMBING SPECIFICATIONS	9/15/2025	12/15/2025	1/7/2026				
PS1.00	09.15.2025 60% CDs	PLUMBING SITE PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
		Plumbing Drawings							
P0.20	09.15.2025 60% CDs	PLUMBING GENERAL NOTES, AND LEGENDS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P2.21	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P2.22	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - ROOF	9/15/2025	12/15/2025	1/7/2026				
P3.21	09.15.2025 60% CDs	PLUMBING WATER AND GAS PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P3.22	09.15.2025 60% CDs	PLUMBING WATER AND GAS PLAN - ROOF	9/15/2025	12/15/2025	1/7/2026				
P4.21	09.15.2025 60% CDs	PLUMBING ENLARGED FLOOR PLANS	9/15/2025	12/15/2025	1/7/2026				
P4.22	09.15.2025 60% CDs	PLUMBING ENLARGED FLOOR PLANS	9/15/2025	12/15/2025	1/7/2026				
P5.20	09.15.2025 60% CDs	PLUMBING DIAGRAMS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P6.20	09.15.2025 60% CDs	PLUMBING SCHEDULES	9/15/2025	12/15/2025	1/7/2026				
P6.50	12.15.2025 95% CDs	PLUMBING CALCULATIONS		12/15/2025	1/7/2026				
P7.20	09.15.2025 60% CDs	PLUMBING RISER DIAGRAMS - WASTE	9/15/2025	12/15/2025	1/7/2026				
P7.21	09.15.2025 60% CDs	PLUMBING RISER DIAGRAM - WATER	9/15/2025	12/15/2025	1/7/2026				
P7.22	09.15.2025 60% CDs	PLUMBING RISER DIAGRAM - GAS	9/15/2025	12/15/2025	1/7/2026				
		Electrical Site Drawings							
ES0.00	09.15.2025 60% CDs	ELECTRICAL LEGEND, NOTES, AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES0.01	09.15.2025 60% CDs	IECC, LIGHT FIXTURE SCHEDULE, AND ELECTRICAL DIAGRAMS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES1.00	09.15.2025 60% CDs	ELECTRICAL SITE PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES1.00P	09.15.2025 60% CDs	ELECTRICAL SITE PHOTOMETRIC	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES1.00PE	12.15.2025 95% CDs	ELECTRICAL SITE PHOTOMETRIC - EMERGENCY		12/15/2025	1/7/2026	2/6/2026			
ES1.10	09.15.2025 60% CDs	ELECTRICAL ENLARGED SITE PLAN - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES1.11	09.15.2025 60% CDs	ELECTRICAL ENLARGED SITE PLAN - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			

RFP 607319-24
EXHIBIT D - TECHNICAL SPECIFICATIONS AND DRAWINGS

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company
2/20/2026

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
ES1.12	09.15.2025 60% CDs	ELECTRICAL ENLARGED SITE PLAN - AREA C	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES6.00	09.15.2025 60% CDs	SINGLE LINE DIAGRAM & SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
ES6.00	12.15.2025 95% CDs	ELECTRICAL SITE SCHEDULES		12/15/2025	1/7/2026	2/6/2026			
		Electrical Drawings							
E0.20	09.15.2025 60% CDs	ELECTRICAL LEGEND, NOTES, AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E0.21	09.15.2025 60% CDs	IECC AND LIGHT FIXTURE SCHEDULE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E1.20	09.15.2025 60% CDs	POWER PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E3.20	09.15.2025 60% CDs	LIGHTING PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E4.20	09.15.2025 60% CDs	POWER PLAN - ROOF	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E5.20	09.15.2025 60% CDs	SINGLE LINE DIAGRAM & SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E9.20	09.15.2025 60% CDs	ELECTRICAL DIAGRAMS	9/15/2025	12/15/2025	1/7/2026				
E9.21	09.15.2025 60% CDs	ELECTRICAL DIAGRAMS	9/15/2025	12/15/2025	1/7/2026				
E9.22	12.15.2025 95% CDs	LOCATION EQUIPMENT LAYOUT		12/15/2025	1/7/2026				
		Telecom Drawings							
T001	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE LEGENDS AND NOTES	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T002	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE LEGENDS AND LEGEND NOTES	9/15/2025	12/15/2025	1/7/2026				
T120	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL ONE	9/15/2025	12/15/2025	1/7/2026				
T320	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL ONE	9/15/2025	12/15/2025	1/7/2026				
T420	09.15.2025 60% CDs	TELECOM PLAN LEVEL ONE	9/15/2025	12/15/2025	1/7/2026				
T501	09.15.2025 60% CDs	TELECOM ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
T601	09.15.2025 60% CDs	AUDIOVISUAL INFRASTRUCTURE ROOM RISERS	9/15/2025	12/15/2025	1/7/2026				
T652	09.15.2025 60% CDs	TYPICAL TELECOM RISER	9/15/2025	12/15/2025	1/7/2026				
T701	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
TS01	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE DETAILS	9/15/2025	12/15/2025	1/7/2026				
		Fire Alarm Drawings							
FA0.10	09.15.2025 60% CDs	FIRE ALARM GENERAL NOTES, ABBREVIATIONS AND LEGENDS	9/15/2025	12/15/2025	1/7/2026				
FA1.01	09.15.2025 60% CDs	FIRE ALARM OVERALL FLOORPLAN	9/15/2025	12/15/2025	1/7/2026				
		Security Drawings							
Y001	09.15.2025 60% CDs	SECURITY SYMBOLS LEGEND, NOTES, AND SCHEDULES	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y120	09.15.2025 60% CDs	SECURITY PLAN LEVEL ONE	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
YS01	09.15.2025 60% CDs	SECURITY DETAILS	9/15/2025	12/15/2025	1/7/2026				
		MAINTENANCE BUILDING							
		DRAWINGS							
		General							
G0.00	09.15.2025 60% CDs	COVER SHEET	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
G0.03	09.15.2025 60% CDs	GENERAL INFORMATION/CODE ANALYSIS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
G0.30	09.15.2025 60% CDs	TYPICAL ACCESSIBILITY DETAILS	9/15/2025	12/15/2025	1/7/2026				
G1.10	09.15.2025 60% CDs	LIFE SAFETY PLAN - MAINTENANCE BUILDING	9/15/2025	12/15/2025	1/7/2026				
G1.31	12.15.2025 95% CDs	IECC ENVELOPE COMPLIANCE		12/15/2025	1/7/2026				
		Civil Drawings							
C1.01	09.15.2025 60% CDs	COVER SHEET	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C1.02	09.15.2025 60% CDs	GENERAL NOTES SHEET	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C1.03	09.15.2025 60% CDs	PROJECT DATA	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.01	09.15.2025 60% CDs	DEMOLITION PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C2.02	09.15.2025 60% CDs	DEMOLITION PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.03	09.15.2025 60% CDs	DEMOLITION PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.04	09.15.2025 60% CDs	DEMOLITION PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C2.05	09.15.2025 60% CDs	DEMOLITION PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C3.01	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.02	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.03	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.04	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C3.05	09.15.2025 60% CDs	HORIZONTAL CONTROL PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C4.01	09.15.2025 60% CDs	TRAFFIC SIGNAL PLAN AT TROPICANA AND ARVILLE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C4.02	09.15.2025 60% CDs	TRAFFIC SIGNAL SCHEDULE AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C4.03	09.15.2025 60% CDs	EMERGENCY SIGNAL PLAN SCHEDULE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C4.04	09.15.2025 60% CDs	GENERAL TRAFFIC NOTES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C5.01	09.15.2025 60% CDs	MASTER GRADING PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C5.02	09.15.2025 60% CDs	GRADING PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.03	09.15.2025 60% CDs	GRADING PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.04	09.15.2025 60% CDs	GRADING PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.05	09.15.2025 60% CDs	GRADING PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C5.06	09.15.2025 60% CDs	GRADING PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.01	09.15.2025 60% CDs	TROPICANA AVE & PROFILE	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.02	12.15.2025 95% CDs	TROPICANA AVE - UTILITY PLAN AND PROFILE		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.03	12.15.2025 95% CDs	ARVILLE ST - UTILITY PLAN AND PROFILE 1		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.04	12.15.2025 95% CDs	ARVILLE ST - UTILITY PLAN AND PROFILE 2		12/15/2025	1/7/2026	2/6/2026	2/19/2026		

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company
2/20/26

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
C6.05	12.15.2025 95% CDs	ARVILLE ST - UTILITY PLAN AND PROFILE 3		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C6.06	01.07.2026 Build PS	SEWER LATERAL PLAN AND PROFILES			1/7/2026	2/6/2026	2/19/2026		
C7.01	09.15.2025 60% CDs	MASTER UTILITY SHEET	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.02	09.15.2025 60% CDs	UTILITY PLAN 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.03	09.15.2025 60% CDs	UTILITY PLAN 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.04	09.15.2025 60% CDs	UTILITY PLAN 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.05	09.15.2025 60% CDs	UTILITY PLAN 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C7.06	09.15.2025 60% CDs	UTILITY PLAN 5	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C8.01	09.15.2025 60% CDs	GENERAL STRUCTURAL NOTES & TYPICAL DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C8.02	09.15.2025 60% CDs	JUCTION STRUCTURES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C8.03	09.15.2025 60% CDs	RETAINING WALL	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C9.01	09.15.2025 60% CDs	DETAIL SHEET 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C9.02	09.15.2025 60% CDs	DETAIL SHEET 2	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
C9.03	09.15.2025 60% CDs	DETAIL SHEET 3	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
C9.04	12.15.2025 95% CDs	DETAIL SHEET 4	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
				12/15/2025	1/7/2026				
		Landscape Drawings							
L1.01	09.15.2025 60% CDs	OVERALL LANDSCAPE PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L1.02	09.15.2025 60% CDs	LANDSCAPE PLAN ENLARGEMENT "A"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L1.03	09.15.2025 60% CDs	LANDSCAPE PLAN ENLARGEMENT "B"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L1.04	12.15.2025 95% CDs	LEVEL 3 PLAZA PLANTING PLAN		12/15/2025	1/7/2026				
L2.01	09.15.2025 60% CDs	OVERALL IRRIGATION PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L2.02	09.15.2025 60% CDs	IRRIGATION PLAN ENLARGEMENT "A"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L2.03	09.15.2025 60% CDs	IRRIGATION PLAN ENLARGEMENT "B"	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
L3.01	09.15.2025 60% CDs	PROJECT DETAILS	9/15/2025	12/15/2025	1/7/2026				
L3.02	12.15.2025 95% CDs	PROJECT DETAILS		12/15/2025	1/7/2026				
		Architectural Site Drawings							
AS1.01	09.15.2025 60% CDs	OVERALL ARCHITECTURAL SITE PLAN	9/15/2025	12/15/2025	1/7/2026				
AS1.10	09.15.2025 60% CDs	ENLARGED ARCHITECTURAL SITE PLAN - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.11	09.15.2025 60% CDs	ENLARGED ARCHITECTURAL SITE PLAN - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.12	09.15.2025 60% CDs	ENLARGED ARCHITECTURAL SITE PLAN - AREA C	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.20	09.15.2025 60% CDs	ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS1.21	09.15.2025 60% CDs	ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS3.00	09.15.2025 60% CDs	SITE GATE SCHEDULE AND DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
AS3.10	09.15.2025 60% CDs	ARCHITECTURAL SITE DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
		Architectural Drawings							
A0.10	09.15.2025 60% CDs	PARTITION TYPES	9/15/2025	12/15/2025	1/7/2026				
A1.10	09.15.2025 60% CDs	FLOOR PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A1.11	09.15.2025 60% CDs	SIGNAGE SCHEDULE AND PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A1.50	09.15.2025 60% CDs	FINISH INDEX	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A1.51	09.15.2025 60% CDs	FINISH FLOOR PLAN	9/15/2025	12/15/2025	1/7/2026				
A1.52	09.15.2025 60% CDs	ROOF PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A2.10	09.15.2025 60% CDs	MAINTENANCE BUILDING - ENLARGED PLANS & ELEVATIONS - RESTROOMS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A2.11	09.15.2025 60% CDs	MAINTENANCE BUILDING - ENLARGED PLANS & ELEVATIONS - CASEWORK	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A2.12	12.15.2025 95% CDs	MAINTENANCE BUILDING - ENLARGED PLANS & SECTIONS - SERVICE PIT		12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A3.10	09.15.2025 60% CDs	OVERALL REFLECTED CEILING PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A3.11	12.15.2025 95% CDs	CEILING DETAILS		12/15/2025	1/7/2026				
A4.10	09.15.2025 60% CDs	ROOF PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A5.10	09.15.2025 60% CDs	EXTERIOR ELEVATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A5.11	09.15.2025 60% CDs	EXTERIOR ELEVATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A5.12	09.15.2025 60% CDs	EXTERIOR AXONS	9/15/2025	12/15/2025	1/7/2026				
A5.13	09.15.2025 60% CDs	EXTERIOR RENDERINGS	9/15/2025	12/15/2025	1/7/2026				
A6.10	09.15.2025 60% CDs	BUILDING SECTIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A6.11	09.15.2025 60% CDs	BUILDING SECTIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
A7.10	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
A7.11	09.15.2025 60% CDs	WALL SECTIONS	9/15/2025	12/15/2025		2/6/2026	2/19/2026		
A8.10	09.15.2025 60% CDs	MAINTENANCE BUILDING - DOOR SCHEDULE, TYPES, AND WINDOW TYPES	9/15/2025	12/15/2025	1/7/2026				
A8.11	09.15.2025 60% CDs	MAINTENANCE BUILDING - DOOR AND WINDOW DETAILS	9/15/2025	12/15/2025	1/7/2026				
A8.12	09.15.2025 60% CDs	MAINTENANCE BUILDING - DOOR AND WINDOW DETAILS	9/15/2025	12/15/2025	1/7/2026				
A8.13	12.15.2025 95% CDs	MAINTENANCE BUILDING - DOOR AND WINDOW DETAILS		12/15/2025	1/7/2026				
A9.10	09.15.2025 60% CDs	CASEWORK DETAILS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
A9.11	12.15.2025 95% CDs	MAINTENANCE BUILDING - DETAILS		12/15/2025	1/7/2026				
		Structural Drawings							
SG0.10	09.15.2025 60% CDs	COVER SHEET	9/15/2025	12/15/2025	1/7/2026				
SG1.11	09.15.2025 60% CDs	GENERAL NOTES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
SG1.12	09.15.2025 60% CDs	GENERAL NOTES	9/15/2025	12/15/2025	1/7/2026				
S1.10	09.15.2025 60% CDs	MAINTENANCE BUILDING FOUNDATION PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S9.10	09.15.2025 60% CDs	FOUNDATION SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
S9.11	09.15.2025 60% CDs	FOUNDATION SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company
2/19/2026

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
S0.14	09.15.2025 60% CDs	CONCRETE SECTIONS AND DETAILS	9/15/2025	12/15/2025	1/7/2026				
		Food Service Drawings							
FS1.10	09.15.2025 60% CDs	FOOD SERVICE EQUIPMENT FLOOR PLAN	9/15/2025	12/15/2025	1/7/2026				
FS2.10	09.15.2025 60% CDs	FOOD SERVICE EQUIPMENT SCHEDULE	9/15/2025	12/15/2025	1/7/2026				
FS3.10	09.15.2025 60% CDs	FOOD SERVICE ELECTRICAL PLAN	9/15/2025	12/15/2025	1/7/2026				
FS4.10	09.15.2025 60% CDs	FOOD SERVICE PLUMBING PLAN	9/15/2025	12/15/2025	1/7/2026				
FS4.10.1	09.15.2025 60% CDs	FOOD SERVICE PLUMBING FLOOR SINK & FLOOR DRAIN PLAN	9/15/2025	12/15/2025	1/7/2026				
FS6.10	09.15.2025 60% CDs	FOOD SERVICE BUILDING CONDITIONS PLAN	9/15/2025	12/15/2025	1/7/2026				
FS7.10	12.15.2025 95% CDs	FOOD SERVICE ELEVATION PLAN		12/15/2025	1/7/2026				
		Mechanical Drawings							
M0.10	09.15.2025 60% CDs	MECHANICAL LEGEND, NOTES AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M2.10	09.15.2025 60% CDs	MECHANICAL DUCTWORK OVERALL PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
M4.10	09.15.2025 60% CDs	MECHANICAL DUCTWORK OVERALL PLAN - ROOF	9/15/2025	12/15/2025	1/7/2026				
M5.10	09.15.2025 60% CDs	MECHANICAL DETAILS	9/15/2025	12/15/2025	1/7/2026				
M5.11	09.15.2025 60% CDs	MECHANICAL DETAILS	9/15/2025	12/15/2025	1/7/2026				
M6.10	09.15.2025 60% CDs	MECHANICAL SCHEDULES	9/15/2025	12/15/2025	1/7/2026				
M7.10	01.07.2026 Build PS	MECHANICAL 3D VIEWS			1/7/2026				
		Plumbing Site Drawings							
P0.00	09.15.2025 60% CDs	PLUMBING GENERAL NOTES, AND LEGENDS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
P0.01	09.15.2025 60% CDs	PLUMBING SPECIFICATIONS	9/15/2025	12/15/2025	1/7/2026				
PS1.00	09.15.2025 60% CDs	PLUMBING SITE PLAN	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
		Plumbing Drawings							
P0.10	09.15.2025 60% CDs	PLUMBING GENERAL NOTES, AND LEGENDS	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
P0.11	09.15.2025 60% CDs	PLUMBING SPECIFICATIONS	9/15/2025	12/15/2025	1/7/2026				
P1.10	09.15.2025 60% CDs	PLUMBING OVERALL PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
P2.10	09.15.2025 60% CDs	PLUMBING WASTE AND VENT OVERALL PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
P2.10A	09.15.2025 60% CDs	PLUMBING WASTE AND VENT PLAN - LEVEL 1 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
P3.11.1	09.15.2025 60% CDs	PLUMBING WATER SYSTEMS PLAN - LEVEL 1 - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
P4.10A	09.15.2025 60% CDs	PLUMBING WASTE AND VENT ROOF PLAN - AREA A	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
P4.11.1	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - LEVEL 1 - AREA	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P4.12.1	09.15.2025 60% CDs	PLUMBING GAS SYSTEMS PLAN - ROOF AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
P5.10	09.15.2025 60% CDs	PLUMBING DIAGRAMS - WASTE	9/15/2025	12/15/2025	1/7/2026				
P5.11	09.15.2025 60% CDs	PLUMBING DIAGRAMS - WATER	9/15/2025	12/15/2025	1/7/2026				
P6.10	09.15.2025 60% CDs	PLUMBING SCHEDULES	9/15/2025	12/15/2025	1/7/2026				
P6.50	12.15.2025 95% CDs	PLUMBING CALCULATIONS		12/15/2025	1/7/2026				
P7.10	09.15.2025 60% CDs	PLUMBING RISER SCHEMATIC - WASTE	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
P7.11	09.15.2025 60% CDs	PLUMBING RISER SCHEMATIC - WATER	9/15/2025	12/15/2025	1/7/2026	2/6/2026	2/19/2026		
P7.12	09.15.2025 60% CDs	PLUMBING RISER SCHEMATIC - GAS	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
P8.00	09.15.2025 60% CDs	ENLARGED FLOOR PLANS - WASTE & VENT	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
P9.00	09.15.2025 60% CDs	ENLARGED FLOOR PLANS - WATER	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
		Electrical Drawings							
E0.00	09.15.2025 60% CDs	ELECTRICAL LEGEND, NOTES AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E0.01	09.15.2025 60% CDs	IECC, LIGHT FIXTURE SCHEDULE, AND ELECTRICAL DIAGRAMS	9/15/2025	12/15/2025	1/7/2026	2/5/2026			
E1.00	09.15.2025 60% CDs	ELECTRICAL SITE PLAN	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E1.00P	09.15.2025 60% CDs	ELECTRICAL SITE PHOTOMETRIC	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E1.00PE	12.15.2025 95% CDs	ELECTRICAL SITE PHOTOMETRIC - EMERGENCY		12/15/2025	1/7/2026	2/6/2026			
E1.10	09.15.2025 60% CDs	ELECTRICAL ENLARGED SITE PLAN - AREA A	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E1.11	09.15.2025 60% CDs	ELECTRICAL ENLARGED SITE PLAN - AREA B	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E1.12	09.15.2025 60% CDs	ELECTRICAL ENLARGED SITE PLAN - AREA C	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E5.00	09.15.2025 60% CDs	SINGLE LINE DIAGRAM & SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E6.00	12.15.2025 95% CDs	ELECTRICAL SITE SCHEDULES		12/15/2025	1/7/2026	2/6/2026			
E0.10	09.15.2025 60% CDs	ELECTRICAL LEGEND, NOTES AND ABBREVIATIONS	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E0.11	09.15.2025 60% CDs	IECC AND LIGHT FIXTURE SCHEDULE	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E1.10	09.15.2025 60% CDs	POWER PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E3.10	09.15.2025 60% CDs	LIGHTING PLAN - LEVEL 1	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E4.10	09.15.2025 60% CDs	ELECTRICAL PLAN - ROOF	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
E5.10	09.15.2025 60% CDs	SINGLE LINE DIAGRAM & SCHEDULES	9/15/2025	12/15/2025	1/7/2026	2/6/2026			
		Telecom Drawings							
T002	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE LEGENDS AND NOTES	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T002	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE LEGENDS AND LEGEND NOTES	9/15/2025	12/15/2025	1/7/2026				
T101	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN LEVEL ONE	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T102	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE PLAN ROOF	9/15/2025	12/15/2025	1/7/2026				
T301	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE REFLECTED CEILING PLAN LEVEL ONE	9/15/2025	12/15/2025	1/7/2026				
T401	09.15.2025 60% CDs	TELECOM PLAN LEVEL ONE	9/15/2025	12/15/2025	1/7/2026				
T402	09.15.2025 60% CDs	TELECOM PLAN ROOF	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T501	09.15.2025 60% CDs	TELECOM ENLARGED PLANS AND ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
T601	09.15.2025 60% CDs	AUDIOVISUAL TYPICAL RISER	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
T652	09.15.2025 60% CDs	TYPICAL TELECOM RISER	9/15/2025	12/15/2025	1/7/2026				

WHITING-TURNER

Clark County Fire Training Center

Document Log - Clark County Fire Training Center
The Whiting-Turner Contracting Company
2/12/26

Item #	Design Issue	Title	9/15/2025 09.15.2025 60% Construction Drawings	12/15/2025 12.15.2025 95% Construction Drawings	1/7/2026 01.07.2026 Building Permit Set	2/6/2026 02.06.2026 Addendum A Bid Set	2/19/2026 02.20.2026 Addendum B Issuance	Current Date	Notes
T701	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE ELEVATIONS	9/15/2025	12/15/2025	1/7/2026				
T801	09.15.2025 60% CDs	TECHNOLOGY INFRASTRUCTURE DETAILS	9/15/2025	12/15/2025	1/7/2026				
		Fire Alarm Drawings							
FA0.10	09.15.2025 60% CDs	FIRE ALARM GENERAL NOTES, ABBREVIATIONS AND LEGEND	9/15/2025	12/15/2025	1/7/2026				
FA2.01	09.15.2025 60% CDs	FIRE ALARM OVERALL FLOOR PLAN	9/15/2025	12/15/2025	1/7/2026				
		Security Drawings							
Y001	09.15.2025 60% CDs	SECURITY SYMBOLS LEGEND, NOTES, AND SCHEDULES	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y101	09.15.2025 60% CDs	SECURITY PLAN LEVEL ONE	9/15/2025	12/15/2025	1/7/2026		2/19/2026		
Y102	09.15.2025 60% CDs	SECURITY PLAN ROOF	9/15/2025	12/15/2025	1/7/2026				
Y801	12.15.2025 95% CDs			12/15/2025	1/7/2026				

EXHIBIT E
Whiting-Turner Key Personnel

WHITING-TURNER

CONSTRUCTION SERVICES PERSONNEL (INCLUDES KEY PERSONNEL)

Name	Job Title
Joe Swanson	Project Executive
Mark Latimer	Lead Superintendent
Ruben Cueva	Lead Project Manager
Hunter Hayden	Assistant Project Manager
JT Hoppins	Scheduler
Miguel Oliva	VDC Engineer
Josh Dickson	MEP Manager
Zac Crane	Executive Leadership
Daniel Davis	Quality Manager
Ruby Carrillo	EH&S Manager

EXHIBIT F
NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE
GEOTECHNICAL AND ENVIRONMENTAL REPORTS

Left intentionally blank

FINAL LAB REPORT

FC30428

C2281

28-Jan-2026

Prepared by

SGS NORTH AMERICA

Prepared for

SGS North America Inc. - Orlando

Andrea Colby

4405 Vineland Road, Suite C-15
Orlando, FL 32811
Phone: 407-425-6700
Email: andrea.colby@sgs.com

This report is approved by

Amy.Boehm
I have reviewed this document
Wilmington, NC
2026.01.28 09:07:47-05'00'

Amy Boehm

amy.boehm@sgs.com

Senior Project Manager

This document is issued by the Company under its General Conditions of Service accessible at http://www.sgs.com/en/terms_and_conditions.htm. Attention is drawn to the limitation of liability, indemnification and jurisdiction issues defined therein.

SGS remains committed to serving you in the most effective manner. Should you have any questions or need additional information and technical support, please do not hesitate to contact us.

The management and staff of SGS welcomes customer feedback, both positive and negative, as we continually improve our services. Please visit our web site at www.sgs.com/ultratrace and click on the 'Email Us' link or go to our survey. Your feedback helps us improve our service and takes less than a minute to complete. Thank you for choosing SGS.

Any holder of this document is advised that it is a final submission and supersedes and voids all prior reports with the same report or identification number. The information contained hereon reflects the Company's findings at the time of its intervention only and within the limits of Client's instructions, if any. The Company's sole responsibility in conducting the work herein is to its Client and does not exonerate parties to a transaction from exercising all of their rights and obligations under such applicable transaction documents. This report may be reproduced in full only. The Company expressly disclaims any and all liability for the Client's use of or reliance upon the data contained herein. Any alteration, forgery or falsification of the content or appearance of this document which is not expressly authorized by the Company is unlawful and offenders may be prosecuted to the fullest extent of the law. Results reported relate only to the items tested.

SGS

PROJECT INFORMATION SUMMARY *(When applicable, see QC Annotations for details)*

Client Project	FC30428
SGS Project #	C2281
Analytical Protocol(s)	8290A
No. Samples Submitted	1
Additional QC Sample(s)	0
No. Laboratory Method Blanks	1
No. OPRs / Batch CS3	1
Date Received	31-Dec-25
Condition Received	Good
Temperature upon Receipt (°C)	0.8
Extraction within Holding Time	Yes
Analysis within Holding Time	Yes

SGS

QC ANNOTATIONS:

1. Please see Appendices attached for data qualifier/attribute and lab identifier descriptions which may be contained in the project.

APPENDIX A: GENERAL DATA QUALIFIERS / DATA ATTRIBUTES

B	The analyte was found in the method blank, at a concentration that was at least 10% of the concentration in the sample.
C	Two or more congeners co-elute. In EDDs, C denotes the lowest IUPAC congener in a co-elution group and additional co-eluters for the group are shown with the number of the lowest IUPAC co-eluter.
E	The reported concentration exceeds the calibration range (upper point of the calibration curve) and is an estimated value.
EMPC	Represents an Estimated Maximum Possible Concentration. EMPCs arise in cases where the signal/noise ratio is not sufficient for peak identification (the determined ion-abundance ratio is outside the allowed theoretical range), or where there is a co-eluting interference.
H/h	If the standard recovery is below the method or SOP specified value "H" is assigned. If the obtained value is less than half the specified value "h" is assigned.
J	Indicates that an analyte has a concentration below the reporting limit (lowest point of the calibration curve) and is an estimated value.
ND	Indicates a non-detect.
NR or R	Indicates a value that is not reportable.
PR	Due to interference, the associated congener is poorly resolved.
QI	Indicates the presence of a quantitative interference.
SI	Denotes "Single Ion Mode" and is utilized for PCBs where the secondary ion trace has a significantly elevated noise level due to background PFK. Responses for such peaks are calculated using an EMPC approach based solely on the primary ion area(s) and may be considered estimates.
U	The analyte was not detected. The estimated detection limit (EDL) may be reported for this analyte.
V	The labeled standard recovery was found to be outside of the method control limits.

APPENDIX B: DRBC/TMDL SPECIFIC DATA QUALIFIERS / DATA ATTRIBUTES

J	The reported result is an estimate. The value is less than the minimum calibration level but greater than the estimated detection limit (EDL).
U	The analyte was not detected in the sample at the estimated detection limit (EDL).
E	The reported concentration is an estimate. The value exceeds the upper calibration range (upper point of the calibration curve).
D	Dilution Data. Result was obtained from the analysis of a dilution.
B	Analyte found in the sample and associated method blank.
C	Co-eluting congener
Cxx	Co-elutes with the indicated congener, data is reported under the lowest IUPAC congener. 'Xx' denotes the IUPAC number with the lowest numerical designated congener.
NR	Analyte is not reportable because of problems in sample preparation or analysis.
V	Labeled standard recovery is not within method control limits.
X	Results from re-injection/repeat/second-column analysis.
EMPC	Estimated maximum possible concentration. Indicates that a peak is identified but did not meet the method specified ion-abundance ratio.

APPENDIX C: LAB IDENTIFIERS

AR	Indicates use of the archived portion of the sample extract.
CU	Indicates a sample that required additional clean-up prior to MS injection/processing.
D	Indicates a dilution of the sample extract. The number that follows the "D" indicates the dilution factor.
DE	Indicates a dilution performed with the addition of ES (extraction standard) solution.
DUP	Designation for a duplicate sample.
MS	Designation for a matrix spike.
MSD	Designation for a matrix spike duplicate.
RJ	Indicates a reinjection of the sample extract.
S	Indicates a sample split. The number that follows the "S" indicates the split factor.

SGS CERTIFICATIONS / APPROVALS / PERMITS

Alaska DEC LAP	17-012
Alaska DEC LCP	NC00919
Arkansas	88-0682
California (ELAP)	ELAP Cert #2914
CLIA	34D1013708
Colorado	NC00919
Connecticut	PH-0258
USDA Soil Permit	P330-20-00103
American Association for Laboratory Accreditation (A2LA)	2726.01 (ISO 17025:2017, 2009 TNI, DoD ELAP QSM 5.4)
Florida DOH	E87634
Hawaii DOH	Approval
Louisiana DEQ	4115
Louisiana DOH	LA031
Maine	2020020
Massachusetts	M-NC919
Michigan	9950
Minnesota (Primary NELAP For Method 23)	037-999-459
Montana	0106
New Hampshire (Secondary NELAP)	2083
New Jersey	NC100
New York	11685
North Carolina DEQ	481
Ohio	87785
Oklahoma	2205
Oregon	NC200002
Pennsylvania	68-03675
South Carolina	99029002
Texas	T104704260
UCMR 5	NC00919
US Coast Guard	16714/159.317/SGS
U.S. Fish and Wildlife Service	A22801
Vermont	VT-87634
Virginia	460214
Washington	C913

Sample ID: W-01

Method 8290A

Client Data		Sample Data		Laboratory Data			
Name:	SGS North America Inc. - Orlando	Matrix:	Solid	Lab Project ID:	C2281	Date Received:	31-Dec-2025
Project ID:	FC30428	Weight/Volume:	100.00 cm2	Lab Sample ID	C2281_22743_DF_001	Date Extracted:	07-Jan-2026
Date Collected:	30-Dec-2025	% Solid:	n/a	QC Batch No:	22743	Date Analyzed:	22-Jan-2026
		Split:	-	Dilution:	-	Time Analyzed:	18:37:29

Analyte	Conc. (pg/cm2)	DL (pg/cm2)	EMPC (pg/cm2)	Qualifiers
2378-TCDD	ND	0.0209		
12378-PeCDD	ND	0.0261		
123478-HxCDD	0.0354			J B
123678-HxCDD	0.0283			J
123789-HxCDD	EMPC		0.0212	J
1234678-HpCDD	0.214			J
OCDD	1.14			
2378-TCDF	EMPC		0.0407	J
12378-PeCDF	0.0268			J
23478-PeCDF	EMPC		0.0313	J
123478-HxCDF	EMPC		0.0205	J
123678-HxCDF	EMPC		0.0186	J
234678-HxCDF	0.0191			J
123789-HxCDF	ND	0.0119		
1234678-HpCDF	ND	0.0491		
1234789-HpCDF	ND	0.0678		
OCDF	ND	0.0216		
Totals				
Total TCDD	ND	0.0209	ND	
Total PeCDD	ND	0.0261	ND	
Total HxCDD	0.15		0.212	
Total HpCDD	0.434		0.434	
Total TCDF	0.686		0.956	
Total PeCDF	0.109		0.251	
Total HxCDF	0.0656		0.105	
Total HpCDF	ND	0.057	ND	
Total PCDD/Fs	**2.58**		**3.09**	
ITEF TEQs				
TEQ: ND=0	0.0129		0.0387	
TEQ: ND=DL/2	0.0311	0.0277	0.0568	
TEQ: ND=DL	0.0492	0.0554	0.075	

Standard	ES Recoveries	Qualifiers
ES 2378-TCDD	90.3	
ES 12378-PeCDD	103	
ES 123478-HxCDD	81.4	
ES 123678-HxCDD	78.9	
ES 123789-HxCDD	82.7	
ES 1234678-HpCDD	89.6	
ES OCDD	66.8	
ES 2378-TCDF	84.2	
ES 12378-PeCDF	103	
ES 23478-PeCDF	96.9	
ES 123478-HxCDF	69.1	
ES 123678-HxCDF	71	
ES 234678-HxCDF	68.8	
ES 123789-HxCDF	74	
ES 1234678-HpCDF	84.4	
ES 1234789-HpCDF	73.3	
ES OCDF	60.3	

Standard	CS Recoveries
CS 37Cl-2378-TCDD	91.1
CS 12347-PeCDD	101
CS 12346-PeCDF	86.8
CS 123469-HxCDF	69.4
CS 1234689-HpCDF	79.7

SGS
5500 Business Drive
Wilmington, NC 28405. USA
www.us.sgs.com
Tel: +1 910 794-1613: Toll-Free 866 846-8290

Sample ID: W-01

TEQ Summary

Method 8290A

Client Project Name:	SGS North America Inc. - Orlando	Matrix:	Solid	Lab Sample ID:	C2281_22743_DF_001
Client Project ID:	FC30428	Weight/Volume:	100.00 cm2	QC Batch No.:	22743
Date Collected:	30-Dec-2025	Split:	-	Date Extracted:	07-Jan-2026
Date Received:	31-Dec-2025	Dilution:	-	Date Analyzed:	22-Jan-2026 18:37
Lab Project No:	C2281	Units	cm2/wipe		

Analyte	Result	Qualifiers	DLs	I-TEQ	WHO-1998	WHO-2005
2378-TCDD	(0.0209)		0.0209	(0.0209)	(0.0209)	(0.0209)
12378-PeCDD	(0.0261)		0.0261	(0.0131)	(0.0261)	(0.0261)
123478-HxCDD	0.0354	J B	0.0155	0.00354	0.00354	0.00354
123678-HxCDD	0.0283	J	0.0156	0.00283	0.00283	0.00283
123789-HxCDD	[0.0212]	J	0.0158	[0.00212]	[0.00212]	[0.00212]
1234678-HpCDD	0.214	J	0.0193	0.00214	0.00214	0.00214
OCDD	1.14		0.0493	0.00114	0.000114	0.000341
2378-TCDF	[0.0407]	J	0.00902	[0.00407]	[0.00407]	[0.00407]
12378-PeCDF	0.0268	J	0.0172	0.00134	0.00134	0.000804
23478-PeCDF	[0.0313]	J	0.0181	[0.0157]	[0.0157]	[0.0094]
123478-HxCDF	[0.0205]	J	0.0114	[0.00205]	[0.00205]	[0.00205]
123678-HxCDF	[0.0186]	J	0.01	[0.00186]	[0.00186]	[0.00186]
234678-HxCDF	0.0191	J	0.0116	0.00191	0.00191	0.00191
123789-HxCDF	(0.0119)		0.0119	(0.00119)	(0.00119)	(0.00119)
1234678-HpCDF	(0.0491)		0.0491	(0.000491)	(0.000491)	(0.000491)
1234789-HpCDF	(0.0678)		0.0678	(0.000678)	(0.000678)	(0.000678)
OCDF	(0.0216)		0.0216	(0.0000216)	(0.00000216)	(0.00000649)

5500 Business Drive
Wilmington, NC 28405, USA
Tel: +1 910 794-1613; Toll-Free 866 846-8290
www.us.sgs.com

TEQ Summaries			
EMPC = 0, ND = 0	0.0129	0.0119	0.0116
EMPC = 0, ND = DL / 2	0.0311	0.0366	0.0362
EMPC = 0, ND = DL	0.0492	0.0612	0.0609
EMPC = 0, < J-level = 0	0.00114	0.000114	0.000341
EMPC = EMPC, ND = 0	0.0387	0.0376	0.0311
EMPC = EMPC, ND = DL / 2	0.0568	0.0623	0.0557
EMPC = EMPC, ND = DL	0.075	0.087	0.0804
EMPC = EMPC, < J-level = 0	0.00114	0.000114	0.000341

Checkcode: 255-836-NQP

SGS North America - DF v0.99

Sample ID: Method Blank C2281_22743

Method 8290A

Client Data		Sample Data		Laboratory Data			
Name:	SGS North America Inc. - Orlando	Matrix:	Solid	Lab Project ID:	C2281	Date Received:	n/a
Project ID:	FC30428	Weight/Volume:	100.00 cm2	Lab Sample ID	MB1_22743_DF_SDS	Date Extracted:	07-Jan-2026
Date Collected:	n/a	% Solid:	n/a	QC Batch No:	22743	Date Analyzed:	22-Jan-2026
		Split:	-	Dilution:	-	Time Analyzed:	17:01:56

Analyte	Conc. (pg/cm2)	DL (pg/cm2)	EMPC (pg/cm2)	Qualifiers
2378-TCDD	ND	0.00988		
12378-PeCDD	ND	0.011		
123478-HxCDD	0.0186			J
123678-HxCDD	ND	0.0125		
123789-HxCDD	ND	0.0117		
1234678-HpCDD	ND	0.0161		
OCDD	ND	0.0376		
2378-TCDF	ND	0.00842		
12378-PeCDF	ND	0.00912		
23478-PeCDF	ND	0.00915		
123478-HxCDF	ND	0.00854		
123678-HxCDF	ND	0.00808		
234678-HxCDF	ND	0.0096		
123789-HxCDF	ND	0.00958		
1234678-HpCDF	ND	0.00699		
1234789-HpCDF	ND	0.00963		
OCDF	ND	0.017		
Totals				
Total TCDD	ND	0.00988	ND	
Total PeCDD	ND	0.011	ND	
Total HxCDD	0.0186		0.0186	
Total HpCDD	ND	0.0161	ND	
Total TCDF	ND	0.00842	ND	
Total PeCDF	ND	0.00913	ND	
Total HxCDF	ND	0.00891	ND	
Total HpCDF	ND	0.00815	ND	
Total PCDD/Fs	**0.0186**		**0.0186**	
ITEF TEQs				
TEQ: ND=0	0.00186		0.00186	
TEQ: ND=DL/2	0.0157	0.0144	0.0157	
TEQ: ND=DL	0.0295	0.0287	0.0295	

Standard	ES Recoveries	Qualifiers
ES 2378-TCDD	91.1	
ES 12378-PeCDD	93.6	
ES 123478-HxCDD	88.5	
ES 123678-HxCDD	86.4	
ES 123789-HxCDD	90	
ES 1234678-HpCDD	101	
ES OCDD	91.8	
ES 2378-TCDF	85	
ES 12378-PeCDF	92.9	
ES 23478-PeCDF	88.5	
ES 123478-HxCDF	72.4	
ES 123678-HxCDF	75.4	
ES 234678-HxCDF	71.4	
ES 123789-HxCDF	79	
ES 1234678-HpCDF	91.8	
ES 1234789-HpCDF	86.8	
ES OCDF	79.5	

Standard	CS Recoveries
CS 37Cl-2378-TCDD	98.9
CS 12347-PeCDD	98.3
CS 12346-PeCDF	88.6
CS 123469-HxCDF	81.4
CS 1234689-HpCDF	92

SGS
5500 Business Drive
Wilmington, NC 28405, USA
www.us.sgs.com
Tel: +1 910 794-1613; Toll-Free 866 846-8290

Sample ID: Method Blank C2281_22743

TEQ Summary

Method 8290A

Client Project Name:	SGS North America Inc. - Orlando	Matrix:	Solid	Lab Sample ID:	MB1_22743_DF_SDS
Client Project ID:	FC30428	Weight/Volume:	100.00 cm2	QC Batch No.:	22743
Date Collected:	n/a	Split:	-	Date Extracted:	07-Jan-2026
Date Received:	n/a	Dilution:	-	Date Analyzed:	22-Jan-2026 17:01
Lab Project No:	C2281	Units	cm2/wipe		

Analyte	Result	Qualifiers	DLs	I-TEQ	WHO-1998	WHO-2005
2378-TCDD	(0.00988)		0.00988	(0.00988)	(0.00988)	(0.00988)
12378-PeCDD	(0.011)		0.011	(0.00548)	(0.011)	(0.011)
123478-HxCDD	0.0186	J	0.0113	0.00186	0.00186	0.00186
123678-HxCDD	(0.0125)		0.0125	(0.00125)	(0.00125)	(0.00125)
123789-HxCDD	(0.0117)		0.0117	(0.00117)	(0.00117)	(0.00117)
1234678-HpCDD	(0.0161)		0.0161	(0.000161)	(0.000161)	(0.000161)
OCDD	(0.0376)		0.0376	(0.0000376)	(0.00000376)	(0.0000113)
2378-TCDF	(0.00842)		0.00842	(0.000842)	(0.000842)	(0.000842)
12378-PeCDF	(0.00912)		0.00912	(0.000456)	(0.000456)	(0.000274)
23478-PeCDF	(0.00915)		0.00915	(0.00457)	(0.00457)	(0.00274)
123478-HxCDF	(0.00854)		0.00854	(0.000854)	(0.000854)	(0.000854)
123678-HxCDF	(0.00808)		0.00808	(0.000808)	(0.000808)	(0.000808)
234678-HxCDF	(0.0096)		0.0096	(0.00096)	(0.00096)	(0.00096)
123789-HxCDF	(0.00958)		0.00958	(0.000958)	(0.000958)	(0.000958)
1234678-HpCDF	(0.00699)		0.00699	(0.0000699)	(0.0000699)	(0.0000699)
1234789-HpCDF	(0.00963)		0.00963	(0.0000963)	(0.0000963)	(0.0000963)
OCDF	(0.017)		0.017	(0.000017)	(0.0000017)	(0.00000509)

5500 Business Drive
Wilmington, NC 28405, USA
Tel: +1 910 794-1613; Toll-Free 866 846-8290
www.us.sgs.com

TEQ Summaries			
EMPC = 0, ND = 0	0.00186	0.00186	0.00186
EMPC = 0, ND = DL / 2	0.0157	0.0184	0.0174
EMPC = 0, ND = DL	0.0295	0.0349	0.0329
EMPC = 0, < J-level = 0	0	0	0
EMPC = EMPC, ND = 0	0.00186	0.00186	0.00186
EMPC = EMPC, ND = DL / 2	0.0157	0.0184	0.0174
EMPC = EMPC, ND = DL	0.0295	0.0349	0.0329
EMPC = EMPC, < J-level = 0	0	0	0

Checkcode: 461-884-WRS

SGS North America - DF v0.99

METHOD 8290A **PCDD/F ONGOING PRECISION AND RECOVERY (OPR)** **FORM 8A**

Lab Name:	SGS North America		
Initial Calibration:	ICAL: MM1_DF_11012024_03JAN2025		
Instrument ID:	MM1	GC Column ID:	ZB-5ms
VER Data Filename:	260122P10	Analysis Date:	22-JAN-2026 14:40:52
Lab ID:	OPR1_22743_DF		

NATIVE ANALYTES	SPIKE CONC.	CONC. FOUND	RANGE (ng/mL)			OK
2,3,7,8-TCDD	10	11.3	6.7	-	15.8	Y
1,2,3,7,8-PeCDD	50	50.3	35	-	71	Y
1,2,3,4,7,8-HxCDD	50	54.7	35	-	82	Y
1,2,3,6,7,8-HxCDD	50	56.1	38	-	67	Y
1,2,3,7,8,9-HxCDD	50	52.3	32	-	81	Y
1,2,3,4,6,7,8-HpCDD	50	48.2	35	-	70	Y
OCDD	100	117	78	-	144	Y
2,3,7,8-TCDF	10	10	7.5	-	15.8	Y
1,2,3,7,8-PeCDF	50	50.2	40	-	67	Y
2,3,4,7,8-PeCDF	50	53.6	34	-	80	Y
1,2,3,4,7,8-HxCDF	50	53.6	36	-	67	Y
1,2,3,6,7,8-HxCDF	50	53.3	42	-	65	Y
2,3,4,6,7,8-HxCDF	50	56.1	35	-	78	Y
1,2,3,7,8,9-HxCDF	50	51.8	39	-	65	Y
1,2,3,4,6,7,8-HpCDF	50	52.5	41	-	61	Y
1,2,3,4,7,8,9-HpCDF	50	56.6	39	-	69	Y
OCDF	100	108	63	-	170	Y

Contract-required concentration limits for OPR as specified in Table 6, Method 1613, 10/94

Processed: 23 Jan 2026 11:37 Analyst: pw

METHOD 8290A **PCDD/F ONGOING PRECISION AND RECOVERY (OPR)** **FORM 8B**

Lab Name: SGS North America
Initial Calibration: ICAL: MM1_DF_11012024_03JAN2025
Instrument ID: MM1 GC Column ID: ZB-5ms
VER Data Filename: 260122P10 Analysis Date: 22-JAN-2026 14:40:52
Lab ID: OPR1_22743_DF

LABELED ANALYTES	SPIKE CONC.	CONC. FOUND	RANGE (ng/mL)			OK
13C-2,3,7,8-TCDD	100	95.3	20	-	175	Y
13C-1,2,3,7,8-PeCDD	100	97.3	21	-	227	Y
13C-1,2,3,4,7,8-HxCDD	100	86.9	21	-	193	Y
13C-1,2,3,6,7,8-HxCDD	100	86.8	25	-	163	Y
13C-1,2,3,7,8,9-HxCDD	100	88	26	-	166	Y
13C-1,2,3,4,6,7,8-HpCDD	100	100	26	-	166	Y
13C-OCDD	200	178	26	-	397	Y
13C-2,3,7,8-TCDF	100	88.9	22	-	152	Y
13C-1,2,3,7,8-PeCDF	100	99	21	-	192	Y
13C-2,3,4,7,8-PeCDF	100	94.3	13	-	328	Y
13C-1,2,3,4,7,8-HxCDF	100	73.3	19	-	202	Y
13C-1,2,3,6,7,8-HxCDF	100	76.2	21	-	159	Y
13C-2,3,4,6,7,8-HxCDF	100	75.5	22	-	176	Y
13C-1,2,3,7,8,9-HxCDF	100	82	17	-	205	Y
13C-1,2,3,4,6,7,8-HpCDF	100	94.5	21	-	158	Y
13C-1,2,3,4,7,8,9-HpCDF	100	83.9	20	-	186	Y
13C-OCDF	200	149	26	-	397	Y
CLEANUP STANDARD						
37Cl-2,3,7,8-TCDD	40	41.6	12.4	-	76.4	Y

Contract-required concentration limits for OPR as specified in Table 6, Method 1613. 10/94

Processed: 23 Jan 2026 11:37 Analyst: pw

Sample Receipt Notification

5500 Business Drive
Wilmington, NC 28405 USA
Tel: 910 794-1613
Toll Free: 866 846-8290
Fax: 910 794-3919

Project Manager:	*Amy Boehm*
Receipt Date & Time:	*31-Dec-25 at 11:34*
AP Project name:	*C2281*
Requested TAT:	*20 business days*
Projected due date:	*29-Jan-26*
Matrix:	*Wipe*
Phone#:	*910-794-1613*
Email Address:	*Amy.Boehm@sgs.com*

Company Contact:	*Andrea Colby*
Company:	*SGS North America Inc. - Orlando*
Project Name & Site:	*FC30428*
Project PO#:	*FC30428*
QAAP/Contract #:	*2025 407*
Requested Analysis:	*M8290A*
Phone#:	*407-425-6700*
Email Address:	*andrea.colby@sgs.com*

Client Smp ID	AP Smp ID	Sample Condition & Notes	Quantity	Size	Sampling Date	Sampling Time	Received Temp (°C)	Container #	Shipping #
W-01	C2281_001	100 cm2	1	4oz amber glass jar	30-Dec-25	n/a	0.8	1	8875 2575 0049

Preservation Type: **Sample Seals:** No

Notes/Comments:

Samples received intact

Any un-extracted sample will be stored for 90 days from reporting date. Additional storage fees may apply for any samples stored longer than 90 days.

Received by: Gisselle Bautista Remigio *Logged in by: Gisselle Bautista Remigio*

QC'ed by: AK 2 Jan 26

All services are rendered in accordance with the applicable SGS General Conditions of Service accessible via: http://www.sgs.com/terms_and_conditions.htm

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - FINAL LAB REPORT
RFP 607319-24

C2281

SGS GALSON LABORATORIES

6601 Kirkville Rd
East Syracuse, NY 13057
Tel: (315) 432-5227
888-432-LABS (5227)
Fax: (315) 437-0571
www.galsonlabs.com

☐ New Client?

Client Account No.*: _____

Report To*: Benjamin Bojda
Dominion Environmental
150 N. Durango Dr., Suite 190
Las Vegas, Nevada 89145
Phone No.*: 702-368-2700
Cell No.: 702-403-0200
Email Results to: Benjamin Bojda
Email address: bbojda@dominion-env.com; acalero@dominion-env.com

Invoice To*: NV Accounting
Dominion Environmental
20045 N. 19th Ave., Bldg. 7
Phoenix, AZ 85027
Phone No.: 623-516-1415
Email: nvaccounting@dominion-env.com
P.O. No.: 9161
Credit Card: ☐ Card on File ☐ Call for Credit Card Info.

☐ Samples submitted using the FreePumpLoan™ Program ☐ Samples submitted using the FreeSamplingBadges™ Program

Need Results By:	(surcharge)
☒ Standard	0%
☐ 4 Business Days	35%
☐ 3 Business Days	50%
☐ 2 Business Days	75%
☐ Next Day by 6pm	100%
☐ Next Day by Noon	150%
☐ Same Day	200%

Site Name: CC Fire Training Center Project: NV1256.228 Sampled by: B Bojda

Comments: Cinder Block Demo

List description of industry or Process/interferences present in sampling area :

State samples were collected in (e.g., NY): NV

Please indicate which OEL this data will be used for : ☐ OSHA PEL ☐ ACGIH TLV ☐ Cal OSHA ☐ MSHA ☐ Other (specify):

Sample Identification* (Maximum of 20 Characters)	Date Sampled	Collection Medium	Sample Volume . Sample Time Sample Area*	Sample Units*: L, ml,min,in2,cm2,ft2	Analysis Requested*	Method Reference^	Hexavalent Chromium Process (e.g., welding plating, painting, etc.)*
EXAMPLE	04/24/13	2pc UW PVC	960	L	Hexavalent Chromium (Cr6)	Mod OSHA ID-215	Welding
W-01	12/30/25	M8290 wipe	100	cm^2	Dioxin + Furans	EPA 8290	

^Galson Laboratories will subsitute our routine/preferred method if it does not match the method listed on the COC unless this box is checked: ☐ Use method(s) listed on COC

For metals analysis: if requesting an analyte with the option of a lower LOQ, please indicate if the lower LOQ is required (only available for certain analytes - see SAG) :

For crystalline silica: form(s) of silica needed must be indicated (Quartz, Cristobalite, and/or Tridymite)* :

Chain of Custody	Print Name/Signature	Date	Time		Print Name/Signature	Date	Time
Relinquished by :	B Bojda	12/30/25	1015	Received by :	Kenny Kuhn	12-30-25	1015
Relinquished by :	Kenny Kuhn	12-30-25	1430	Received by :		12/31/25	11:34

Samples received after 3pm will be considered as next day's business
* Required fields, failure to complete these fields may result in a delay in your samples being processed.

Page 1 of 1

C2281 Page 14 of 15

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - FINAL LAB REPORT
RFP 607319-24
125.0 S

ORIGIN ID:LASA (702) 873-4478 RFP 607319-24
SHIPPING DEPARTMENT SGS LAS VEGAS
SGS LAS VEGAS
3626 E. SUNSET SUITE 100

LAS VEGAS, NV 89120
UNITED STATES US

SHIP DATE: 30DEC25
ACTWGT: 20.00 LB
CAD: 113979271/INET4535

BILL SENDER

C2281

TO **SAMPLE RECEIVING**
SGS NORTH AMERICA - WILMINGTON
5500 BUSINESS DR

12/31/25
11:34
0.8°

WILMINGTON NC 28405
(910) 350-1903 REF:
INV:
PO: DEPT:

58HJ6/077E/59F2

FedEx Express

J2540250924O1uv

WED - 31 DEC 12:00P
PRIORITY OVERNIGHT

TRK# 0201 **8875 2575 0049**

28405

XX ILMA

NC-US **RDU**

Prepared for:

Clark County, Nevada
500 South Grand Central Parkway, 4th Floor
Las Vegas, Nevada 89155

COMPREHENSIVE ASBESTOS & LEAD TOXICITY CHARACTERISTIC LEACHING PROCEDURE (TCLP) SURVEY REPORT

NEW FIRE TRAINING CENTER
4425 WEST TROPICANA AVENUE
LAS VEGAS, NEVADA 89103

Prepared by:

Dominion Environmental Consultants NV, Inc.
150 North Durango Drive, Suite 190
Las Vegas, Nevada 89145
(702) 368-2700

Dominion Project Number: NV1256.217

Inspection Dates: January 16 and 17, 2024

TABLE OF CONTENTS

LIMITATIONS ..... SECTION 1

EXECUTIVE SUMMARY ..... SECTION 2

AERIAL/SITE MAPS ..... SECTION 3

PHOTO LOGS ..... SECTION 4

PLM BULK SAMPLE LOCATION MAPS ..... SECTION 5

PLM LABORATORY ANALYSIS REPORT ..... SECTION 6

ASBESTOS-CONTAINING MATERIALS LOCATION MAPS ..... SECTION 7

TEM LABORATORY ANALYSIS REPORT ..... SECTION 8

TCLP LABORATORY ANALYSIS REPORT ..... SECTION 9

EPA NESHAP NOTIFICATION INFORMATION SHEET ..... SECTION 10

GENERAL NOTES/EXCLUSIONS ..... SECTION 11

INSPECTOR CERTIFICATIONS ..... SECTION 12

LABORATORY CERTIFICATION ..... SECTION 13

SECTION 1

♦

LIMITATIONS

LIMITATIONS

The conclusions and results contained herein are based solely on the information presented in this report and are for the sole use of the Client exclusively and are subject to the terms and conditions of "The Contract." No other person or entity may rely on this report without the prior written consent of Dominion Environmental Consultants NV, Inc.

The sampling, testing, and observations described in the report represent conditions only at the specified times and locations. Additional materials or information which were hidden, undiscovered, inaccessible, or are not a part of the finding presented herein, would result in the modification of the conclusions and recommendations made herein. Any response action guidelines are based solely on the findings contained herein. The response action guidelines are presented as a courtesy and are not to be considered a complete or detailed set of specifications. Dominion performed these services using the degree of care and skill ordinarily exercised under similar conditions by reputable members of the profession practicing in the same or similar circumstances.

Please note, with regard to laboratory analysis of suspect bulk asbestos-containing materials: The Environmental Protection Agency (EPA) Method 600/R-93-116, Polarized Light Microscopy (PLM) is used for the testing of bulk building materials for asbestos by performing a visual estimation. This method is the most widely used method for estimating asbestos in bulk building materials and works well for most sample types. However, it might require a more detailed method such as point counting for accurate estimation of asbestos in samples with low asbestos concentration. This method is also not applicable for samples containing large amounts of fine fibers below the resolution of the PLM (<0.3 microns). Typically, the asbestos fibers present in non-friable organically bound (NOB) materials are often less than 0.1 microns in diameter and therefore may cause the PLM method to yield low estimates or even false negative results.

Dominion suggests that Transmission Electron Microscopy (TEM) Chatfield Semi-Quantitative EPA Method 600/R-93-116 be used to confirm all negative results of NOB materials. This method is particularly useful to reduce the possibility of false negatives in NOBs and to provide additional quantitative data for samples which contain low levels of asbestos. The TEM method is available at additional cost and is done only at the client's request.

Dominion's scope of service for this report did not include the inspection for, or identification of fungi, or any other hazardous or controlled substances not specifically identified herein.

Dominion is not responsible for the accuracy of information or services provided by others, or for conditions or consequences arising from relevant facts that were withheld, concealed, undiscovered, or not fully disclosed. Dominion is not a law firm and therefore, makes no representations regarding any potential liability of any person or entity for site conditions. Further, Dominion is not qualified to present medical advice. If any present or future health issues are in question, it is recommended that the findings in this report be presented to a qualified medical professional for evaluation.

SECTION 2

♦

EXECUTIVE SUMMARY

EXECUTIVE SUMMARY

INTRODUCTION

This report presents the results of a comprehensive asbestos inspection and Lead Toxicity Characteristic Leaching Procedure (TCLP) conducted at the Fire Training Center, located at 4425 West Tropicana Avenue, in Las Vegas, Nevada. A notice to proceed was received via email authorization from Ms. Monica Tate, Design & Construction Administrator, with Clark County, Nevada on March 4, 2022.

BACKGROUND INFORMATION

The above stated property is a government facility with four buildings originally constructed in 1983. The property is currently occupied as the Clark County Fire Training Center.

Ms. Monica Tate informed Dominion that all four buildings on the property are scheduled for demolition (see Section 3 – Aerial/Site Maps and Section 4 – Photo Logs).

ASBESTOS SAMPLING

The comprehensive asbestos inspection was conducted on January 16 and 17, 2024 by Mr. Benpeng Lin and Ms. Lanie Dakin, EPA-accredited AHERA asbestos building inspectors and Nevada OSHA licensed asbestos inspectors. Ms. Tate outlined the specific areas and materials scheduled to be disturbed during the scheduled demolition activities, instructed Dominion to only collect bulk samples of those outlined materials, and to have those samples analyzed for the presence of asbestos fibers by a qualified laboratory.

A total of two hundred and fifty-two (252) bulk samples were collected from the client-specified suspect building materials within the outlined areas of the building (see Section 5 – PLM Bulk Sample Location Maps). The suspect bulk samples were submitted to SGS Forensic Laboratories (SGS) for analysis using Polarized Light Microscopy (PLM) methods. SGS used the methods prescribed in Method 40 CFR, Part 763, in the Code of Federal Register in analyzing bulk samples. SGS is certified by the National Institute of Standards and Technology (NIST) as adhering to and in compliance with the National Voluntary Laboratory Accreditation Program (NVLAP) and holds the certification number 200908-0. The suspect asbestos bulk samples were collected and submitted to the laboratory using established chain of custody procedures. Bulk samples were collected utilizing safety and health practices as required by the Occupational Safety and Health Administration (OSHA).

Identified in the following list, are the bulk suspect materials sampled during the comprehensive asbestos inspection (the materials determined by laboratory analysis to contain greater than one percent (>1%) asbestos content, are indicated in **bold**):

BUILDING 1 –WAREHOUSE BUILDING

- Roof Insulation & Paper
  - Yellow Fibrous Material
  - White Non-Fibrous Material
- Gray Concrete Slab
- Gray Concrete Sidewalk
- White, Orange Peel Textured Drywall System
  - White Drywall
  - White Joint Compound
  - Drywall Tape
  - White Joint Compound

  - Paint
  - White Texture (Samples 11 & 12)
  - Paint (Samples 11 & 12)

- Black Cove Base System
  - Black Cove Base
  - Off-White Mastic
  - Paint (Samples 14 & 15)
  - Yellow Mastic (Samples 14 & 15)
  - White Non-Fibrous Material (Samples 14 & 15)

- Gray 12 in. by 24 in. Vinyl Floor Tile and Yellow Mastic

- White 2 ft. by 4 ft. Cement Acoustic Ceiling Tile and White Drywall

- White 2 ft. by 4 ft. Acoustic Ceiling Tile and Paint

- Pink Insulation

- White 1.5 in. by 1.5 in. Ceramic Tile and Yellow Mastic

- Pink 4 in. by 4 in. Ceramic Wall Tile and Dark Yellow Mastic

- Gray Wall and Floor Grout

- White Sink Counter Caulking

- White TSI Pipe Insulation
  - Yellow Fibrous Material
  - White Fibrous Material with Foil

- Gray/Purple CMU and Paint

BUILDING 2 – BURN BUILDING

- Off-White CMU Block

- Tan CMU Mortar

- Tan Concrete

- Decorative Black Felt and Clear Adhesive

- Clear Electrical Box Caulking

- Green Semi-Fibrous Pump Gasket

BUILDING 3 – SHOP/MAINTENANCE BUILDING

- Red 4 in. by 12 in. Ceramic Tile and Gray Grout

- Gray Decorative Block

- Multicolored CMU and Paint
- Gray Mortar
- Gray Epoxy Concrete Floor
  - Gray Cementitious Material
  - Gray Non-Fibrous Material
- White 2 ft. by 4 ft. Acoustic Ceiling Tile and Paint
- White, Orange Peel Textured Drywall System
  - White Drywall
  - Off-White Joint Compound
  - Drywall Tape
  - Off-White Texture
  - Paint
- Black 4 in. Cove Base System
  - Black Cove Base
  - Tan Mastic
  - Brown Mastic
- **12 in by 24 in. Gray Vinyl Floor Tile System**
  - Gray Vinyl Floor Tile
  - Dark Yellow Mastic
  - **Black Mastic**
- White Smooth Textured Drywall System
  - Beige Drywall
  - Beige Joint Compound
  - Drywall Tape
  - Beige Texture
  - Paint
- White 4 in. by 4 in. Ceramic Wall Tile and Gray Mastic
- White Grout
- Gray 1 in. by 1 in. Ceramic Floor Tile System
  - Gray Ceramic Floor Tile
  - Yellow Mastic
  - Black Mastic
- Gray Grout
- White Sink Caulking and Paint
- White Urinal Caulking and Paint
- Beige Stucco
  - Beige Cementitious Material

  - White Cementitious Material
  - Paint

- White Rail Roof Caulking and Paint

- PVC Roll-On Roof with Foam and Dirt Padding
  - Brown Fibrous Material
  - Yellow Non-Fibrous Material
  - White Non-Fibrous Material

BUILDING 4 – TRAINING CENTER

- Gray 24 in. by 24 in. Carpet Tile and Yellow Mastic

- Beige 12 in. by 12 in. Vinyl Floor Tile and Yellow Mastic

- Gray Decorative CMU Block

- Gray Mortar

- White 1 ft. by 1 ft. Acoustic Ceiling Tile and Paint

- White Wallpaper Drywall System
  - White Drywall
  - Off-White Joint Compound
  - Drywall Tape
  - Off-White Joint Compound
  - Yellow Adhesive
  - Gray Wall Covering

- Silver Duct Tape and Yellow Mastic

- Beige 6 in. Cove Base and Yellow Mastic

- Black Window Caulking

- White/Gray, Orange-Peel Textured Drywall System
  - White Drywall
  - Off-White Texture
  - Yellow Adhesive
  - Wallcovering

- White 2 ft. by 2 ft. Acoustic Ceiling Tile and Paint

- Black Door Frame Caulking

- White Interior Stucco and Paint

- White Grout

- 4 in. by 4 in. Pink Ceramic Wall Tile and Yellow Mastic

- 4 in by 4 in. White Ceramic Wall Tile and Yellow Mastic
- 2 in. by 2 in. Cream Ceramic Floor Tile and Yellow Mastic
- Gray Grout
- Gray 1 in. by 1 in. Ceramic Floor Tile System
  - Gray Ceramic Tile
  - Yellow Mastic
  - Black Adhesive
- Gray Grout
- Red 4 in. by 4 in. Wall Ceramic Tile and Yellow Mastic
- Gray 4 in. by 4 in. Ceramic Wall Tile and Yellow Mastic
- White Grout
- 2 ft. by 2 ft. Smooth Ceiling Tile and Paint
- White Sink Caulking and Paint
- White Ceiling Plaster System
  - Off-White/Gray Plaster
  - White Plaster
  - Paint
- Multicolored CMU Block and Paint
- Gray Mortar
- Gray 4 in. Cove Base and Yellow Mastic
- Beige 4 in. Cove Base and Yellow Mastic
- 2 ft. by 2 ft. White Smooth Ceiling Tile and Paint
- Red Carpet Wall Tile and Yellow Mastic
- Gray Wallpaper Drywall System
  - White Drywall
  - Off-White Joint Compound
  - Drywall Tape
  - Off-White Joint Compound
  - Yellow Adhesive
  - Gray Wallpaper
- **Cream 12 in. by 12 in. Vinyl Floor Tile System**
  - Cream Vinyl Floor Tile
  - Yellow Mastic
  - **Black Mastic**

- Black 4 in. Vinyl Cove Base and Yellow Mastic
- Blue 12 in. by 12 in. Vinyl Floor Tile and Yellow Mastic
- Multicolored CMU Block and Paint
- Gray Mortar
- Gray Sidewalk Concrete
- Red 4 in. by 12 in. Ceramic Tile and Gray Grout
- Black Grout
- Beige Stucco and Paint
- PVC Roll-On Roof System
    - White Drywall
    - Yellow Foam
    - White Non-Fibrous Material
- White Vent Caulking and Paint

Eight-six (86) of the eighty-four (84) building materials sampled were reported by the laboratory using the PLM analysis method to be "none detected" for asbestos-content (see Section 6 – PLM Laboratory Analysis Report).

As seen in Table 1, two of the building materials sampled were reported by laboratory PLM analysis to contain greater than one percent (>1%) asbestos-content (see Section 7 – Asbestos-Containing Materials Location Maps).

TABLE 1 – PLM Analyzed Materials Containing >1% Asbestos

Material	Location	NESHAP Category	OSHA Classification	Estimated Quantity	Laboratory Results
12 in by 24 in. Gray Vinyl Floor Tile System **(Black Mastic)**	Building 3 – Shop & Maintenance – NE Office	Category 2	Class II	208 ft^2	3% Chrysotile
Cream 12 in. by 12 in. Vinyl Floor Tile System **(Black Mastic)**	Building 4 – Training Center – Water Heater Room	Category 2	Class II	36 ft^2	5% Chrysotile

NESHAP Category: NESHAP may or may not apply to a project depending on the friability of the building material and the total square footage to be disturbed. When the amount of building material is less than 160 ft^2, NESHAP is not applicable. However, all asbestos waste still must be labeled and shipped to an asbestos landfill.

NESHAP Category 2 non-friable ACM is any material containing more than 1% asbestos as determined using PLM according to the methods specified in Appendix A, Subpart F, 40 CFR Part 763 that when dry, cannot be crumbled, pulverized, or reduced to powder by hand pressure.

OSHA Class II work means any activity involving the removal of ACM which is not thermal systems insulation (TSI) or surfacing material.

The **Estimated Quantity** refers to the total amount of estimated material.

PLM analysis cannot detect asbestos fibers less than 0.2 microns in diameter. Because asbestos fibers found in Non-friable Organically Bound (NOB) materials are often less than 0.1 microns in diameter, this method can sometimes yield low estimates or even false negative results. Conversely, TEM analysis, performed at a much higher magnification can sometimes miss extremely large asbestos fibers. For this reason, it is recommended that both PLM and TEM analyses be performed before an NOB material can be classified as Non-Asbestos Containing Construction Material (non-ACM).

One sample each of the following material was requested by the client to be reanalyzed by the laboratory using TEM methodology:

- Gray 12 in. by 24 in. Vinyl Floor Tile
- 12 in. by 24 in. Gray Vinyl Floor Tile
- Beige 12 in. by 12 in. Vinyl Floor Tile
- Cream 12 in. by 12 in. Vinyl Floor Tile
- Blue 12 in. by 12 in. Vinyl Floor Tile

The analytical laboratory report indicates that asbestos was "not detected" in the above samples by TEM analysis (see Section 8 – TEM Laboratory Analysis Report).

LEAD COMPOSITE TCLP SAMPLING

Due to the information that the building will be demolished, and to offer a total cost savings to the client, the painted surfaces throughout the building were assumed to be lead-based, will be treated as lead-based paint during the demolition, and a TCLP sample collected for disposal purposes.

One TCLP composite sample was collected on January 16 and 17, 2024 by Mr. Benpeng Lin, an EPA-accredited Lead Risk Assessor, and Ms. Lanie Dakin, an EPA-accredited Lead Inspector. The samples were analyzed to determine if the building waste is to be considered hazardous or if the waste may be disposed of at a non-hazardous waste landfill.

The composite sample was submitted to SGS Forensic Laboratories (SGS) for TCLP analysis. The sample was collected and submitted to the laboratory using established chain-of-custody procedures.

Identified in the following list, are the suspect materials sampled during the TCLP composite sampling:

BUILDING 1 –WAREHOUSE BUILDING

- Roof Insulation & Paper
  - Yellow Fibrous Material
  - White Non-Fibrous Material
- Gray Concrete Slab
- Gray Concrete Sidewalk
- White, Orange Peel Textured Drywall System
  - White Drywall
  - White Joint Compound
  - Drywall Tape
  - White Joint Compound
  - Paint
  - White Texture (Samples 11 & 12)
  - Paint (Samples 11 & 12)
- Black Cove Base System

  - Black Cove Base
  - Off-White Mastic
  - Paint (Samples 14 & 15)
  - Yellow Mastic (Samples 14 & 15)
  - White Non-Fibrous Material (Samples 14 & 15)

- Gray 12 in. by 24 in. Vinyl Floor Tile and Yellow Mastic
- White 2 ft. by 4 ft. Cement Acoustic Ceiling Tile and White Drywall
- White 2 ft. by 4 ft. Acoustic Ceiling Tile and Paint
- Pink Insulation
- White 1.5 in. by 1.5 in. Ceramic Tile and Yellow Mastic
- Pink 4 in. by 4 in. Ceramic Wall Tile and Dark Yellow Mastic
- Gray Wall and Floor Grout
- White Sink Counter Caulking
- White TSI Pipe Insulation
  - Yellow Fibrous Material
  - White Fibrous Material with Foil
- Gray/Purple CMU and Paint

BUILDING 2 – BURN BUILDING

- Off-White CMU Block
- Tan CMU Mortar
- Tan Concrete
- Decorative Black Felt and Clear Adhesive
- Clear Electrical Box Caulking
- Green Semi-Fibrous Pump Gasket

BUILDING 3 – SHOP/MAINTENANCE BUILDING

- Red 4 in. by 12 in. Ceramic Tile and Gray Grout
- Gray Decorative Block
- Multicolored CMU and Paint
- Gray Mortar

- Gray Epoxy Concrete Floor
  - Gray Cementitious Material
  - Gray Non-Fibrous Material

- White 2 ft. by 4 ft. Acoustic Ceiling Tile and Paint

- White, Orange Peel Textured Drywall System
  - White Drywall
  - Off-White Joint Compound
  - Drywall Tape
  - Off-White Texture
  - Paint

- Black 4 in. Cove Base System
  - Black Cove Base
  - Tan Mastic
  - Brown Mastic

- 12 in by 24 in. Gray Vinyl Floor Tile System
  - Gray Vinyl Floor Tile
  - Dark Yellow Mastic
  - Black Mastic

- White Smooth Textured Drywall System
  - Beige Drywall
  - Beige Joint Compound
  - Drywall Tape
  - Beige Texture
  - Paint

- White 4 in. by 4 in. Ceramic Wall Tile and Gray Mastic

- White Grout

- Gray 1 in. by 1 in. Ceramic Floor Tile System
  - Gray Ceramic Floor Tile
  - Yellow Mastic
  - Black Mastic

- Gray Grout

- White Sink Caulking and Paint

- White Urinal Caulking and Paint

- Beige Stucco
  - Beige Cementitious Material
  - White Cementitious Material
  - Paint

- White Rail Roof Caulking and Paint

- PVC Roll-On Roof with Foam and Dirt Padding

  - Brown Fibrous Material
  - Yellow Non-Fibrous Material
  - White Non-Fibrous Material

BUILDING 4 – TRAINING CENTER

- Gray 24 in. by 24 in. Carpet Tile and Yellow Mastic
- Beige 12 in. by 12 in. Vinyl Floor Tile and Yellow Mastic
- Gray Decorative CMU Block
- Gray Mortar
- White 1 ft. by 1 ft. Acoustic Ceiling Tile and Paint
- White Wallpaper Drywall System
  - White Drywall
  - Off-White Joint Compound
  - Drywall Tape
  - Off-White Joint Compound
  - Yellow Adhesive
  - Gray Wall Covering
- Silver Duct Tape and Yellow Mastic
- Beige 6 in. Cove Base and Yellow Mastic
- Black Window Caulking
- White/Gray, Orange-Peel Textured Drywall System
  - White Drywall
  - Off-White Texture
  - Yellow Adhesive
  - Wallcovering
- White 2 ft. by 2 ft. Acoustic Ceiling Tile and Paint
- Black Door Frame Caulking
- White Interior Stucco and Paint
- White Grout
- 4 in. by 4 in. Pink Ceramic Wall Tile and Yellow Mastic
- 4 in by 4 in. White Ceramic Wall Tile and Yellow Mastic
- 2 in. by 2 in. Cream Ceramic Floor Tile and Yellow Mastic
- Gray Grout
- Gray 1 in. by 1 in. Ceramic Floor Tile System

  - Gray Ceramic Tile
  - Yellow Mastic
  - Black Adhesive

- Gray Grout
- Red 4 in. by 4 in. Wall Ceramic Tile and Yellow Mastic
- Gray 4 in. by 4 in. Ceramic Wall Tile and Yellow Mastic
- White Grout
- 2 ft. by 2 ft. Smooth Ceiling Tile and Paint
- White Sink Caulking and Paint
- White Ceiling Plaster System
  - Off-White/Gray Plaster
  - White Plaster
  - Paint
- Multicolored CMU Block and Paint
- Gray Mortar
- Gray 4 in. Cove Base and Yellow Mastic
- Beige 4 in. Cove Base and Yellow Mastic
- 2 ft. by 2 ft. White Smooth Ceiling Tile and Paint
- Red Carpet Wall Tile and Yellow Mastic
- Gray Wallpaper Drywall System
  - White Drywall
  - Off-White Joint Compound
  - Drywall Tape
  - Off-White Joint Compound
  - Yellow Adhesive
  - Gray Wallpaper
- Cream 12 in. by 12 in. Vinyl Floor Tile System
  - Cream Vinyl Floor Tile
  - Yellow Mastic
  - Black Mastic
- Black 4 in. Vinyl Cove Base and Yellow Mastic
- Blue 12 in. by 12 in. Vinyl Floor Tile and Yellow Mastic
- Multicolored CMU Block and Paint
- Gray Mortar

- Gray Sidewalk Concrete
- Red 4 in. by 12 in. Ceramic Tile and Gray Grout
- Black Grout
- Beige Stucco and Paint
- PVC Roll-On Roof System
    - White Drywall
    - Yellow Foam
    - White Non-Fibrous Material
- White Vent Caulking and Paint

All four (4) TCLP lead composite samples collected were reported by the laboratory to be <0.3 mg/L, which is below the EPA regulatory threshold of 5 mg/L (see Section 9 – TCLP Laboratory Analysis Report). Therefore, the building materials waste that will be generated during the demolition can be disposed of at a non-hazardous waste landfill.

RECOMMENDATIONS

Asbestos

Dominion recommends that the above identified asbestos-containing materials (ACM) be removed by a licensed and qualified asbestos abatement contractor. The contractor should comply with all governing regulatory agency guidelines. If any un-sampled suspect building materials are discovered during the demolition project, those materials should be properly sampled by a certified inspector and analyzed by a qualified asbestos testing laboratory prior to their disturbance.

Dominion recommends that the client consider retaining the services of an independent asbestos consulting firm to have an AHERA accredited Project Designer write an industry standard technical specification for the abatement activities and to have an AHERA accredited Project Supervisor monitor the performance of a qualified and licensed abatement contractor. Depending on the extent of the above services that are performed, on completion the consultant can then provide final close-out documentation of the abatement activities.

All documentation is provided to Clark County, Nevada and should be retained in a permanent record. Should you have any questions regarding the procedures that were followed on this project, please contact me at any time. Thank you for the opportunity to provide these environmental consulting services.

Lanie Dakin
Project Supervisor

NEVADA Asbestos Abatement Consultant
NV License Number: IM-2398
Expires: May 3, 2024

AHERA Asbestos Building Inspector
AHERA Certificate Number: 4380-15844-050323
Expires: May 3, 2024

US EPA Lead Inspector
EPA Certificate Number: LBP-I-I251307-1
Expires: October 6, 2026

Benpeng Lin, MPH
Project Manager

NEVADA Asbestos Abatement Consultant
NV License Number: IM-2068
Expires: May 19, 2024

AHERA Asbestos Building Inspector
AHERA Certificate Number: ON-4644-7268-051923
Expires: May 19, 2024

US EPA Lead Risk Assessor
EPA Certificate Number: LBP-R-1218128-2
Expires: June 11, 2026

Reviewed By:



Benjamin Bojda, CIH, CSP
Vice President, Director of Operations

NEVADA Asbestos Abatement Consultant
NV License Number: IJPM-1380
Expires: June 30, 2024

AHERA Asbestos Building Inspector
AHERA Certificate Number: 4608-229-063023
Expires: June 30, 2024

US EPA Lead Risk Assessor
EPA Certificate Number: LBP-R-16125-3
Expires: May 8, 2026

SECTION 3

♦

AERIAL/SITE MAPS

Not to Scale

N

Aerial Site Map
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

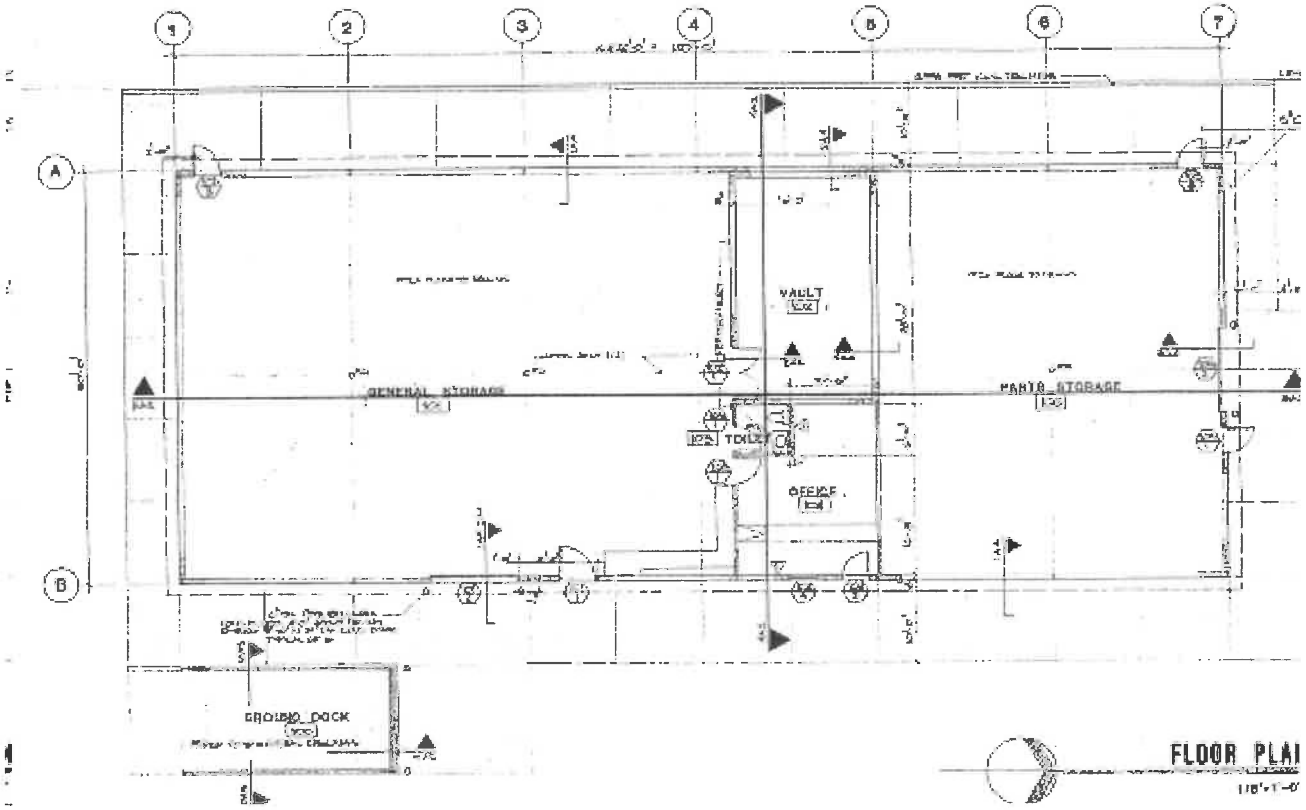

Site Map - Building 1 - Warehouse Building
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

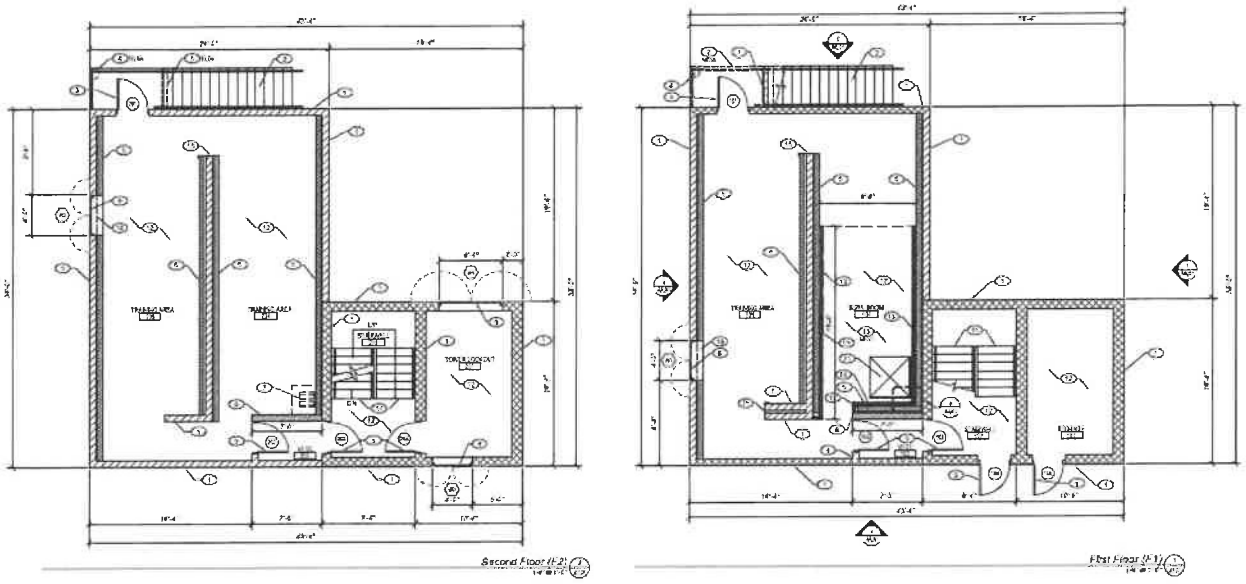

Site Map - Building 2 - Burn Building
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

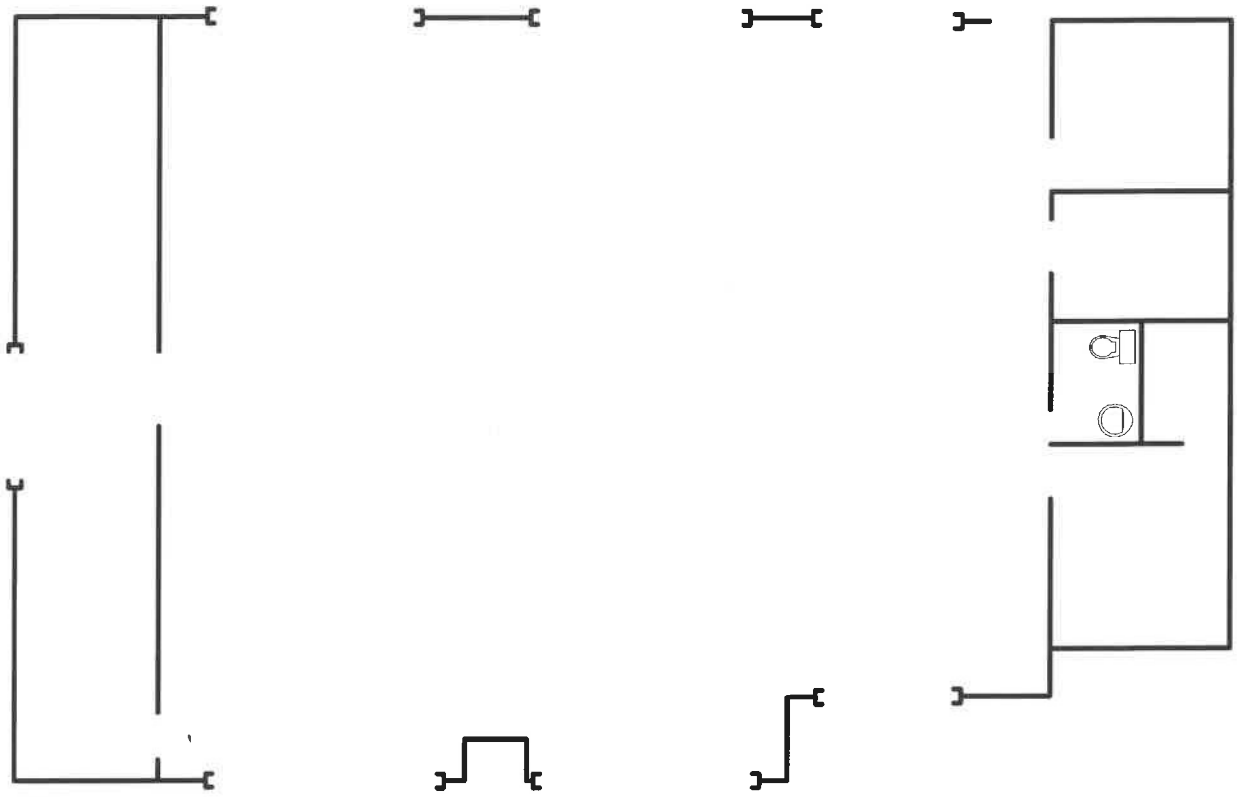

Site Map - Shop/Maintenance Building
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

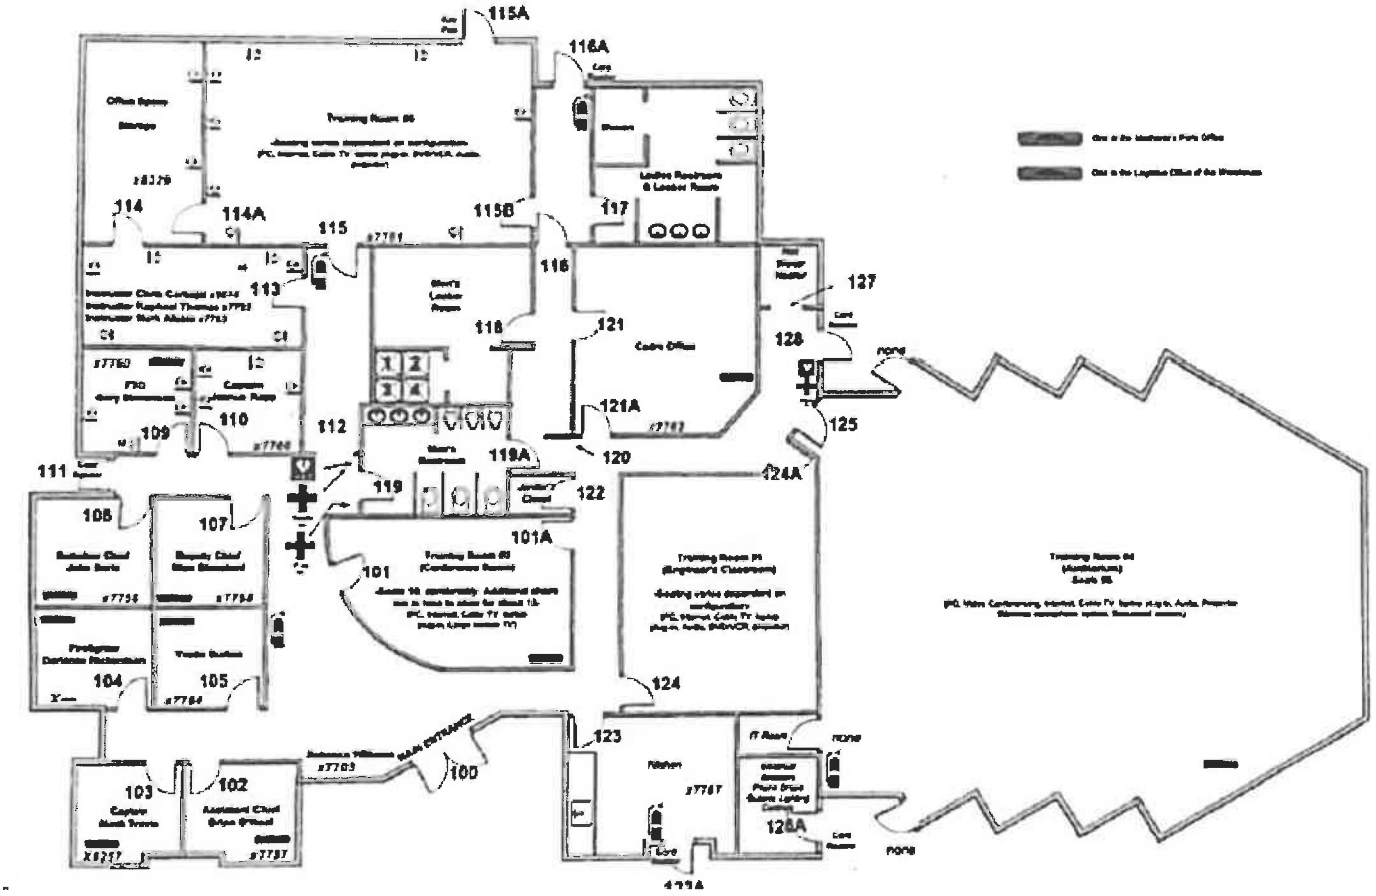

Site Map - Building 4 - Clark County Fire Dept Training Center
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

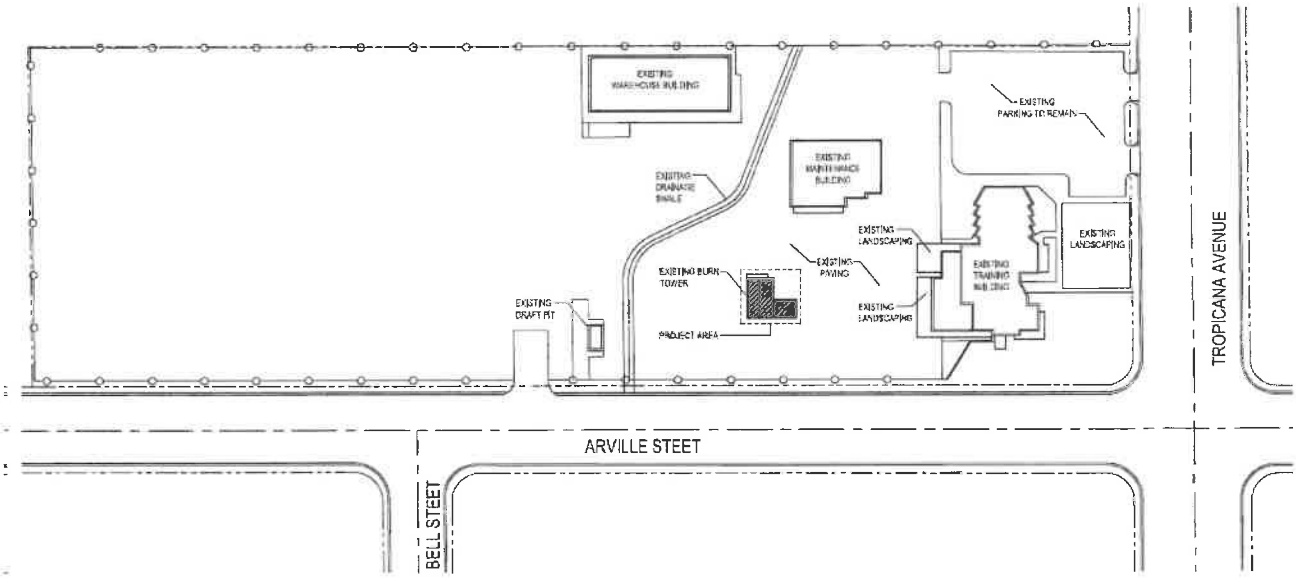

Site Map - General Plan - Roof
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

SECTION 4

♦

PHOTO LOGS

SITE PHOTOGRAPHS – BUILDING 1 - WAREHOUSE BUILDING

1.	2.
	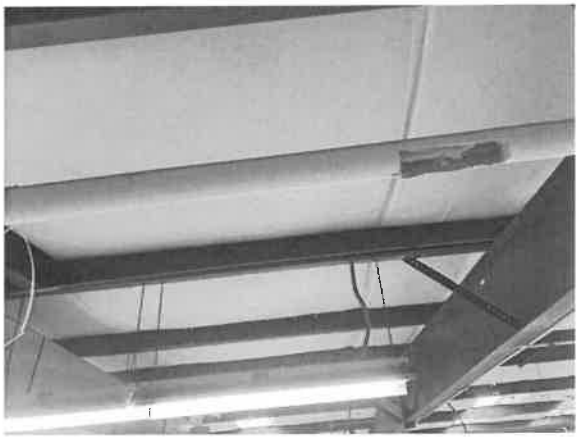
3.	4.

5.	6.

7.	8.

9.	10.

11.	12.

DOMINION

SITE PHOTOGRAPHS – BUILDING 2 – BURN BUILDING

1.	2.
3.	4.

DOMINION

5.	6.
	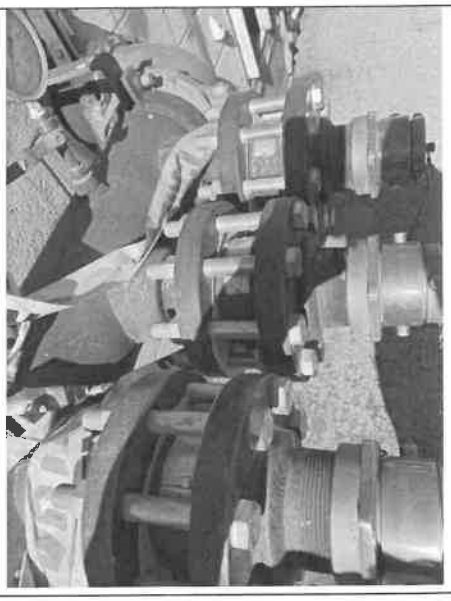

DOMINION

SITE PHOTOGRAPHS – BUILDING 3 – SHOP BUILDING

1.

2.

3.

4.

5.	6.
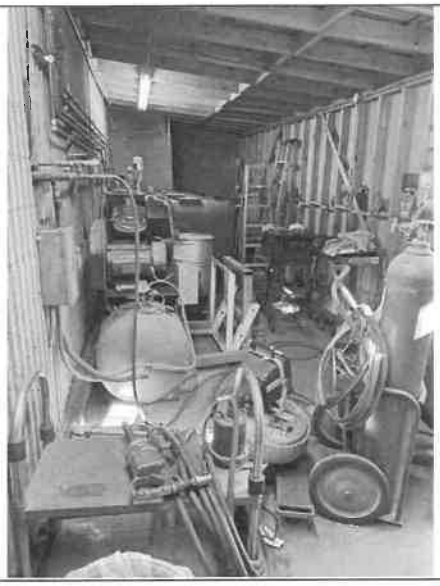	

7.	8.

9.	10.
11.	12.

13.	14.

DOMINION

SITE PHOTOGRAPHS – BUILDING 4 – TRAINING CENTER

1.	2.

3.	4.

5.	6.

7.	8.

9.	10.

11.	12.
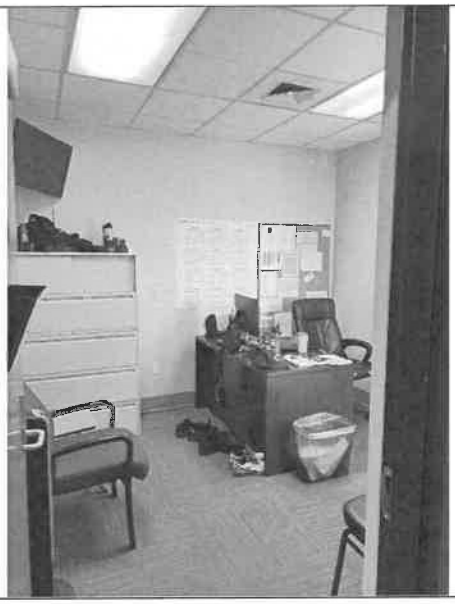	

13.	14.

15.	16.

17.	18.

19.	20.

21.	22.
23.	24.

DOMINION

SITE PHOTOGRAPHS - ROOF

1. Shop Building	2. Shop Building
3. Shop Building	4. Shop Building

5. Shop Building	6. Shop Building
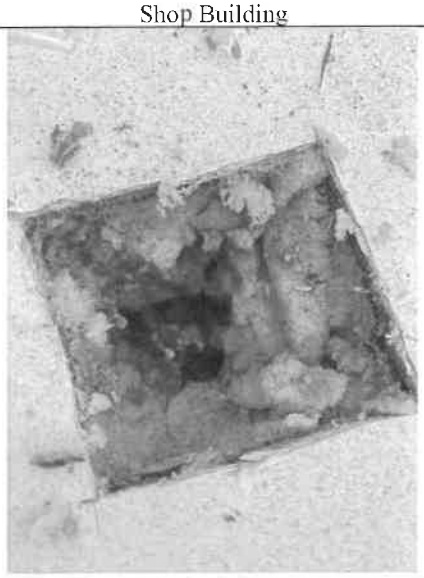	

7. Training Center	8. Training Center

9. Training Center	10. Training Center

11. Training Center	12. Training Center

SECTION 5

♦

PLM BULK SAMPLE LOCATION MAP

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

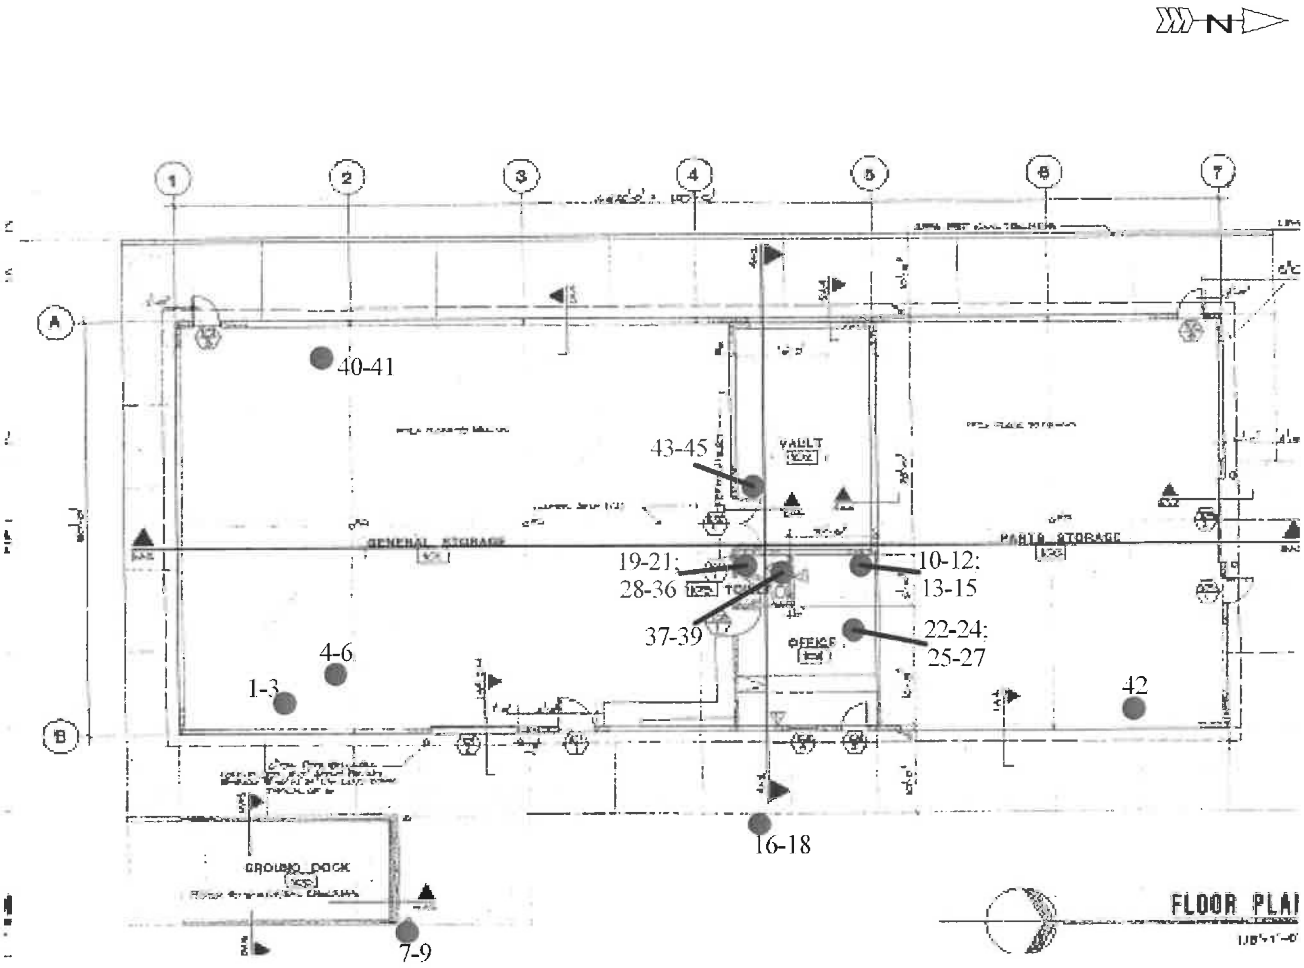

● PLM Bulk Sample Location

PLM Bulk Sample Location Map - Building 1 - Warehouse Building
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

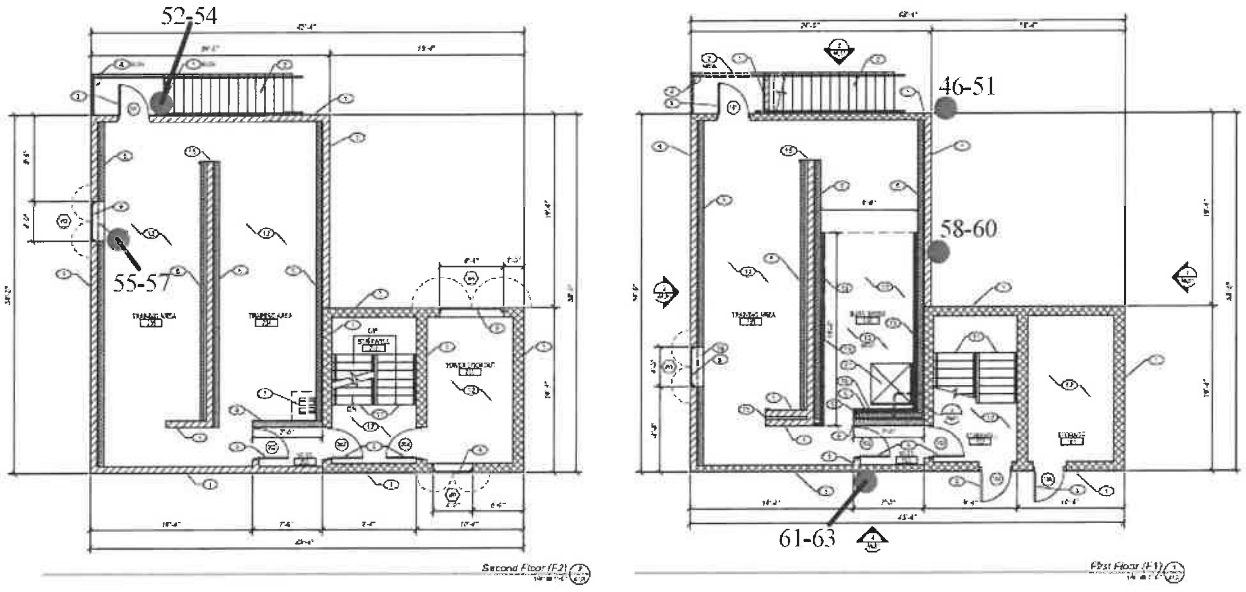

● PLM Bulk Sample Location

PLM Bulk Sample Location Map - Building 2 - Burn Building
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

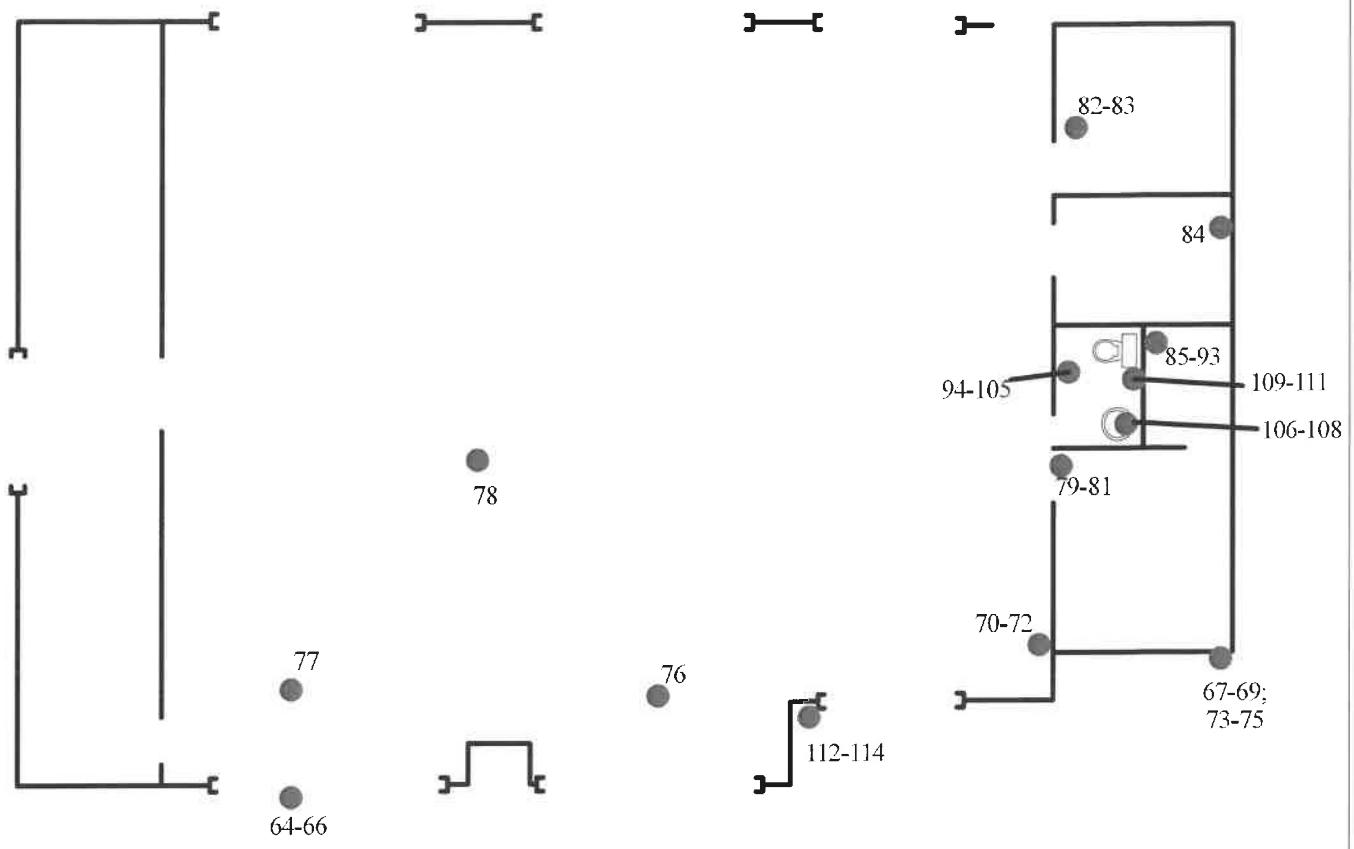

PLM Bulk Sample Location Map - Shop/Maintenance Building
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

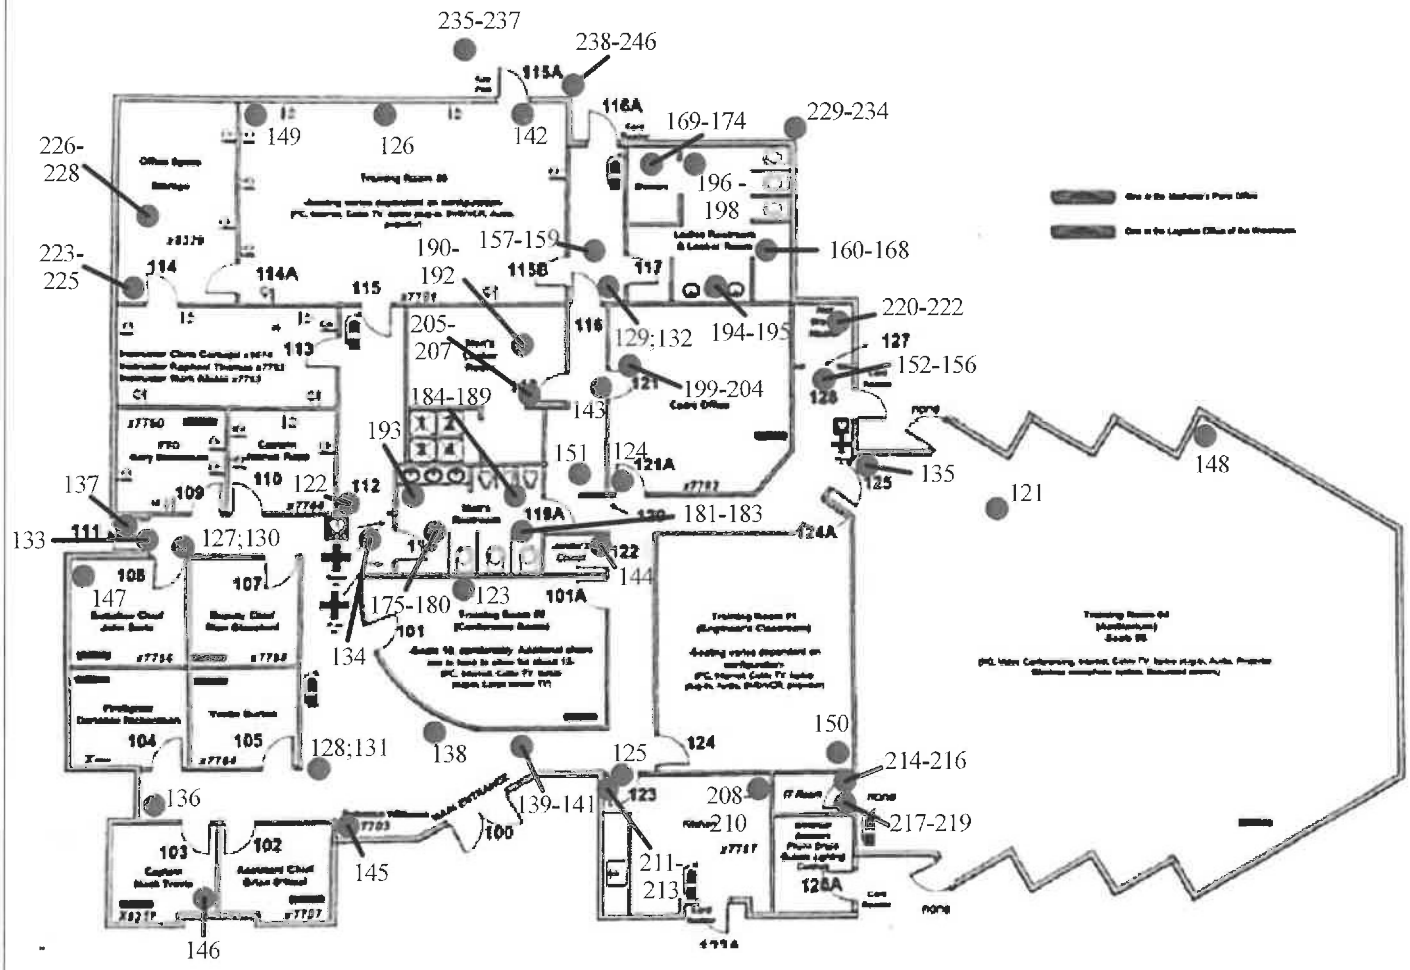

● PLM Bulk Sample Location

PLM Bulk Sample Location Map - CC Fire Dept Training Center
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

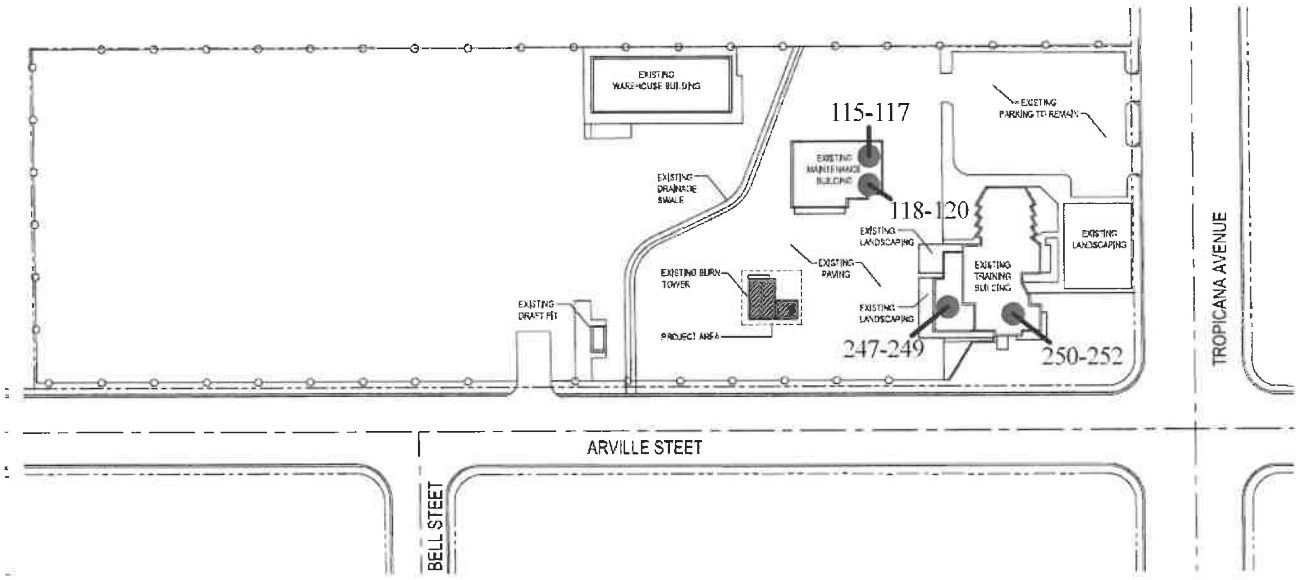

● PLM Bulk Sample Location

PLM Bulk Sample Location Map - General Plan - Roof
New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

SECTION 6

♦

PLM LABORATORY ANALYSIS REPORT

Bulk Asbestos Analysis

(EPA Method 40CFR, Part 763, Appendix E to Subpart E and EPA 600/R-93-116, Visual Area Estimation)
NVLAP Lab Code: 200908-0

Dominion Environmental Consultants
Ben Bojda
150 N. Durango Dr.
Suite 190
Las Vegas, NV 89145

Client ID: L2118
Report Number: B355832
Date Received: 01/17/24
Date Analyzed: 01/24/24
Date Printed: 01/24/24
First Reported: 01/24/24

Job ID/Site: 170166 NV1256.217, CCFD Training Center, 4425 W. Tropicana Ave

SGSFL Job ID: L2118
Total Samples Submitted: 252
Total Samples Analyzed: 252

Date(s) Collected: 01/17/2024

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 1	01354757						
Layer: Yellow Fibrous Material			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Fibrous Glass (85 %)		**Asbestos (ND)**					
PLM 2	01354758						
Layer: Yellow Fibrous Material			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Fibrous Glass (85 %)		**Asbestos (ND)**					
PLM 3	01354759						
Layer: Yellow Fibrous Material			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Fibrous Glass (85 %)		**Asbestos (ND)**					
PLM 4	01354760						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 5	01354761						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 6	01354762						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 7	01354763						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 8	01354764						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 9	01354765						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 10	01354766						
Layer: White Drywall			**ND**				
Layer: White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: White Joint Compound			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 11	01354767						
Layer: White Drywall			**ND**				
Layer: White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: White Joint Compound			**ND**				
Layer: Paint			**ND**				
Layer: White Texture			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 12	01354768						
Layer: White Drywall			**ND**				
Layer: White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: White Joint Compound			**ND**				
Layer: Paint			**ND**				
Layer: White Texture			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 13	01354769						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Off-White Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 14	01354770						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Off-White Mastic			**ND**				
Layer: Paint			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 15	01354771						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Off-White Mastic			**ND**				
Layer: Paint			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 16	01354772						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
PLM 17	01354773						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
PLM 18	01354774						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
PLM 19	01354775						
Layer: White Drywall			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %)		**Asbestos (ND)**					
PLM 20	01354776						
Layer: White Drywall			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 21	01354777						
Layer: White Drywall			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %)		**Asbestos (ND)**					
PLM 22	01354778						
Layer: Beige Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (35 %) Fibrous Glass (45 %)		**Asbestos (ND)**					
PLM 23	01354779						
Layer: Beige Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (35 %) Fibrous Glass (45 %)		**Asbestos (ND)**					
PLM 24	01354780						
Layer: Beige Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (35 %) Fibrous Glass (45 %)		**Asbestos (ND)**					
PLM 25	01354781						
Layer: Pink Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Fibrous Glass (99 %)		**Asbestos (ND)**					
PLM 26	01354782						
Layer: Pink Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Fibrous Glass (99 %)		**Asbestos (ND)**					
PLM 27	01354783						
Layer: Pink Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Fibrous Glass (99 %)		**Asbestos (ND)**					
PLM 28	01354784						
Layer: White Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 29	01354785						
Layer: White Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 30	01354786						
Layer: White Ceramic Tile			**ND**				
Layer: White Woven Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace) Synthetic (2 %)		**Asbestos (ND)**					
PLM 31	01354787						
Layer: Pink Ceramic Tile			**ND**				
Layer: Dark Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 32	01354788						
Layer: Pink Ceramic Tile			**ND**				
Layer: Dark Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 33	01354789						
Layer: Pink Ceramic Tile			**ND**				
Layer: Dark Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 34	01354790						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 35	01354791						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 36	01354792						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 37	01354793						
Layer: White Caulk			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 38	01354794						
Layer: White Caulk			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 39	01354795						
Layer: White Caulk			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 40	01354796						
Layer: Yellow Fibrous Material			**ND**				
Layer: White Fibrous Material with Foil			**ND**				
Total Composite Values of Fibrous Components: Cellulose (5 %) Fibrous Glass (3 %)		**Asbestos (ND)**					
PLM 41	01354797						
Layer: Yellow Fibrous Material			**ND**				
Layer: White Fibrous Material with Foil			**ND**				
Total Composite Values of Fibrous Components: Cellulose (5 %) Fibrous Glass (3 %)		**Asbestos (ND)**					
PLM 42	01354798						
Layer: Yellow Fibrous Material			**ND**				
Layer: White Fibrous Material with Foil			**ND**				
Total Composite Values of Fibrous Components: Cellulose (5 %) Fibrous Glass (3 %)		**Asbestos (ND)**					
PLM 43	01354799						
Layer: Grey and Purple Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 44	01354800						
Layer: Grey and Purple Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 45	01354801						
Layer: Grey and Purple Cementitious Material			**ND**				
Layer: Grey Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 46	01354802						
Layer: Off-White Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 47	01354803						
Layer: Off-White Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 48	01354804						
Layer: Off-White Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 49	01354805						
Layer: Tan Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 50	01354806						
Layer: Tan Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 51	01354807						
Layer: Tan Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 52	01354808						
Layer: Tan Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 53	01354809						
Layer: Tan Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 54	01354810						
Layer: Tan Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 55	01354811						
Layer: Black Fibrous Wallcovering			**ND**				
Layer: Clear Adhesive with Debris			**ND**				
Total Composite Values of Fibrous Components: Synthetic (90 %)		**Asbestos (ND)**					
PLM 56	01354812						
Layer: Black Fibrous Wallcovering			**ND**				
Layer: Clear Adhesive with Debris			**ND**				
Total Composite Values of Fibrous Components: Synthetic (90 %)		**Asbestos (ND)**					
PLM 57	01354813						
Layer: Black Fibrous Wallcovering			**ND**				
Layer: Clear Adhesive with Debris			**ND**				
Total Composite Values of Fibrous Components: Synthetic (90 %)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 58	01354814						
Layer: Clear Caulk			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 59	01354815						
Layer: Clear Caulk			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 60	01354816						
Layer: Clear Caulk			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 61	01354817						
Layer: Green Semi-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (40 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 62	01354818						
Layer: Green Semi-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (40 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 63	01354819						
Layer: Green Semi-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (40 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 64	01354820						
Layer: Red Ceramic Tile			**ND**				
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 65	01354821						
Layer: Red Ceramic Tile			**ND**				
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 66	01354822						
Layer: Red Ceramic Tile			**ND**				
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 67	01354823						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 68	01354824						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 69	01354825						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 70	01354826						
Layer: Multicolored Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 71	01354827						
Layer: Multicolored Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 72	01354828						
Layer: Multicolored Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 73	01354829						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 74	01354830						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 75	01354831						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 76	01354832						
Layer: Grey Cementitious Material			**ND**				
Layer: Grey Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 77	01354833						
Layer: Grey Cementitious Material			**ND**				
Layer: Grey Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 78	01354834						
Layer: Grey Cementitious Material			**ND**				
Layer: Grey Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 79	01354835						
Layer: Off-White Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (35 %) Fibrous Glass (45 %)		**Asbestos (ND)**					
PLM 80	01354836						
Layer: Off-White Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (35 %) Fibrous Glass (45 %)		**Asbestos (ND)**					
PLM 81	01354837						
Layer: Off-White Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (35 %) Fibrous Glass (45 %)		**Asbestos (ND)**					
PLM 82	01354838						
Layer: White Drywall			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Off-White Texture			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 83	01354839						
Layer: White Drywall			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Off-White Texture			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 84	01354840						
Layer: White Drywall			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Off-White Texture			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (20 %) Fibrous Glass (10 %)							
PLM 85	01354841						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Tan Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace)							
PLM 86	01354842						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Tan Mastic			**ND**				
Layer: Brown Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace) Talc (Trace)							
PLM 87	01354843						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Tan Mastic			**ND**				
Layer: Brown Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace) Talc (Trace)							
PLM 88	01354844						
Layer: Grey Tile			**ND**				
Layer: Dark Yellow Mastic			**ND**				
Layer: Black Mastic		Chrysotile	**3 %**				
Total Composite Values of Fibrous Components:		**Asbestos (Trace)**					
Cellulose (Trace)							
PLM 89	01354845						
Layer: Grey Tile			**ND**				
Layer: Dark Yellow Mastic			**ND**				
Layer: Black Mastic		Chrysotile	**3 %**				
Total Composite Values of Fibrous Components:		**Asbestos (Trace)**					
Cellulose (Trace)							
PLM 90	01354846						
Layer: Grey Tile			**ND**				
Layer: Dark Yellow Mastic			**ND**				
Layer: Black Mastic		Chrysotile	**3 %**				
Total Composite Values of Fibrous Components:		**Asbestos (Trace)**					
Cellulose (Trace)							

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 91	01354847						
Layer: Beige Drywall			**ND**				
Layer: Beige Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Beige Texture			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 92	01354848						
Layer: Beige Drywall			**ND**				
Layer: Beige Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Beige Texture			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 93	01354849						
Layer: Beige Drywall			**ND**				
Layer: Beige Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Beige Texture			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 94	01354850						
Layer: White Ceramic Tile			**ND**				
Layer: Grey Adhesive			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 95	01354851						
Layer: White Ceramic Tile			**ND**				
Layer: Grey Adhesive			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 96	01354852						
Layer: White Ceramic Tile			**ND**				
Layer: Grey Adhesive			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 97	01354853						
Layer: White Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 98	01354854						
Layer: White Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 99	01354855						
Layer: White Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 100	01354856						
Layer: Grey Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 101	01354857						
Layer: Grey Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 102	01354858						
Layer: Grey Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 103	01354859						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 104	01354860						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 105	01354861						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 106	01354862						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 107	01354863						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 108	01354864						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 109	01354865						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 110	01354866						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 111	01354867						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 112	01354868						
Layer: Beige Cementitious Material			**ND**				
Layer: White Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 113	01354869						
Layer: Beige Cementitious Material			**ND**				
Layer: White Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 114	01354870						
Layer: Beige Cementitious Material			**ND**				
Layer: White Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 115	01354871						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 116	01354872						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 117	01354873						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 118	01354874						
Layer: Brown Fibrous Material			**ND**				
Layer: Yellow Non-Fibrous Material			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 119	01354875						
Layer: Brown Fibrous Material			**ND**				
Layer: Yellow Non-Fibrous Material			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 120	01354876						
Layer: Brown Fibrous Material			**ND**				
Layer: Yellow Non-Fibrous Material			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 121	01354877						
Layer: Grey Carpet			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace) Synthetic (85 %)		**Asbestos (ND)**					
PLM 122	01354878						
Layer: Grey Carpet			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace) Synthetic (85 %)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 123	01354879						
Layer: Grey Carpet			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace) Synthetic (85 %)		**Asbestos (ND)**					
PLM 124	01354880						
Layer: Beige Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 125	01354881						
Layer: Beige Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 126	01354882						
Layer: Beige Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 127	01354883						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 128	01354884						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 129	01354885						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 130	01354886						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 131	01354887						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 132	01354888						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace)							
PLM 133	01354889						
Layer: Off-White Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (35 %) Fibrous Glass (45 %)							
PLM 134	01354890						
Layer: Off-White Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (35 %) Fibrous Glass (45 %)							
PLM 135	01354891						
Layer: Off-White Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (35 %) Fibrous Glass (45 %)							
PLM 136	01354892						
Layer: White Drywall			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Yellow Adhesive			**ND**				
Layer: Grey Wallcovering			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (20 %) Fibrous Glass (10 %)							
PLM 137	01354893						
Layer: White Drywall			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Yellow Adhesive			**ND**				
Layer: Grey Wallcovering			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (20 %) Fibrous Glass (10 %)							

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 138	01354894						
Layer: White Drywall			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Yellow Adhesive			**ND**				
Layer: Grey Wallcovering			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 139	01354895						
Layer: Yellow Mastic			**ND**				
Layer: Silver Duct Tape			**ND**				
Total Composite Values of Fibrous Components: Cellulose (10 %) Synthetic (60 %)		**Asbestos (ND)**					
PLM 140	01354896						
Layer: Yellow Mastic			**ND**				
Layer: Silver Duct Tape			**ND**				
Total Composite Values of Fibrous Components: Cellulose (10 %) Synthetic (60 %)		**Asbestos (ND)**					
PLM 141	01354897						
Layer: Yellow Mastic			**ND**				
Layer: Silver Duct Tape			**ND**				
Total Composite Values of Fibrous Components: Cellulose (10 %) Synthetic (60 %)		**Asbestos (ND)**					
PLM 142	01354898						
Layer: Beige Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 143	01354899						
Layer: Beige Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 144	01354900						
Layer: Beige Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Adhesive			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 145	01354901						
Layer: Black Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 146	01354902						
Layer: Black Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 147	01354903						
Layer: Black Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 148	01354904						
Layer: White Drywall			**ND**				
Layer: Off-White Texture			**ND**				
Layer: Yellow Adhesive			**ND**				
Layer: Wallcovering			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 149	01354905						
Layer: White Drywall			**ND**				
Layer: Off-White Texture			**ND**				
Layer: Yellow Adhesive			**ND**				
Layer: Wallcovering			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 150	01354906						
Layer: White Drywall			**ND**				
Layer: Off-White Texture			**ND**				
Layer: Yellow Adhesive			**ND**				
Layer: Wallcovering			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 151	01354907						
Layer: Off-White Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (35 %) Fibrous Glass (45 %)		**Asbestos (ND)**					
PLM 152	01354908						
Layer: Off-White Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (35 %) Fibrous Glass (45 %)		**Asbestos (ND)**					
PLM 153	01354909						
Layer: Off-White Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (35 %) Fibrous Glass (45 %)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 154	01354910						
Layer: Black Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 155	01354911						
Layer: Black Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 156	01354912						
Layer: Black Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 157	01354913						
Layer: White Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 158	01354914						
Layer: White Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 159	01354915						
Layer: White Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 160	01354916						
Layer: White Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 161	01354917						
Layer: White Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 162	01354918						
Layer: White Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 163	01354919						
Layer: Pink Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 164	01354920						
Layer: Pink Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 165	01354921						
Layer: Pink Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 166	01354922						
Layer: White Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 167	01354923						
Layer: White Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 168	01354924						
Layer: White Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 169	01354925						
Layer: Cream Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 170	01354926						
Layer: Cream Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 171	01354927						
Layer: Cream Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 172	01354928						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 173	01354929						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 174	01354930						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 175	01354931						
Layer: Grey Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Adhesive			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 176	01354932						
Layer: Grey Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Adhesive			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 177	01354933						
Layer: Grey Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Adhesive			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 178	01354934						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 179	01354935						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 180	01354936						
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 181	01354937						
Layer: Red Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 182	01354938						
Layer: Red Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 183	01354939						
Layer: Red Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 184	01354940						
Layer: Grey Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 185	01354941						
Layer: Grey Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 186	01354942						
Layer: Grey Ceramic Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 187	01354943						
Layer: White Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 188	01354944						
Layer: White Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 189	01354945						
Layer: White Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 190	01354946						
Layer: White Semi-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 191	01354947						
Layer: White Semi-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 192	01354948						
Layer: White Semi-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 193	01354949						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 194	01354950						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 195	01354951						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 196	01354952						
Layer: White Plaster			**ND**				
Layer: Off-White Plaster			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 197	01354953						
Layer: Grey Plaster			**ND**				
Layer: White Plaster			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 198	01354954						
Layer: Grey Plaster			**ND**				
Layer: White Plaster			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 199	01354955						
Layer: Multicolored Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 200	01354956						
Layer: Multicolored Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 201	01354957						
Layer: Multicolored Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 202	01354958						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 203	01354959						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 204	01354960						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 205	01354961						
Layer: Grey Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 206	01354962						
Layer: Grey Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 207	01354963						
Layer: Grey Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 208	01354964						
Layer: Beige Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 209	01354965						
Layer: Beige Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 210	01354966						
Layer: Beige Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 211	01354967						
Layer: White Semi-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 212	01354968						
Layer: White Semi-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 213	01354969						
Layer: White Semi-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 214	01354970						
Layer: Red Carpet			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace) Synthetic (85 %)							
PLM 215	01354971						
Layer: Red Carpet			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace) Synthetic (85 %)							
PLM 216	01354972						
Layer: Red Carpet			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace) Synthetic (85 %)							
PLM 217	01354973						
Layer: White Drywall			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Yellow Adhesive			**ND**				
Layer: Grey Wallpaper			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (20 %) Fibrous Glass (10 %)							
PLM 218	01354974						
Layer: White Drywall			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Yellow Adhesive			**ND**				
Layer: Grey Wallpaper			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (20 %) Fibrous Glass (10 %)							
PLM 219	01354975						
Layer: White Drywall			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Drywall Tape			**ND**				
Layer: Off-White Joint Compound			**ND**				
Layer: Yellow Adhesive			**ND**				
Layer: Grey Wallpaper			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (20 %) Fibrous Glass (10 %)							

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 220	01354976						
Layer: Cream Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Mastic		Chrysotile	**5 %**				
Total Composite Values of Fibrous Components:		**Asbestos (Trace)**					
Cellulose (Trace)							
PLM 221	01354977						
Layer: Cream Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Mastic		Chrysotile	**5 %**				
Total Composite Values of Fibrous Components:		**Asbestos (Trace)**					
Cellulose (Trace)							
PLM 222	01354978						
Layer: Cream Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Layer: Black Mastic		Chrysotile	**5 %**				
Total Composite Values of Fibrous Components:		**Asbestos (Trace)**					
Cellulose (Trace)							
PLM 223	01354979						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace)							
PLM 224	01354980						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace)							
PLM 225	01354981						
Layer: Black Non-Fibrous Material			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace)							
PLM 226	01354982						
Layer: Blue Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace)							
PLM 227	01354983						
Layer: Blue Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components:		**Asbestos (ND)**					
Cellulose (Trace)							

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 228	01354984						
Layer: Blue Tile			**ND**				
Layer: Yellow Mastic			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 229	01354985						
Layer: Multi-Color Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 230	01354986						
Layer: Multi-Color Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 231	01354987						
Layer: Multi-Color Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 232	01354988						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 233	01354989						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 234	01354990						
Layer: Grey Mortar			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 235	01354991						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 236	01354992						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 237	01354993						
Layer: Grey Cementitious Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 238	01354994						
Layer: Red Ceramic Tile			**ND**				
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 239	01354995						
Layer: Red Ceramic Tile			**ND**				
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 240	01354996						
Layer: Red Ceramic Tile			**ND**				
Layer: Grey Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 241	01354997						
Layer: Black Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 242	01354998						
Layer: Black Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 243	01354999						
Layer: Black Grout			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 244	01355000						
Layer: Beige Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 245	01355001						
Layer: Beige Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110. Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Client Name: Dominion Environmental Consultants

Report Number: B355832
Date Printed: 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer
PLM 246	01355002						
Layer: Beige Cementitious Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 247	01355003						
Layer: White Drywall			**ND**				
Layer: Yellow Foam			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 248	01355004						
Layer: White Drywall			**ND**				
Layer: Yellow Foam			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 249	01355005						
Layer: White Drywall			**ND**				
Layer: Yellow Foam			**ND**				
Layer: White Non-Fibrous Material			**ND**				
Total Composite Values of Fibrous Components: Cellulose (20 %) Fibrous Glass (10 %)		**Asbestos (ND)**					
PLM 250	01355006						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 251	01355007						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					
PLM 252	01355008						
Layer: White Non-Fibrous Material			**ND**				
Layer: Paint			**ND**				
Total Composite Values of Fibrous Components: Cellulose (Trace)		**Asbestos (ND)**					

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

Report Number: B355832
Client Name: Dominion Environmental Consultants **Date Printed:** 01/24/24

Sample ID	Lab Number	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer	Asbestos Type	Percent in Layer

Mariah Douds, Laboratory Supervisor, Las Vegas Laboratory

Note: Limit of Quantification ('LOQ') = 1%. 'Trace' denotes the presence of asbestos below the LOQ. 'ND' = 'None Detected'.

Analytical results and reports are generated by SGS Forensic Laboratories (SGSFL) at the request of and for the exclusive use of the person or entity (client) named on such report. Results, reports or copies of same will not be released by SGSFL to any third party without prior written request from client. This report applies only to the sample(s) tested. Supporting laboratory documentation is available upon request. This report must not be reproduced except in full, unless approved by SGSFL. The client is solely responsible for the use and interpretation of test results and reports requested from SGSFL. This report must not be used by the client to claim product endorsement by NVLAP or any other agency of the U.S. Government. SGSFL is not able to assess the degree of hazard resulting from materials analyzed. SGS Forensic Laboratories reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified. All samples were received in acceptable condition unless otherwise noted.

3620 E. Sunset Road, Suite 110, Las Vegas, NV 89120 | phone: 702.873.4478 Fax: 702.784.0030 | https://falaboratories.sgs.com

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Client No.:

Dominion Environmental Consultants NV, Inc.
150 N. Durango Drive, Las Vegas, NV 89145

PO / Job#: 70116 NV1256.217 Date: 1.17.24

Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / (5Day)

☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer

☐ PLM: ☒ Standard / ☐ Point Count 400 / 1000 / ☐ CARB 435

Contact: Benjamin Bojda Phone: (702) 368-2700

E-mail: bbojda@dominion-env.com

☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402
☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield
☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight %
☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)

Site Name: CCFD Training Center

Site Location: 4425 W. Tropicana Ave

☐ IAQ Particle Identification ☐ Opaques/Char (Wildfire)
☐ Limited Particle ID (Wildfire) ☐ Special Project

☐ Metals Analysis Matrix: Method: Analytes:

Comments:

☐ Silica in Air ☐ w/Gravimetry ☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
PLM 1-3	1.17.24	Bldg 1 - roof insulation + paper	A P C				
4-6		- concrete slab	A P C				
7-9		- concrete sidewalk	A P C				
10-12		- white paint OP texture, JC, tape + drywall	A P C				
13-15		- black cove base + mastic	A P C				
16-18		- grey 12"x24" VFT + mastic	A P C				
19-21		- white 2'x4' cement acoustic ceiling tile	A P C				
22-24		- white 2'x4' acoustic ceiling tile	A P C				
25-27		- pink insulation	A P C				
28-30		- white 1.5" SF ceramic tile (wall + floor) + mastic	A P C				

Sampled By: Benjamin Bojda / Janie Baker Date / Time: 1.17.24 Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By:	Relinquished By:	Relinquished By:
Date / Time: 1.17.24 16:09	Date / Time:	Date / Time:
Received By:	Received By:	Received By:
Date / Time: 1/17/24 1610	Date / Time:	Date / Time:
Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Client No.:

Dominion Environmental Consultants NV, Inc.
150 N. Durango Drive, Las Vegas, NV 89145

PO/Job#: 1907166 NV1256.217 Date: 1.17.24

Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / 5Day

☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer

☐ PLM: ☒ Standard / ☐ Point Count 400 / 1000 / ☐ CARB 435

Contact: Benjamin Bojda Phone: (702) 368-2700

E-mail: bbojda@dominion-env.com

☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402
☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield
☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight %
☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)

Site Name: CCFD Training Center

Site Location: 4425 W. Tropicana Ave

☐ IAQ Particle Identification ☐ Opaques/Char (Wildfire)
☐ Limited Particle ID (Wildfire) ☐ Special Project

☐ Metals Analysis Matrix: Method: Analytes:

Comments:

☐ Silica in Air ☐ w/Gravimetry ☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
PLM 31-33	1.17.24	Bldg 1 - pink 4"sq ceramic wall tile + mastic	A P C				
34-36		- grey grout (wall + floor)	A P C				
37-39		- sink counter caulk	A P C				
40-42		- white pipe insulation (TSI)	A P C				
43-45		- CMU	A P C				
46-48		Bldg 2 - CMU block	A P C				
49-51		- CMU mortar	A P C				
52-54		- concrete	A P C				
55-57		- decorative black felt	A P C				
58-60		- caulking - electric box	A P C				

Sampled By: Daniel Sutton Date/Time: 1.17.24 Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By:	Relinquished By:	Relinquished By:
Date / Time: 1.17.24 16:09	Date / Time:	Date / Time:
Received By:	Received By:	Received By:
Date / Time: 1/17/24 1610	Date / Time:	Date / Time:
Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Client No.:

Dominion Environmental Consultants NV, Inc.
150 N. Durango Drive, Las Vegas, NV 89145

PO / Job#: 770166 NV1756.217 Date: 1.17.24

Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / (5Day)

☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer

☐ PLM: ☒ Standard / ☐ Point Count 400 - 1000 / ☐ CARB 435

Contact: Benjamin Bojda Phone: (702) 368-2700

E-mail: bbojda@dominion-env.com

☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402
☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield
☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight %
☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)

Site Name: CCFD Training Center

Site Location: 4425 W. Tropicana Ave

☐ IAQ Particle Identification ☐ Opaques/Char (Wildfire)
☐ Limited Particle ID (Wildfire) ☐ Special Project

☐ Metals Analysis Matrix: Method: Analytes:

Comments:

☐ Silica in Air ☐ w/Gravimetry ☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
PLM 61-63	1.17.24	Bldg 2 - pump gasket	[A] [P] [C]				
64-66		Bldg 3 - red 4"X12" ceramic tile + grout	[A] [P] [C]				
67-69		- decorative block	[A] [P] [C]				
70-72		- CMU	[A] [P] [C]				
73-75		- mortar	[A] [P] [C]				
76-78		- epoxy concrete floor	[A] [P] [C]				
79-81		- white 2'x4' acoustic ceiling tile	[A] [P] [C]				
82-84		- white paint, DP texture, JT tape, drywall	[A] [P] [C]				
85-87		- black 4" cove base + mastic	[A] [P] [C]				
88-90		- 12"X24" gray VFT + mastic	[A] [P] [C]				

Sampled By: Benjamin + Vanie Bojda Date / Time: 1.17.24 Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By:	Relinquished By:	Relinquished By:
Date / Time: 1-17-24 16:09	Date / Time:	Date / Time:
Received By:	Received By:	Received By:
Date / Time: 1/17/24 1610	Date / Time:	Date / Time:
Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Client No.:

Dominion Environmental Consultants NV, Inc.
150 N. Durango Drive, Las Vegas, NV 89145

PO / Job #: Proposal NV1256.24 Date: 1.17.24

Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / 5Day

☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer

☐ PLM: ☒ Standard / ☐ Point Count 400-1000 / ☐ CARB 435

Contact: Benjamin Bojda Phone: (702) 368-2700

E-mail: bbojda@dominion-env.com

☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402
☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield
☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight %
☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)

Site Name: CLFD Training Center

Site Location: 4425 W. Tropicana Ave

☐ IAQ Particle Identification ☐ Opaques/Char (Wildfire)
☐ Limited Particle ID (Wildfire) ☐ Special Project

☐ Metals Analysis Matrix: Method: Analytes:

Comments:

☐ Silica in Air ☐ w/Gravimetry ☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
PLM 91-93	1.17.24	Bldg 3- white paint smooth texture drywall, tape,	A P C				
94-96		white 4"sq ceramic wall tile + mastic	A P C				
97-99		- white grout	A P C				
100-102		- grey 1"sq ceramic floor tile + mastic	A P C				
103-105		- grey grout	A P C				
106-108		- sink caulk	A P C				
109-111		- urinal caulk	A P C				
112-114		- beige stucco	A P C				
115-117		- roof caulk - rail	A P C				
118-120		- PVC roof rollon w/ foam + dirt padding	A P C				

Sampled By: Benjamin + Jamie Date/Time: 1.17.24 Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By:	Relinquished By:	Relinquished By:
Date / Time: 1.17.24 16:09	Date / Time:	Date / Time:
Received By:	Received By:	Received By:
Date / Time: 1/17/24 Condition Acceptable? ☐ Yes ☐ No	Date / Time: Condition Acceptable? ☐ Yes ☐ No	Date / Time: Condition Acceptable? ☐ Yes ☐ No

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Client No.:

Dominion Environmental Consultants NV, Inc.
150 N. Durango Drive, Las Vegas, NV 89145

PO / Job#: 170166 NV1256.217 Date: 1/17/24

Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / 5Day

☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer

☐ PLM: ☐ Standard / ☐ Point Count 400 - 1000 / ☐ CARB 435

Contact: Benjamin Bojda Phone: (702) 368-2700

E-mail: bbojda@dominion-env.com

☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402
☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield
☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight %
☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)

Site Name: CCFD Training Center

☐ IAQ Particle Identification ☐ Opaques/Char (Wildfire)
☐ Limited Particle ID (Wildfire) ☐ Special Project

Site Location: 4425 W Tropicana Ave

☐ Metals Analysis Matrix: Method:
Analytes:

Comments:

☐ Silica in Air ☐ w/Gravimetry
☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
PLM 121-123	1/17/24	Bldg #4 - Gray 2'x2' vinyl carpet tile & mastic	A P C				
124-126		- Beige 12" X 12" VFT & mastic	A P C				
127-129		- Decorive CMU Block	A P C				
130-132		- Mortar	A P C				
133-135		- white 1'x1' Acoustic ceiling tile	A P C				
136-138		- white wallpaper Drywall system (All layers)	A P C				
139-141		- Duct tape & mastic	A P C				
142-144		- Beige 6" cove base & mastic	A P C				
145-147		- Black window caulk	A P C				
148-150		- white/Gray OP texture Drywall System	A P C				

Sampled By: Ben Cyn/Laine Date/Time: 1/17/24

Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By:	Relinquished By:	Relinquished By:
Date / Time: 1-17-24 16:09	Date / Time:	Date / Time:
Received By:	Received By:	Received By:
Date / Time: 1/17/24 1610	Date / Time:	Date / Time:
Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Client No.:

Dominion Environmental Consultants NV, Inc.
150 N. Durango Drive, Las Vegas, NV 89145

PO / Job#: 1901166 NV1256.217 Date: 1.17.24

Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / 5Day

☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer

☐ PLM: ☒ Standard / ☐ Point Count 400 - 1000 / ☐ CARB 435

Contact: Benjamin Bojda Phone: (702) 368-2700

E-mail: bbojda@dominion-env.com

☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402
☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield
☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight %
☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)

Site Name: CCFD Training Center

Site Location: 4425 W. Tropicana Ave

☐ IAQ Particle Identification ☐ Opaques/Char (Wildfire)
☐ Limited Particle ID (Wildfire) ☐ Special Project

☐ Metals Analysis Matrix: Method: Analytes:

Comments:

☐ Silica in Air ☐ w/Gravimetry ☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
PLM 151-153	1.17.24	Bldg 4-white 2'x2' acoustic ceiling tile	[A] [P] [C]				
154-156		-black door frame caulk	[A] [P] [C]				
157-159		-white stucco (interior)	[A] [P] [C]				
160-162		-white grout	[A] [P] [C]				
163-165		-4"sq pink ceramic wall tile + mastic	[A] [P] [C]				
166-168		-4"sq white ceramic wall tile + mastic	[A] [P] [C]				
169-171		-2"sq cream ceramic floor tile + mastic	[A] [P] [C]				
172-174		-grey grout	[A] [P] [C]				
175-177		-grey 1"sq ceramic floor tile + mastic	[A] [P] [C]				
178-180		-grey grout	[A] [P] [C]				

Sampled By: Benjamin Bojda Date / Time: 1.17.24 Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By:	Relinquished By:	Relinquished By:
Date / Time: 1.17.24 16:09	Date / Time:	Date / Time:
Received By:	Received By:	Received By:
Date / Time: 1/17/24 1640	Date / Time:	Date / Time:
Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Client No.:

Dominion Environmental Consultants NV, Inc.
150 N. Durango Drive, Las Vegas, NV 89145

PO / Job#: 170166 / NV1256217 Date: 1/17/24

Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / 5Day

☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer

☒ PLM: ☐ Standard / ☐ Point Count 400 1000 / ☐ CARB 435

Contact: Benjamin Bojda Phone: (702) 368-2700

E-mail: bbojda@dominion-env.com

☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402
☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield
☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight %
☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)

Site Name: CCFD Training Center

Site Location: 4425 W Tropicana Ave

☐ IAQ Particle Identification ☐ Opaques/Char (Wildfire)
☐ Limited Particle ID (Wildfire) ☐ Special Project

☐ Metals Analysis Matrix: Method: Analytes:

Comments:

☐ Silica in Air ☐ w/Gravimetry ☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
PLM 181-183	1/17/24	Bldg #4 - Red 4"x4" wall ceramic tile	A P C				
184-186		- Gray 4"x4" wall ceramic tile	A P C				
187-189		- white grout	A P C				
190-192		- 2x2' ceiling tile smooth	A P C				
193-195		- Sink Caulk	A P C				
196-198		- white ceiling plaster	A P C				
199-201		- Conc Block	A P C				
202-204		- mortar	A P C				
205-207		- Gray 4" cove base & mastic	A P C				
208-210		- Beige 4" cove base & mastic	A P C				

Sampled By: Benjamin Bojda Date/Time: 1/17/24

Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By:	Relinquished By:	Relinquished By:
Date / Time: 1-17-24 16:09	Date / Time:	Date / Time:
Received By:	Received By:	Received By:
Date / Time: 1/17/24 1610	Date / Time:	Date / Time:
Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Dominion Environmental Consultants NV, Inc. 150 N. Durango Drive, Las Vegas, NV 89145	Client No.:
PO / Job#: 170Tele NV12526.217	Date: 1.17.24
Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / 5Day	
☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer	
☐ PLM: ☒ Standard / ☐ Point Count 400 - 1000 / ☐ CARB 435	
Contact: Benjamin Bojda	Phone: (702) 368-2700
☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402 ☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield ☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight % ☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)	
E-mail: bbojda@dominion-env.com	
Site Name: CCFD Training Center	☐ IAQ Particle Identification ☐ Limited Particle ID (Wildfire) ☐ Opaques/Char (Wildfire) ☐ Special Project
Site Location: 4425 W. Tropicana Ave	☐ Metals Analysis Matrix: Analytes: Method:
Comments:	☐ Silica in Air ☐ w/Gravimetry ☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
PLM 211-213	1.17.24	Bldg 4- 2'x2' white smooth ceiling tile	A P C				
214-216		- red carpet wall tile + mastic	A P C				
217-219		- grey wallpaper drywall system	A P C				
220-222		- cream 12"x12" VFT + mastic	A P C				
223-225		- black 4" vinyl cove base + mastic	A P C				
226-228		- blue 12"x12" VFT + mastic	A P C				
229-231		- cmu block	A P C				
232-234		- mortar	A P C				
235-237		- sidewalk concrete	A P C				
238-240		- red 4"x12" ceramic tile	A P C				

Sampled By: Benjamin/Daniel Date/Time: 1.17.24 Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By: Date / Time: 1.17.24 16:09	Relinquished By: Date / Time:	Relinquished By: Date / Time:
Received By: Date / Time: 1/17/24 1610 Condition Acceptable? ☐ Yes ☐ No	Received By: Date / Time: Condition Acceptable? ☐ Yes ☐ No	Received By: Date / Time: Condition Acceptable? ☐ Yes ☐ No

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Client No.:

Dominion Environmental Consultants NV, Inc.
150 N. Durango Drive, Las Vegas, NV 89145

PO / Job#: 170166 / 1V1256.217 Date: 1/17/24

Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / 5Day

☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer

☑ PLM: ☐ Standard / ☐ Point Count 400 - 1000 / ☐ CARB 435

Contact: Benjamin Bojda Phone: (702) 368-2700

E-mail: bbojda@dominion-env.com

☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402
☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield
☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight %
☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)

Site Name: CCFD Training Center

☐ IAQ Particle Identification ☐ Opaques/Char (Wildfire)
☐ Limited Particle ID (Wildfire) ☐ Special Project

Site Location: 4425 W. Tropicana Ave

☐ Metals Analysis Matrix: Method: Analytes:

Comments:

☐ Silica in Air ☐ w/Gravimetry
☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
PLM 241-243	1/17/24	Bldg #4 - Black grout	A P C				
244-246		- Beige Stucco	A P C				
247-249		- Roof roll-on	A P C				
250-252		- PVC w/drywall & Foam	A P C				
		- Vent caulk	A P C				
			A P C				
			A P C				
			A P C				
			A P C				
			A P C				
			A P C				
			A P C				

Sampled By: Benjamin Bojda Date/Time: 1/17/24

Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By:	Relinquished By:	Relinquished By:
Date / Time: 1.17.24 16:09	Date / Time:	Date / Time:
Received By:	Received By:	Received By:
Date / Time: 1/17/24 1610	Date / Time:	Date / Time:
Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No

SECTION 7

♦

ASBESTOS-CONTAINING MATERIALS LOCATION MAP

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

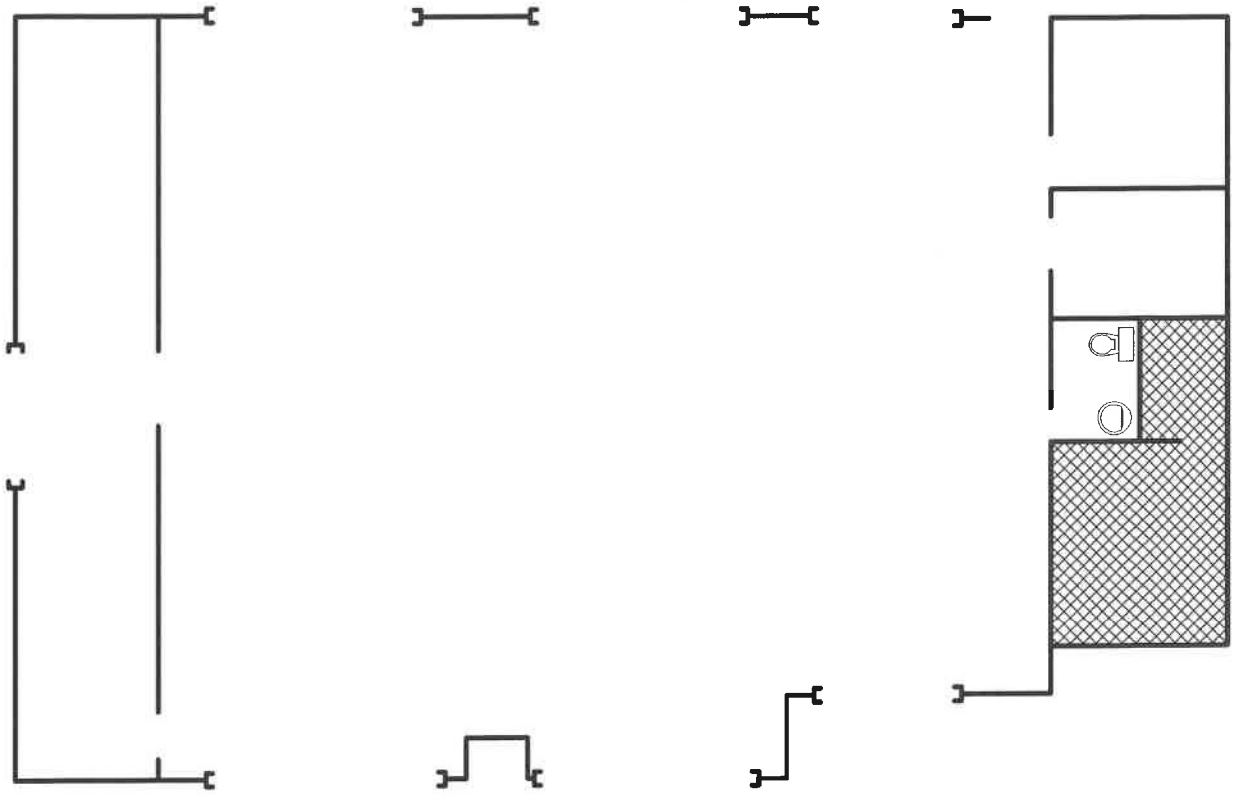

Asbestos-Containing -
Black Floor Mastic - 3% Chrysotile

Asbestos-Containing Materials Location Map
New Fire Training Center - Shop/Maintenance Building 3
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

EXHIBIT F - GEOTECHNICAL AND ENVIRONMENTAL REPORTS - ASBESTOS AND LEAD REPORT

Not to Scale

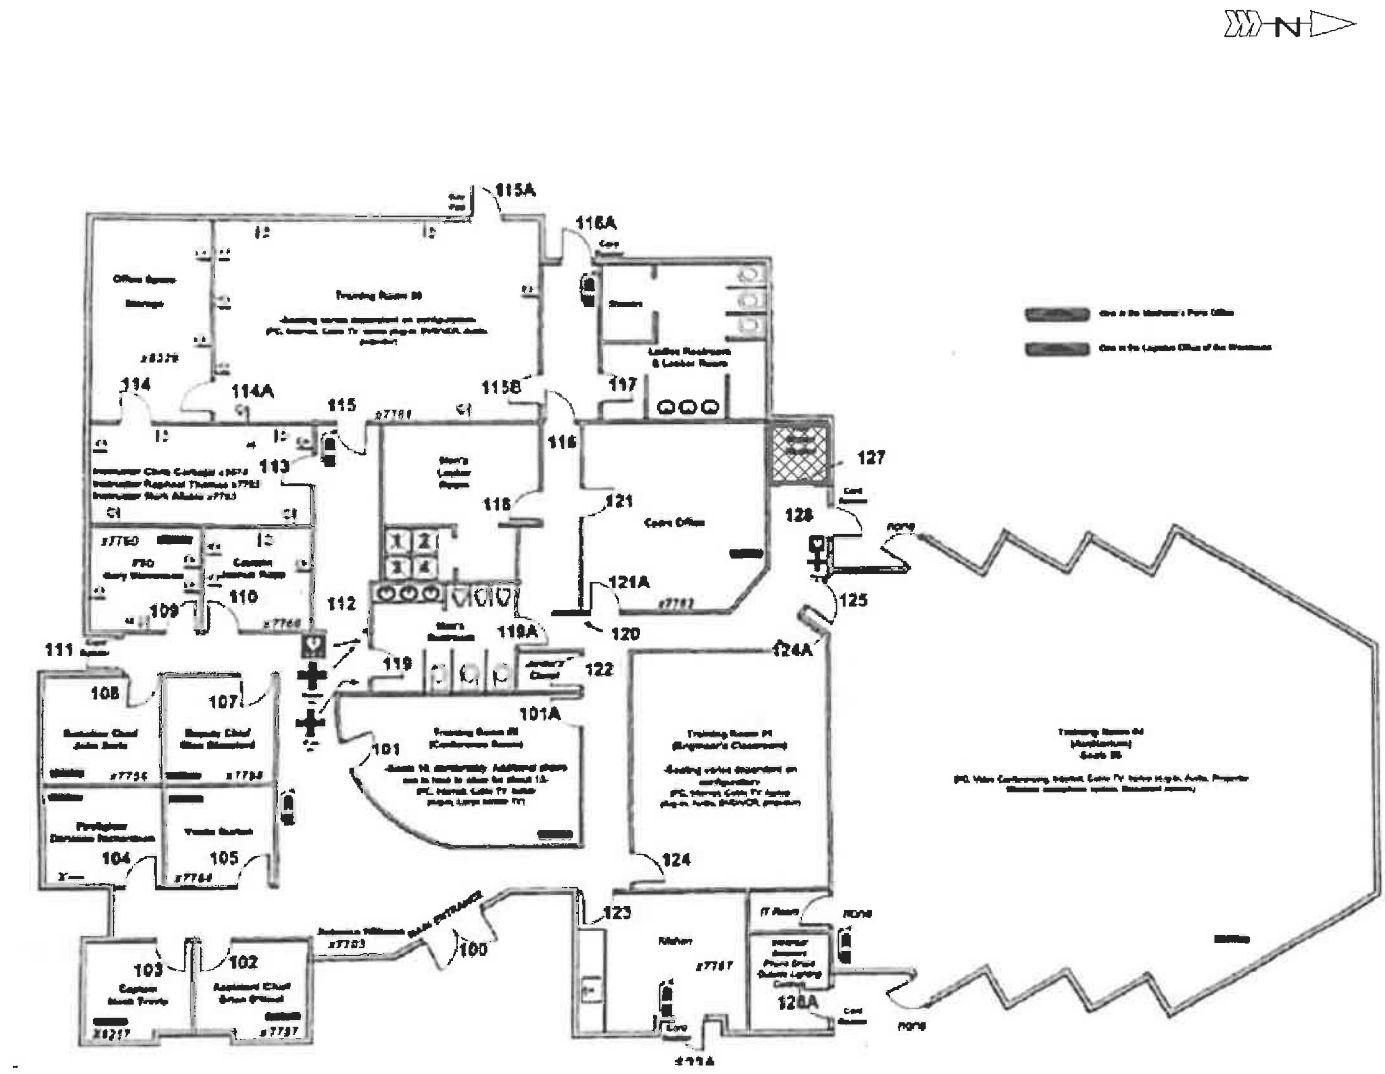

Asbestos-Containing
Black Floor Mastic - 5% Chrysotile

Asbestos Containing Materials Location Map
New Fire Training Center - Building 4 - Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Project No. NV1256.217

DOMINION ENVIRONMENTAL CONSULTANTS NV, INC.
150 North Durango Drive, Suite 190, Las Vegas, Nevada 89145
Office: (702) 368-2700 Fax: (702) 368-2707

SECTION 8

♦

TEM LABORATORY ANALYSIS REPORT

Final

SGS FORENSIC LABORATORIES

ASBESTOS ANALYSIS REPORT
SEMI-QUANTITATIVE BULK (CHATFIELD)
Transmission Electron Microscopy

Client Name:	Dominion Environmental Consultants	Page:	1/1
Contact:	Ben Bajda	Client Number:	L2118
Address:	150 N. Durango Dr., Suite 190	Report Number:	T037160
City,State,Zip:	LasVegas, NV 89145	Date Received:	1/26/2024

Site:	CCFD Training Center	Analyst:	K Buehler
Location:	4425 W. Tropicana Ave.	Date Analyzed:	2/1/2024
P.O. #:	170166 1256.217	Date Printed:	2/1/2024
Dates collected:	1/17/2024		

ANALYTICAL RESULTS

Client Sample Number	Lab Sample Number	Organic Weight Percent	Acid-Soluble Weight Percent	Residue Weight Percent	**Asbestos Weight Percent**	Asbestos Type(s) Detected*
PLM-16	94002883	72.73%	25.21%	2.07%	**<0.001%**	ND
PLM-88	94002884	49.90%	48.04%	2.06%	**<0.001%**	ND
PLM-124	94002885	15.09%	69.00%	15.92%	**<0.001%**	ND
PLM-220	94002886	15.21%	68.50%	16.29%	**<0.001%**	ND
PLM-226	94002887	19.33%	75.50%	5.17%	**<0.001%**	ND

TEM: JEOL 100 CX II EDXA: Kevex/Noran 6 Mag: 20,000x

Karen Buehler

Karen Buehler, Analytical Microscopy Supervisor

* Asbestos types: CH=chrysotile; AM=amosite; CR=crocidolite; AC=actinolite; TR=tremolite; AN=anthophyllite; ND=none detected.

Samples were received in acceptable condition unless otherwise noted. Analytical results and reports are generated by SGS Forensic Laboratories (SGS-FL) at the request of and for the exclusive use of the person or entity (Client) named on such report. Results, reports or copies of same will not be released by SGS-FL to any third party without prior written request from Client. This report applies only to the sample(s) tested, and results are not blank-corrected unless otherwise noted. Supporting laboratory documentation is available upon request. This report must not be reproduced except in full with approval from SGS-FL. The Client is solely responsible for the use and interpretation of test results and reports requested from SGS-FL. This report must not be used by the Client to claim product endorsement by

NVLAP or any U.S. government agency. SGS-FL is unable to assess the degree of hazard resulting from materials analyzed. SGS-FL reserves the right to dispose of all samples after a period of 30 days, according to all state and federal guidelines, unless otherwise specified.

SECTION 9

♦

TCLP LABORATORY ANALYSIS REPORT

Metals Analysis of TCLP Extract

Dominion Environmental Consultants
Ben Bojda
150 N. Durango Dr.
Suite 190
Las Vegas, NV 89145

Client ID: L2118
Report Number: M257070
Date Received: 01/18/24
Date Analyzed: 01/25/24
Date Printed: 01/25/24
First Reported: 01/25/24

Job ID / Site: 170167 / NV1256.217; CCFD Training Center; 4425 W Tropicana Ave
Date(s) Collected: 01/17/2024

SGSFL Job ID: L2118
Total Samples Submitted: 4
Total Samples Analyzed: 4

Sample Number	Lab Number	Analyte	Result	Result Units	Reporting Limit*	Method Reference
TCLP 1	LM265292	Pb	< 0.3	mg/l	0.3	TCLP EPA 1311/7000B
TCLP 2	LM265293	Pb	< 0.3	mg/l	0.3	TCLP EPA 1311/7000B
TCLP 3	LM265294	Pb	< 0.3	mg/l	0.3	TCLP EPA 1311/7000B
TCLP 4	LM265295	Pb	< 0.3	mg/l	0.3	TCLP EPA 1311/7000B

* The Reporting Limit represents the lowest amount of analyte that the laboratory can confidently detect in the sample, and is not a regulatory level. The Units for the Reporting Limit are the same as the Units for the Final Results.

Beatriz Hinojosa, Laboratory Supervisor, Carson Laboratory

Analytical results and reports are generated by SGS at the request of and for the exclusive use of the person or entity (client) named on such report. Results, reports or copies of same will not be released by SGS to any third party without prior written request from client. This report applies only to the sample(s) tested. Supporting laboratory documentation is available upon request. This report must not be reproduced except in full, unless approved by SGS. The client is solely responsible for the use and interpretation of test results and reports requested from SGS. SGS is not able to assess the degree of hazard resulting from materials analyzed. SGS reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified. Any modifications that have been made to referenced test methods are documented in SGS Standard Operating Procedures Manual. Quality control and sample receipt condition were acceptable unless otherwise noted.

20535 South Belshaw Avenue, Carson, CA 90746 | phone: 310.763.2374 / 800.813.9417 Fax: 310.763.4450 | https://falaboratories.sgs.com

SGS FORENSIC LABORATORIES

Analysis Request Form (COC)

Client Name & Address: Client No.: L2118

Dominion Environmental Consultants NV, Inc.
150 N. Durango Drive, Las Vegas, NV 89145

PO / Job#: 170167/NV1256.247 Date: 1.17.24

Turn Around Time: Same Day / 1Day / 2Day / 3Day / 4Day / 5Day

☐ PCM: ☐ NIOSH 7400A / ☐ NIOSH 7400B ☐ Rotometer

☐ PLM: ☐ Standard / ☐ Point Count 400 - 1000 / ☐ CARB 435

Contact: Benjamin Bojda Phone: (702) 368-2700

E-mail: bbojda@dominion-env.com

☐ TEM Air: ☐ AHERA / ☐ Yamate2 / ☐ NIOSH 7402
☐ TEM Bulk: ☐ Quantitative / ☐ Qualitative / ☐ Chatfield
☐ TEM Water: ☐ Potable / ☐ Non-Potable / ☐ Weight %
☐ TEM Dust: ☐ D5755 (microvac) / ☐ D6480 (wipe)

Site Name: CCFD Training Center

☐ IAQ Particle Identification ☐ Opaques/Char (Wildfire)
☐ Limited Particle ID (Wildfire) ☐ Special Project

Site Location: 4425 W. Tropicana Ave

☑ Metals Analysis Matrix: Method: TCLP
Analytes: (Lead) Flame AA

Comments:

☐ Silica in Air ☐ w/Gravimetry
☐ Quartz Only

Sample ID	Date / Time	Sample Location / Description	FOR AIR SAMPLES ONLY: Type	Time On/Off	Avg LPM	Total Time	Sample Area / Air Volume
TCLP 1	1.17.24	Bldg 1	A P C				
2		Bldg 2	A P C				
3		Bldg 3	A P C				
4		Bldg 4	A P C				
			A P C				
			A P C				
			A P C				
			A P C				
			A P C				
			A P C				

Shipped By: Date/Time: 1.17.24 Shipped Via: ☐ Fed Ex ☐ UPS ☐ US Mail ☐ Courier ☐ Drop Off ☐ Other:

Relinquished By:	Relinquished By:	Relinquished By:
Date / Time: 1.19.24 16:13	Date / Time: 1/18/24 (5pm)	Date / Time:
Received By:	Received By:	Received By:
Date / Time: 1/17/24 1614	Date / Time: 1/19/24 10:12 F/E	Date / Time:
Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No	Condition Acceptable? ☐ Yes ☐ No

SECTION 10

♦

EPA NESHAP NOTIFICATION INFORMATION SHEET

EPA NESHAP NOTIFICATION INFORMATION SHEET

New Fire Training Center
4425 West Tropicana Avenue
Las Vegas, Nevada 89103

Property Owner	Clark County, Nevada (Fire Dept)
Inspection Date	January 16 and 17, 2024
Laboratory	SGS Forensic Laboratories
Number of Samples	252 PLM
Dates Analyzed	January 24, 2024
Inspector Certification	
Name	Lanie Dakin
Training Provider	The Asbestos Institute
AHERA Certificate Number	4380-15844-050323
Expiration Date	May 3, 2024
Name	Benpeng Lin
Training Provider	The Asbestos Institute
AHERA Certificate Number	ON-4644-7268-051923
Expiration Date	May 19, 2024

The sampled building materials outlined in the following table were reported by laboratory PLM analysis to contain >1% asbestos.

TABLE 2 – PLM Analyzed Materials Containing >1% Asbestos

Material	Location	NESHAP Category	OSHA Classification	Estimated Quantity	Laboratory Results
12 in by 24 in. Gray Vinyl Floor Tile System **(Black Mastic)**	Building 3 – Shop & Maintenance – NE Office	Category 2	Class II	208 ft^2	3% Chrysotile
Cream 12 in. by 12 in. Vinyl Floor Tile System **(Black Mastic)**	Building 4 – Training Center – Water Heater Room	Category 2	Class II	36 ft^2	5% Chrysotile

SECTION 11

♦

GENERAL NOTES/EXCLUSIONS

GENERAL NOTES/EXCLUSIONS

- Ms. Monica Tate. Design & Construction Administrator with Clark County, Nevada, outlined the specific areas and materials scheduled to be disturbed during the upcoming demolition project, instructed Dominion to only collect bulk samples of those outlined materials, and to have those samples analyzed for the presence of asbestos fibers by a qualified laboratory.

- If any un-sampled suspect building materials are discovered during the demolition project, those materials should be properly sampled by a certified inspector and analyzed by a qualified laboratory prior to their disturbance.

- The Contractor is responsible for his own work and for compliance with all regulatory guidelines.

SECTION 12

♦

INSPECTOR CERTIFICATIONS

STATE OF NEVADA
DEPARTMENT OF BUSINESS AND INDUSTR
DIVISION OF INDUSTRIAL RELATIONS
Occupational Safety and Health Administration
Asbestos Control Program

Certifies That Lanie Dakin

is Licensed As Asbestos Abatement Consultant

License No. IM-2398 Expiration Date: 03/03/2024
Trainee

Signature Of Licensee Lanie Dakin

THE ASBESTOS INSTITUTE

Certifies that

Lanie Dakin

has attended and received instruction in the EPA approved course

AHERA Building Inspector Initial

on

May 1-3 2023

and successfully completed and passed the competency exam.

Certificate:
4380-15844-050323

Date of Examination:
03-May-2023

Date of Expiration:
03-May-2024

William T. Cavness
Director

Approved Instructor

THE ASBESTOS INSTITUTE
20033 N. 19th Ave, Building 6, Phoenix, AZ 85027
602-864-6564 – www.theasbestosinstitute.com

The person receiving this certificate has completed the requisite training for asbestos accreditation under TSCA Title II.

United States Environmental Protection Agency

This is to certify that

Lanie J Dakin

has fulfilled the requirements of the Toxic Substances Control Act (TSCA) Section 402, and has received certification to conduct lead-based paint activities pursuant to 40 CFR Part 745.226 as:

Inspector

In the Jurisdiction of:

All EPA Administered Lead-based Paint Activities Program States, Tribes and Territories

This certification is valid from the date of issuance and expires October 06, 2026

LBP-I-I251307-1
Certification #

September 22, 2023
Issued On

Adrienne Priselac, Manager, Toxics Office
Land Division

STATE OF NEVADA
DEPARTMENT OF BUSINESS AND INDUSTRY
DIVISION OF INDUSTRIAL RELATIONS
Occupational Safety and Health Administration
Asbestos Control Program

Certifies That Benpeng Lin

is Licensed As Asbestos Abatement Consultant

License No. IM-2068 Expiration Date 05/19/2024

Signature Of Licensee

THE ASBESTOS INSTITUTE

Certifies that

Benpeng Lin

has attended and received instruction in the EPA approved course

AHERA Building Inspector Refresher

on

May 19, 2023

and successfully completed and passed the competency exam.

Certificate:
ON-4644-7268-051923

Date of Examination:
19-May-2023
Date of Expiration:
19-May-2024

William T. Cavness
Director

Approved Instructor

THE ASBESTOS INSTITUTE
20033 N. 19th Ave, Building 6, Phoenix, AZ 85027
602-864-6564 – www.theasbestosinstitute.com

The person receiving this certificate has completed the requisite training for asbestos accreditation under TSCA Title II.

United States Environmental Protection Agency

This is to certify that

Benpeng Lin

has fulfilled the requirements of the Toxic Substances Control Act (TSCA) Section 402, and has received certification to conduct lead-based paint activities pursuant to 40 CFR Part 745.226 as:

Risk Assessor

In the Jurisdiction of:

All EPA Administered Lead-based Paint Activities Program States, Tribes and Territories

This certification is valid from the date of issuance and expires June 11, 2026

LBP-R-1218128-2
Certification #

March 02, 2023
Issued On

Adrienne Priselac, Manager, Toxics Office
Land Division

STATE OF NEVADA
DEPARTMENT OF BUSINESS AND INDUSTR
DIVISION OF INDUSTRIAL RELATIONS
Occupational Safety and Health Administration
Asbestos Control Program

Certifies That Benjamin Bojda
Dominion Environmental Consult
is Licensed As Asbestos Abatement Consultant

License No. IJPM-1380 Expiration Date 06/30/2024

Signature Of Licensee

THE ASBESTOS INSTITUTE

Certifies that

Benjamin Bojda

has attended and received instruction in the EPA approved course

AHERA Building Inspector Refresher

Approval Code: CA-089-06

on

June 30, 2023

and successfully completed and passed the competency exam.

Certificate:
4606-229-063023

Date of Examination:
30-Jun-2023

Date of Expiration:
30-Jun-2024

William T. Cavness
Director

Approved Instructor

THE ASBESTOS INSTITUTE
20033 N. 19th Ave, Building 6, Phoenix, AZ 85027
602-864-6564 – www.theasbestosinstitute.com

The person receiving this certificate has completed the requisite training for asbestos accreditation under TSCA Title II.

United States Environmental Protection Agency

This is to certify that

Benjamin E Bojda

has fulfilled the requirements of the Toxic Substances Control Act (TSCA) Section 402, and has received certification to conduct lead-based paint activities pursuant to 40 CFR Part 745.226 as:

Risk Assessor

In the Jurisdiction of:

All EPA Administered Lead-based Paint Activities Program States, Tribes and Territories

This certification is valid from the date of issuance and expires May 08, 2026

LBP-R-16125-3
Certification #

February 03, 2023
Issued On

Adrienne Priselac, Manager, Toxics Office
Land Division

SECTION 13

♦

LABORATORY CERTIFICATION

United States Department of Commerce
National Institute of Standards and Technology

Certificate of Accreditation to ISO/IEC 17025:2017

NVLAP LAB CODE: 200908-0

SGS Forensic Laboratories

Las Vegas, NV

is accredited by the National Voluntary Laboratory Accreditation Program for specific services, listed on the Scope of Accreditation, for:

Asbestos Fiber Analysis

This laboratory is accredited in accordance with the recognized International Standard ISO/IEC 17025:2017. This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (refer to joint ISO-ILAC-IAF Communique dated January 2009).

2023-04-01 through 2024-03-31

Effective Dates

DEPARTMENT OF COMMERCE * UNITED STATES OF AMERICA *

For the National Voluntary Laboratory Accreditation Program

National Voluntary Laboratory Accreditation Program

SCOPE OF ACCREDITATION TO ISO/IEC 17025:2017

SGS Forensic Laboratories
3620 Sunset Rd., Suite 110
Las Vegas, NV 89120
Nerissa Platon
Phone: 510-266-8183
Email: nerissa.platon@sgs.com
http://www.falaboratories.com

ASBESTOS FIBER ANALYSIS — NVLAP LAB CODE 200908-0

Bulk Asbestos Analysis

Code	*Description*
18/A01	EPA -- 40 CFR Appendix E to Subpart E of Part 763, Interim Method of the Determination of Asbestos in Bulk Insulation Samples
18/A03	EPA 600/R-93/116: Method for the Determination of Asbestos in Bulk Building Materials

For the National Voluntary Laboratory Accreditation Program

United States Department of Commerce
National Institute of Standards and Technology

Certificate of Accreditation to ISO/IEC 17025:2017

NVLAP LAB CODE: 200908-0

SGS Forensic Laboratories

Las Vegas, NV

is accredited by the National Voluntary Laboratory Accreditation Program for specific services, listed on the Scope of Accreditation, for:

Asbestos Fiber Analysis

This laboratory is accredited in accordance with the recognized International Standard ISO/IEC 17025:2017. This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (refer to joint ISO-ILAC-IAF Communique dated January 2009).

2023-04-01 through 2024-03-31

Effective Dates

DEPARTMENT OF COMMERCE * UNITED STATES OF AMERICA *

For the National Voluntary Laboratory Accreditation Program

National Voluntary Laboratory Accreditation Program

SCOPE OF ACCREDITATION TO ISO/IEC 17025:2017

SGS Forensic Laboratories
3620 Sunset Rd., Suite 110
Las Vegas, NV 89120
Nerissa Platon
Phone: 510-266-8183
Email: nerissa.platon@sgs.com
http://www.falaboratories.com

ASBESTOS FIBER ANALYSIS — NVLAP LAB CODE 200908-0

Bulk Asbestos Analysis

Code	*Description*
18/A01	EPA -- 40 CFR Appendix E to Subpart E of Part 763, Interim Method of the Determination of Asbestos in Bulk Insulation Samples
18/A03	EPA 600/R-93/116: Method for the Determination of Asbestos in Bulk Building Materials

For the National Voluntary Laboratory Accreditation Program

United States Department of Commerce
National Institute of Standards and Technology

Certificate of Accreditation to ISO/IEC 17025:2017

NVLAP LAB CODE: 101732-0

SGS Forensic Laboratories

Downers Grove, IL

is accredited by the National Voluntary Laboratory Accreditation Program for specific services, listed on the Scope of Accreditation, for:

Asbestos Fiber Analysis

This laboratory is accredited in accordance with the recognized International Standard ISO/IEC 17025:2017. This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (refer to joint ISO-ILAC-IAF Communique dated January 2009).

2023-07-01 through 2024-06-30

Effective Dates

DEPARTMENT OF COMMERCE * UNITED STATES OF AMERICA *

For the National Voluntary Laboratory Accreditation Program

National Voluntary Laboratory Accreditation Program

SCOPE OF ACCREDITATION TO ISO/IEC 17025:2017

SGS Forensic Laboratories
3020 Woodcreek Drive
Suite F
Downers Grove, IL 60515
Nerissa Platon
Phone: 510-266-8183
Email: nerissa.platon@sgs.com

ASBESTOS FIBER ANALYSIS — NVLAP LAB CODE 101732-0

Bulk Asbestos Analysis

Code	*Description*
18/A01	EPA -- 40 CFR Appendix E to Subpart E of Part 763, Interim Method of the Determination of Asbestos in Bulk Insulation Samples
18/A03	EPA 600/R-93/116: Method for the Determination of Asbestos in Bulk Building Materials

Airborne Asbestos Analysis

Code	*Description*
18/A02	U.S. EPA's "Interim Transmission Electron Microscopy Analytical Methods-Mandatory and Nonmandatory-and Mandatory Section to Determine Completion of Response Actions" as found in 40 CFR, Part 763, Subpart E, Appendix A.

For the National Voluntary Laboratory Accreditation Program

Effective 2023-07-01 through 2024-06-30

CALIFORNIA
Water Boards
STATE WATER RESOURCES CONTROL BOARD
REGIONAL WATER QUALITY CONTROL BOARDS

CALIFORNIA STATE

ENVIRONMENTAL LABORATORY ACCREDITATION PROGRAM

CERTIFICATE OF ENVIRONMENTAL LABORATORY ACCREDITATION

Is hereby granted to

SGS Forensic Laboratories

Carson

20535 Belshaw Avenue

Carson, CA 90746

Scope of the certificate is limited to the
"Fields of Accreditation"
which accompany this Certificate.

Continued accredited status depends on compliance with applicable laws and regulations, proficiency testing studies, and payment of applicable fees.

This Certificate is granted in accordance with provisions of Section 100825, et seq. of the Health and Safety Code.

Certificate No.: **1366**

Effective Date: **11/1/2022**

Expiration Date: **10/31/2024**

Sacramento, California
subject to forfeiture or revocation

Christine Sotelo, Program Manager
Environmental Laboratory Accreditation Program

CALIFORNIA STATE
ENVIRONMENTAL LABORATORY ACCREDITATION PROGRAM
Fields of Accreditation

SGS Forensic Laboratories
Carson
20535 Belshaw Avenue
Carson, CA 90746
Phone: 3107632374

Certificate Number: 1366
Expiration Date: 10/31/2024

Field of Accreditation: 103 - Toxic Chemical Elements of Drinking Water

103.130	001	Aluminum	EPA 200.7
103.130	003	Barium	EPA 200.7
103.130	004	Beryllium	EPA 200.7
103.130	007	Chromium	EPA 200.7
103.130	008	Copper	EPA 200.7
103.130	009	Iron	EPA 200.7
103.130	011	Manganese	EPA 200.7
103.130	012	Nickel	EPA 200.7
103.130	015	Silver	EPA 200.7
103.130	017	Zinc	EPA 200.7
103.160	001	Mercury	EPA 245.1

Field of Accreditation: 109 - Metals and Trace Elements in Non-Potable Water

109.623	001	Aluminum	EPA 200.7
109.623	002	Antimony	EPA 200.7
109.623	003	Arsenic	EPA 200.7
109.623	004	Barium	EPA 200.7
109.623	005	Beryllium	EPA 200.7
109.623	007	Cadmium	EPA 200.7
109.623	008	Chromium	EPA 200.7
109.623	009	Cobalt	EPA 200.7
109.623	010	Copper	EPA 200.7
109.623	011	Iron	EPA 200.7
109.623	012	Lead	EPA 200.7
109.623	013	Manganese	EPA 200.7
109.623	014	Molybdenum	EPA 200.7
109.623	015	Nickel	EPA 200.7
109.623	016	Selenium	EPA 200.7
109.623	017	Silver	EPA 200.7
109.623	018	Thallium	EPA 200.7
109.623	019	Tin	EPA 200.7
109.623	021	Vanadium	EPA 200.7
109.623	022	Zinc	EPA 200.7
109.635	001	Mercury	EPA 245.1

As of 11/8/2022 , this list supersedes all previous lists for this certificate number.
Customers: Please verify the current accreditation standing with the State.

SGS Forensic Laboratories

Certificate Number: 1366
Expiration Date: 10/31/2024

109.659	010	Lead	SM 3111 B-2011
Field of Accreditation: 114 - Inorganic Constituents in Hazardous Waste			
114.315	002	Antimony	EPA 6010 B
114.315	003	Arsenic	EPA 6010 B
114.315	004	Barium	EPA 6010 B
114.315	005	Beryllium	EPA 6010 B
114.315	007	Cadmium	EPA 6010 B
114.315	009	Chromium	EPA 6010 B
114.315	010	Cobalt	EPA 6010 B
114.315	011	Copper	EPA 6010 B
114.315	013	Lead	EPA 6010 B
114.315	016	Molybdenum	EPA 6010 B
114.315	017	Nickel	EPA 6010 B
114.315	019	Selenium	EPA 6010 B
114.315	020	Silver	EPA 6010 B
114.315	023	Thallium	EPA 6010 B
114.315	026	Vanadium	EPA 6010 B
114.315	027	Zinc	EPA 6010 B
114.365	011	Lead	EPA 7000 B
114.515	001	Lead	EPA 7420
114.535	001	Mercury	EPA 7471 A
114.545	001	Mercury	EPA 7471 B
Field of Accreditation: 115 - Leaching/Extraction Tests and Physical Characteristics of Hazardous Waste			
115.055	001	Waste Extraction Test (WET)	CCR Chapter11, Article 5, Appendix II
115.065	001	Extraction Procedure Toxicity (EPTox)	EPA 1310 A
115.085	001	Toxicity Characteristic Leaching Procedure (TCLP)	EPA 1311
115.135	001	Corrosivity - pH Determination	EPA 9045 C
Field of Accreditation: 121 - Bulk Asbestos Analysis of Hazardous Waste			
121.010	001	Bulk Asbestos	EPA 600/M4-82-020

As of 11/8/2022 , this list supersedes all previous lists for this certificate number.
Customers: Please verify the current accreditation standing with the State.

EXHIBIT G
NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE
LIST OF WORK ESTIMATED BY CMAR TO EXCEED 1% OF COST OF PUBLIC WORK

ATTACHED HERETO

Geraldine Cruz

From: Cueva, Ruben <Ruben.Cueva@whiting-turner.com>
Sent: Monday, April 6, 2026 5:03 PM
To: Geraldine Cruz
Cc: Swanson, Joseph; Crane, Zachary; Hayden, Hunter; Schmitt, Paul; Monica Tate; Dan Rakers
Subject: RE: 607319-25 New Fire Training Center & Site Improvements with Parking Garage - Construction Services Contract
Attachments: CCFTC - 1% Subcontractor Licenses.zip

Geraldine,

Below is the list of 1% subcontractors for the Training Center. Attached are the subcontractor licenses. The *TBD* scopes noted below are being re-bid due to not enough coverage per NRS.

Let me know if you have any questions or if you need anything further.

Clark County Fire Training Center
Portions of the work estimated to exceed one percent (1%) of the total project cost

CSI Division		Name of Trade
03A	Structural Concrete & Rebar	Largo Concrete, Inc.
04A	Masonry	A-1 Masonry
05A	Structural Steel	Steel Structures Inc.
05B	Metal Panels	B & B Specialties LLC
05C	Pre-Engineered Structures [PEMB]	Image Building Systems
07A	Roofing / Waterproofing	Eberhard Southwest Roofing
08B	Glass & Glazing	*TBD*
09A	Metal Framing, Drywall, Paint	Anning-Johnson Company
09B	ACT & Decorative Ceiling Panels	Performance Contracting, Inc.
10A	Burn Tower (Install Only)	WHP
21A	Fire Suppression	*TBD*
22A	Plumbing	Bombard Plumbing
23A	Mechanical	Bombard Mechanical
26A	Electrical / Low Voltage / Fire Alarm	Helix
31A	Earthwork	Maui One
32A	Site Concrete	*TBD*
33A	Wet Utilities	Maui One

Thanks,

Ruben Cueva
Project Manager
The Whiting-Turner Contracting Company
6720 Via Austi Parkway, Suite 550
Las Vegas, Nevada 89119
Mobile: 702-302-0734
Fax: 702-650-2650
www.whiting-turner.com

From: Geraldine Cruz <Geraldine.Cruz@ClarkCountyNV.gov>
Sent: Wednesday, April 1, 2026 6:57:55 AM
To: Crane, Zachary <Zac.Crane@whiting-turner.com>; Schmitt, Paul <Paul.Schmitt@Whiting-Turner.com>
Cc: Monica Tate <Monica.tate@clarkcountynv.gov>; Dan Rakers <Dan.Rakers@ClarkCountyNV.gov>
Subject: RE: 607319-25 New Fire Training Center & Site Improvements with Parking Garage - Construction Services Contract

Zac

Pursuant to NRS 338.1696, please provide the required information identifying all portions of the work estimated to exceed one percent (1%) of the total project cost, along with the names of each subcontractor selected to perform such work.

In addition, at the County's request, please provide documentation confirming that each listed subcontractor holds all required and current licenses, and that such licensure has been reviewed and validated.

From: Crane, Zachary <Zac.Crane@whiting-turner.com>
Sent: Tuesday, March 31, 2026 1:00 PM
To: Geraldine Cruz <Geraldine.Cruz@ClarkCountyNV.gov>; Schmitt, Paul <Paul.Schmitt@Whiting-Turner.com>
Cc: Monica Tate <Monica.Tate@clarkcountynv.gov>
Subject: RE: 607319-25 New Fire Training Center & Site Improvements with Parking Garage - Construction Services Contract

Thank you. We will get back to you ASAP.

Regards,

Zachary A. Crane
Division Vice President
The Whiting-Turner Contracting Company
6720 Via Austi Parkway, Suite 550
Las Vegas, Nevada 89119
Phone: 702-650-0700
Mobile: 702-604-9216
www.whiting-turner.com

From: Geraldine Cruz <Geraldine.Cruz@ClarkCountyNV.gov>
Sent: Tuesday, March 31, 2026 11:41 AM
To: Schmitt, Paul <Paul.Schmitt@Whiting-Turner.com>
Cc: Crane, Zachary <Zac.Crane@whiting-turner.com>; Monica Tate <Monica.tate@clarkcountynv.gov>
Subject: 607319-25 New Fire Training Center & Site Improvements with Parking Garage - Construction Services Contract
Importance: High

Paul

Attached is the Construction Services Contract for your review. Please let us know if you have any exceptions and provide any proposed redlines for review by our District Attorney.

Please note that, as part of the contract preparation, a Risk Assessment was conducted by County Risk Management, and the insurance requirements have been revised accordingly.

If there are no exceptions, please return the signed signature page (Page 5 of the PDF) by the end of business on Monday, April 6, or sooner.

Please acknowledge your receipt of this communication.
If you have any questions or concerns, please provide as a response to this email.

Geraldine Cruz
Purchasing Analyst
Ph: (702) 455-6277
Email: Geraldine.Cruz@Clarkcountynv.gov
Work Hours: 6:00 am – 4:30 pm
Remote: Mondays (available through email and Teams)
In office: Tuesday – Thursday

EXHIBIT H
NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE
BASELINE PROJECT SCHEDULE

ATTACHED HERETO

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
Clark County Fire Training Center Baseline Schedule		986	07/01/2024 A	05/26/2028
MILESTONES		770	05/07/2025 A	05/26/2028
Preconstruction Milestones		270	05/07/2025 A	05/29/2026
WT.MST.100	WT Awarded Pre-Con	0	05/07/2025 A	
WT.MST.105	Pre-Con PO Executed	0	05/07/2025 A	
WT.MST.115	Pre-Construction Time Period	240	05/07/2025 A	03/20/2026
WT.MST.155	Last Class Graduation 5/18/2026	74	02/02/2026 A	05/15/2026
WT.MST.135	Scope Reviews Complete	0		03/23/2026
WT.MST.125	GMP Submission & County Review	34	03/24/2026	05/11/2026
WT.MST.145	CCBD Board Meeting for GMP Review	1	05/12/2026	05/12/2026
WT.MST.300	Existing Facility Move Out & Salvage	9	05/18/2026	05/29/2026
Construction Milestones		512	05/13/2026	05/26/2028
WT.MST.110	Notice to Proceed / GMP Executed	1	05/13/2026	05/13/2026
WT.MST.120	Permanent Power Available	0		04/15/2027
WT.MST.250	Building Climatization Fire Station	0		04/15/2027
WT.MST.240	Building Climatization Maintenance Building	0		04/27/2027
WT.MST.160	Maintenance Building Certificate of Occupancy	0		07/15/2027*
WT.MST.150	Fire Station Certificate of Occupancy	0		08/12/2027*
WT.MST.230	Building Climatization Training Center	0		09/02/2027
WT.MST.170	Burn Tower Final Completion	0		09/09/2027*
WT.MST.140	Training Building Certificate of Occupancy	0		03/20/2028
WT.MST.260	WT Contingency	48	03/21/2028	05/26/2028
Durations		500	06/01/2026	05/26/2028
WT.MST.220	Construction Duration	705	06/01/2026	05/26/2028
WT.MST.180	Training Building Construction	452	08/10/2026	05/26/2028
WT.MST.210	Maintenance Building Construction	442	08/24/2026	05/26/2028
WT.MST.200	Burn Tower Construction	441	08/25/2026	05/26/2028
WT.MST.190	Fire Station Construction	437	08/31/2026	05/26/2028
Contractual Milestones		0	05/26/2028	05/26/2028
WT.MST.130	Project Final Completion	0		05/26/2028*
DESIGN/PERMITTING		698	07/01/2024 A	04/05/2027
Master Plan & Building Concepts		129	07/01/2024 A	12/31/2024 A
PS.100	Master Plan & Building Concepts	69	07/01/2024 A	10/07/2024 A
PS.110	Entitlement Submittal & Approval	87	08/28/2024 A	12/31/2024 A
Schematic Design		90	01/06/2025 A	05/12/2025 A
SD.100	Schematic Design Phase	51	01/06/2025 A	03/17/2025 A
SD.110	Owner Review	6	03/17/2025 A	03/24/2025 A
SD.120	CMAR Estimate	11	03/17/2025 A	03/31/2025 A
SD.130	Project Page Turn (TBD)	1	05/12/2025 A	05/12/2025 A
30% Design Development		58	05/27/2025 A	07/02/2025 A
DD.30.100	30% Design Development	47	03/26/2025 A	06/02/2025 A
DD.30.110	30% DD Owner Review	6	06/02/2025 A	06/09/2025 A
DD.30.120	30% DD CMAR Estimate	11	06/02/2025 A	07/02/2025 A
DD.30.130	30% DD Project Page Turn	1	07/02/2025 A	07/02/2025 A
60% Construction Documents		82	07/03/2025 A	10/20/2025 A
CD.60.100	60% Construction Documents	58	07/03/2025 A	09/16/2025 A
CD.60.110	60% CD Owner Review	6	09/17/2025 A	09/24/2025 A
CD.60.120	60% CD CMAR Estimate	10	09/25/2025 A	10/17/2025 A
CD.60.130	60% CD Project Page Turn (TBD)	1	10/20/2025 A	10/20/2025 A
95% Construction Documents		80	10/20/2025 A	12/31/2025 A
CD.95.100	95% Construction Documents	39	10/20/2025 A	12/19/2025 A
CD.95.110	95% CD Owner Review	6	12/22/2025 A	12/30/2025 A
CD.95.130	95% CD Project Page Turn (TBD)	1	12/22/2025 A	12/22/2025 A
CD.95.120	95% Final County Drawing Updates	5	12/24/2025 A	12/31/2025 A
100% Construction Documents		25	01/02/2026 A	02/05/2026 A
CD.100.100	100% Construction Documents Bid Set for GMP & CCBD Submission	25	01/02/2026 A	02/05/2026 A

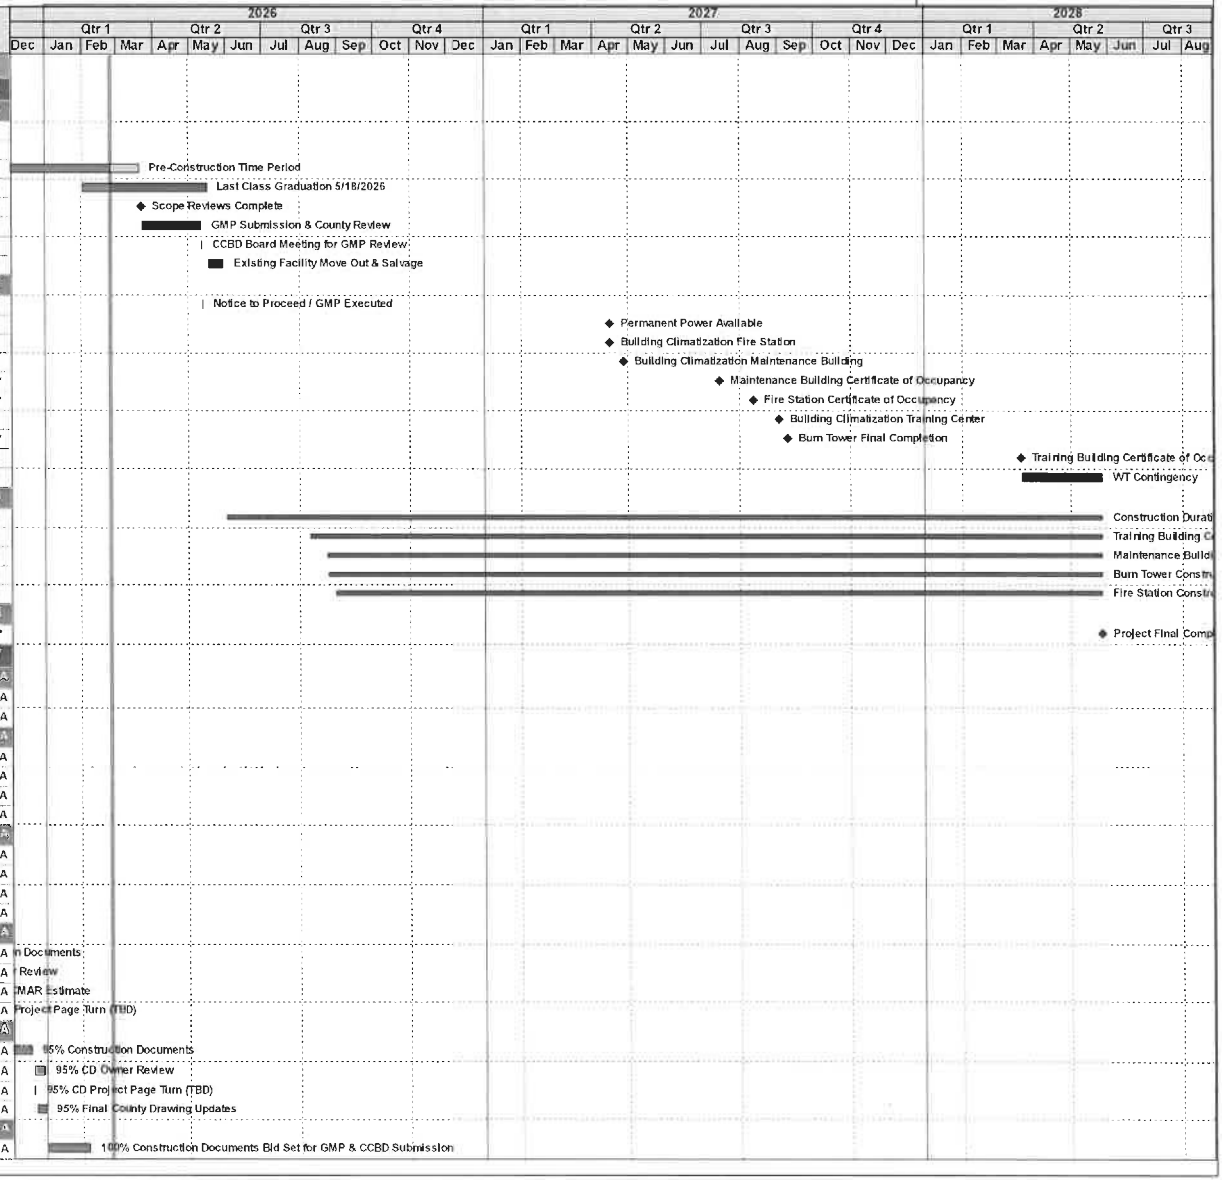

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
Civil		91	01/02/2026 A	05/11/2026
CIV.100	Complete Civil Drawings	5	01/02/2026 A	01/08/2026 A
CIV.110	Submit Civil Drawings	5	01/09/2026 A	01/09/2026 A
CIV.120	CCBD Review/Comment on Civil Drawings (NVE)	60	01/12/2026 A	04/06/2026
CIV.130	A/E Respond/Review CCBD Comments on Civil Drawings (NVE)	5	04/07/2026	04/13/2026
CIV.150	Resubmit Civil Drawings to CCBD	20	04/14/2026	05/11/2026
CIV.140	Receive Approved Civil Drawings	0		05/11/2026
Building		91	01/02/2026 A	05/11/2026
BLD.100	Complete Permit Drawings	5	01/02/2026 A	01/08/2026 A
BLD.110	Submit Permit Drawings	5	01/09/2026 A	01/09/2026 A
BLD.120	CCBD Review/Comment on Permit Drawings	60	01/12/2026 A	04/06/2026
BLD.130	A/E Respond/Review CCBD on Permit Drawings	5	04/07/2026	04/13/2026
BLD.150	Resubmit Permit Drawings to CCBD	20	04/14/2026	05/11/2026
BLD.140	Receive Building Permit	0		05/11/2026
Demolition		48	01/02/2026 A	03/10/2026
DES.DEM.100	Demo Permit Process	20	01/02/2026 A	03/10/2026
DES.DEM.110	Demo Permit	0		03/10/2026
NVE Design		280	11/13/2025 A	12/29/2026
NVE.100	NVE Scope Confirmation Meeting (NVE/Owner)	20	11/13/2025 A	12/12/2025 A
NVE.110	Service Level Agreement	40	12/15/2025 A	03/10/2026
NVE.120	NVE Internal Review & Design Approval Agreement (NVE/Owner)	15	03/11/2026	04/01/2026
NVE.130	Customer Review & Return DAA	20	04/02/2026	04/29/2026
NVE.140	Apply & Receive Easement Permit	15	04/30/2026	05/20/2026
NVE.150	Line Extension Agreement	10	05/21/2026	06/04/2026
NVE.160	Customer Approval of LEA	90	06/05/2026	10/13/2026
NVE.170	Construction Coordination & Scheduling	30	10/14/2026	11/30/2026
NVE.180	NVE Onsite Pull Wire / Transformer	10	12/01/2026	12/14/2026
NVE.190	Meter Set	10	12/15/2026	12/29/2026
Deferred Design		566	11/03/2025 A	04/05/2027
PEMB		244	11/03/2025 A	10/21/2026
DES.PMB.100	PEMB NTP/PO to Start Design	7	11/03/2025 A	11/11/2025 A
DES.PMB.110	PEMB Design Coordination	66	11/11/2025 A	03/24/2026
DES.PMB.130	Submit PEMB Design to CCBD	1	03/25/2026	03/25/2026
DES.PMB.140	CCBD Review of PEMB	60	03/26/2026	06/22/2026
DES.PMB.150	A/E Respond/Review CCBD Comments PEMB Design	5	06/23/2026	06/29/2026
DES.PMB.170	Resubmit PEMB Design to CCBD	20	06/30/2026	07/28/2026
DES.PMB.160	Receive PEMB Permit	0		07/28/2026
DES.PMB.180	PEMB Procurement	60	07/29/2026	10/21/2026
Burn Tower OFCI		278	02/25/2026	04/05/2027
DES.BT.120	Burn Tower Receive NTP	6	02/25/2026	03/04/2026
DES.BT.100	Burn Tower NTP/PO to Start Design	1	03/05/2026	03/05/2026
DES.BT.110	Burn Tower Design Coordination	70	03/06/2026	06/15/2026
DES.BT.130	Submit Burn Tower Design to CCBD	1	06/16/2026	06/16/2026
DES.BT.140	CCBD Review of Burn Tower	60	06/17/2026	09/11/2026
DES.BT.180	Burn Tower Procurement	200	06/17/2026	04/05/2027
DES.BT.150	A/E Respond/Review CCBD Comments Burn Tower Design	5	09/14/2026	09/18/2026
DES.BT.160	Resubmit Burn Tower Design to CCBD	20	09/21/2026	10/16/2026
DES.BT.170	Receive Burn Tower Permit	0		10/16/2026
Southwest Gas		30	02/25/2026	04/08/2026
SWG.100	Southwest Gas Service Agreement	5	02/25/2026	03/03/2026
SWG.110	Review Design Approval Agreement	5	03/04/2026	03/10/2026
SWG.120	Easement Approval	5	03/11/2026	03/17/2026
SWG.130	Construction Coordination Scheduling	5	03/18/2026	03/24/2026
SWG.140	Southwest Gas Install	5	03/25/2026	04/01/2026
SWG.150	Gas Meter Set	5	04/02/2026	04/08/2026
PRECONSTRUCTION		402	02/06/2026 A	09/10/2027
Sub/Supplier Bidding & Award		93	02/06/2026 A	06/26/2026

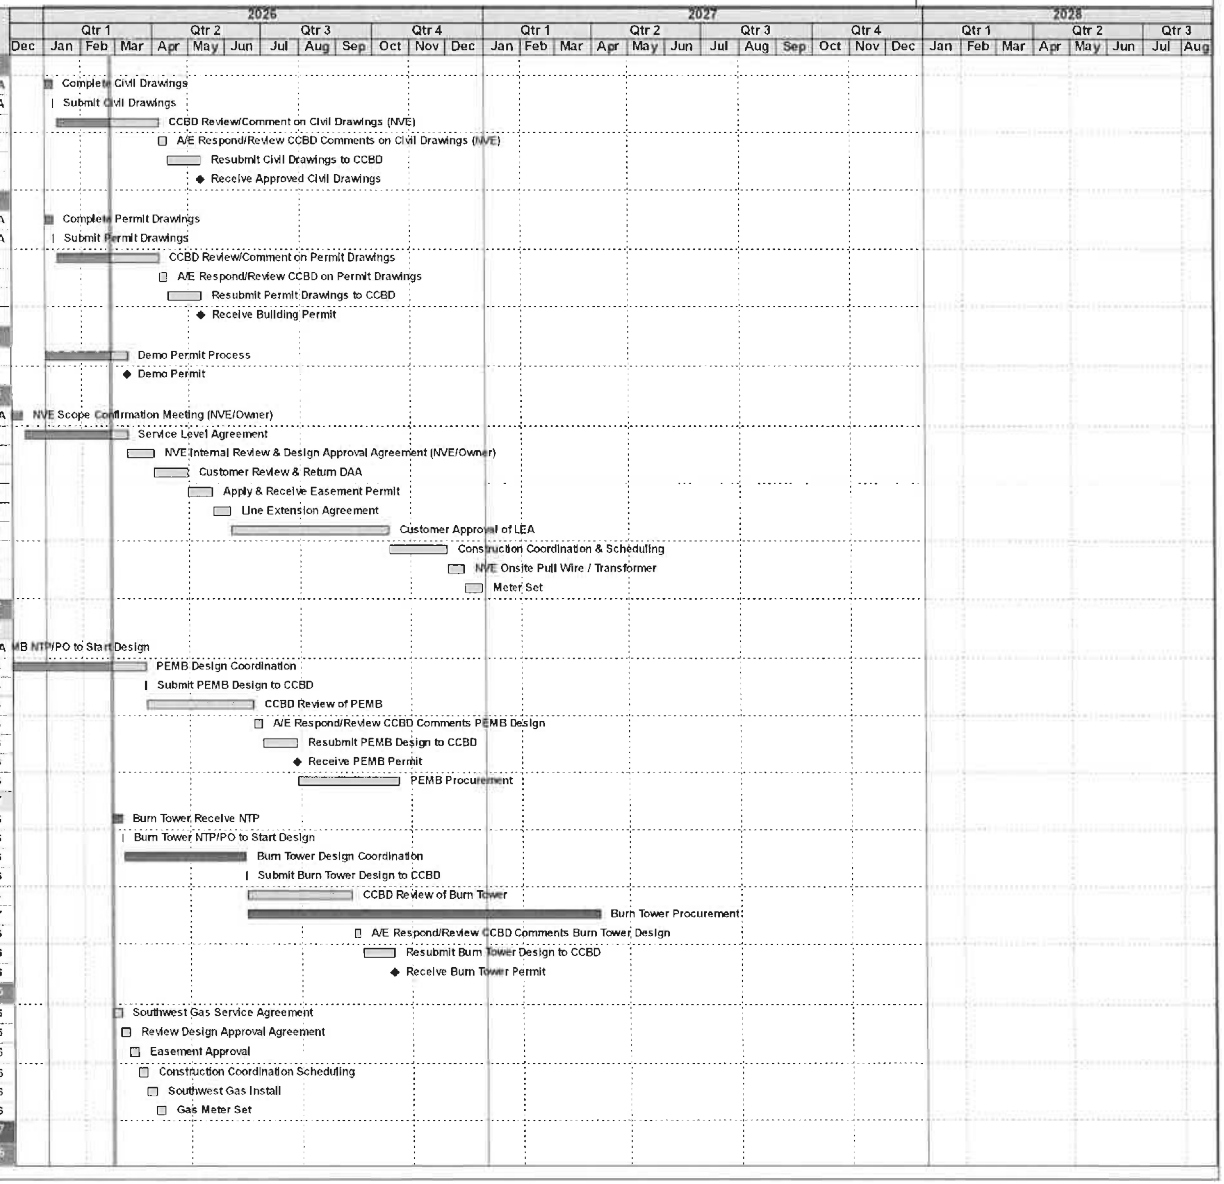

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
Priority 1 Subcontractors		98	02/06/2026 A	06/26/2026
AWD-1000	Subcontractor Priority 1	10	05/13/2026	05/27/2026
AWD-1010	Subcontractor Priority 2	20	05/14/2026	06/11/2026
AWD-1020	Subcontractor Priority 3	30	05/14/2026	06/26/2026
02A - Survey		77	02/06/2026 A	05/27/2026
BUY.02A.100	Survey 02A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.02A.110	Survey 02A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.02A.120	Survey 02A - Subcontractor Award	0		05/27/2026
02B - Demo		77	02/06/2026 A	05/27/2026
BUY.02B.100	Demo 02B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.02B.110	Demo 02B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.02B.120	Demo 02B - Subcontractor Award	0		05/27/2026
03A - Concrete		88	02/06/2026 A	06/11/2026
BUY.03A.100	Concrete 03A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.03A.120	Concrete 03A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.03A.150	Concrete 03A - Subcontractor Award	0		06/11/2026
03A - Reinforcement		77	02/06/2026 A	05/27/2026
BUY.03A.110	Reinforcement 03A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.03A.130	Reinforcement 03A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.03A.140	Reinforcement 03A - Subcontractor Award	0		05/27/2026
04A - Masonry		77	02/06/2026 A	05/27/2026
BUY.04A.100	Masonry 04A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.04A.110	Masonry 04A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.04A.120	Masonry 04A - Subcontractor Award	0		05/27/2026
05A - Structural Steel		77	02/06/2026 A	05/27/2026
BUY.05A.100	Structural Steel 05A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.05A.110	Structural Steel 05A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.05A.120	Structural Steel 05A - Subcontractor Award	0		05/27/2026
05D - PEMB		77	02/06/2026 A	05/27/2026
BUY.05D.100	PEMB 05D - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.05D.110	PEMB 05D - WT Scope Review	10	03/10/2026	03/23/2026
BUY.05D.120	PEMB 05D - Subcontractor Award	0		05/27/2026
14A - Elevator		77	02/06/2026 A	05/27/2026
BUY.14A.100	Elevator 14A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.14A.110	Elevator 14A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.14A.120	Elevator 14A - Subcontractor Award	0		05/27/2026
21A - Fire Suppression		77	02/06/2026 A	05/27/2026
BUY.21A.100	Fire Suppression 21A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.21A.110	Fire Suppression 21A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.21A.120	Fire Suppression 21A - Subcontractor Award	0		05/27/2026
22A - Plumbing		77	02/06/2026 A	05/27/2026
BUY.22A.100	Plumbing 22A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.22A.110	Plumbing 22A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.22A.120	Plumbing 22A - Subcontractor Award	0		05/27/2026
23A - HVAC		77	02/06/2026 A	05/27/2026
BUY.23A.100	HVAC 23A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.23A.120	HVAC 23A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.23A.140	HVAC 23A - Subcontractor Award	0		05/27/2026
23A - Plymovent		77	02/06/2026 A	05/27/2026
BUY.23A.110	Plymovent 23A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.23A.130	Plymovent 23A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.23A.150	Plymovent 23A - Subcontractor Award	0		05/27/2026
26A - Electrical		77	02/06/2026 A	05/27/2026
BUY.26A.100	Electrical 26A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.26A.110	Electrical 26A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.26A.120	Electrical 26A - Subcontractor Award	0		05/27/2026
28B - Fire Alarm		77	02/06/2026 A	05/27/2026
BUY.28B.100	Fire Alarm 28B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026

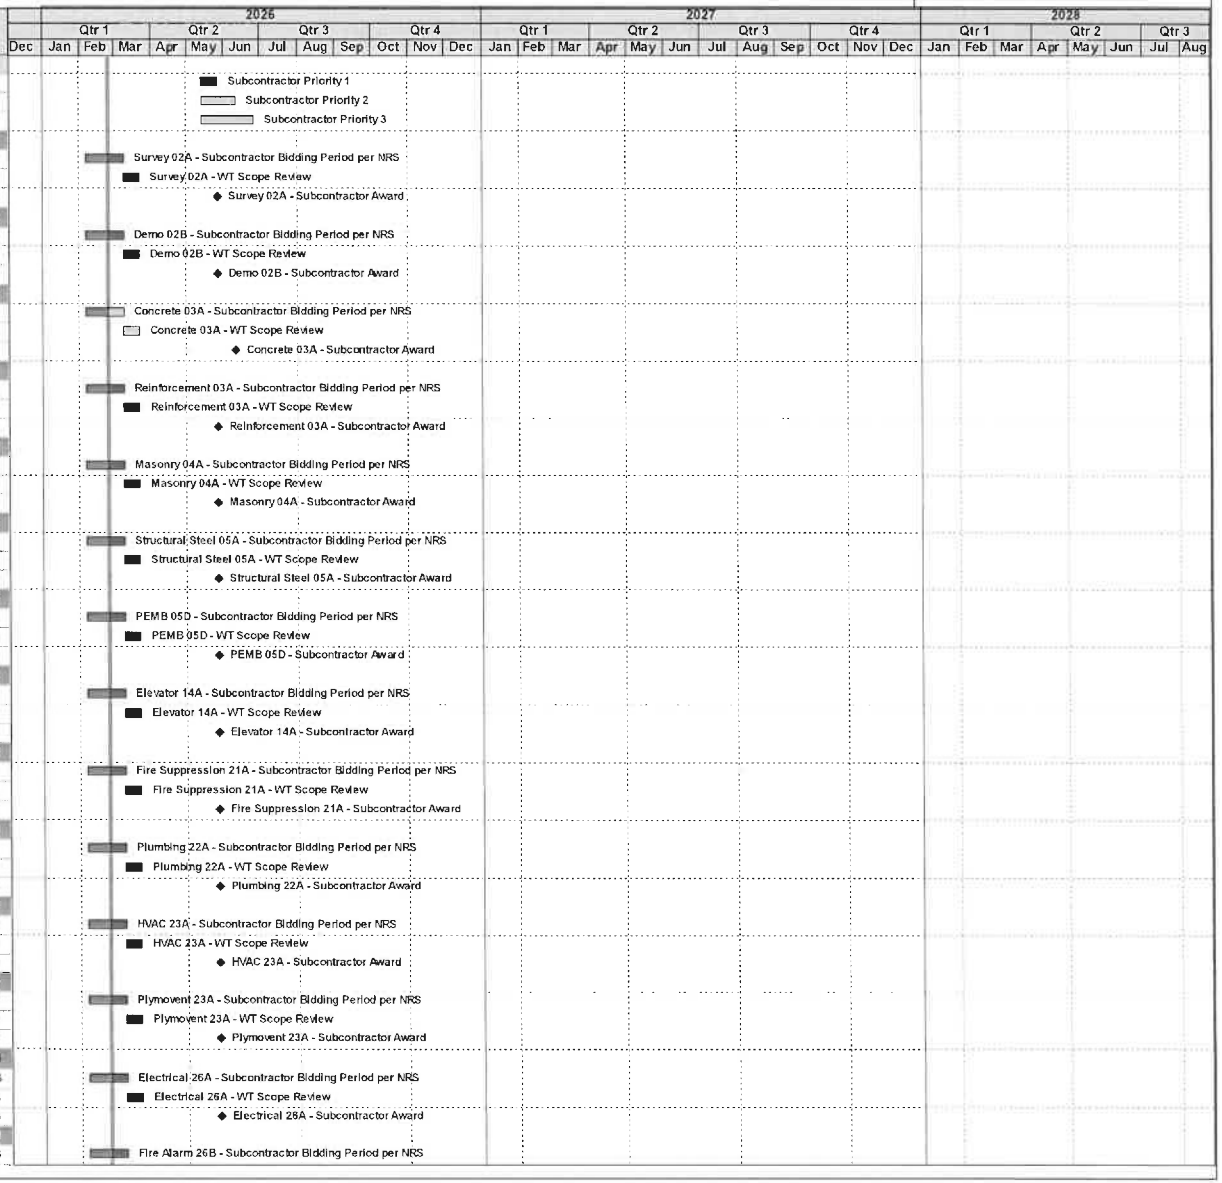

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
BUY.26B.110	Fire Alarm 26B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.26B.120	Fire Alarm 26B - Subcontractor Award	0		05/27/2026
31A - Earthwork		77	02/06/2026 A	05/27/2026
BUY.31A.100	Earthwork 31A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.31A.110	Earthwork 31A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.31A.120	Earthwork 31A - Subcontractor Award	0		05/27/2026
32A - Landscaping		77	02/06/2026 A	05/27/2026
BUY.32A.100	Landscaping 32A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.32A.110	Landscaping 32A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.32A.120	Landscaping 32A - Subcontractor Award	0		05/27/2026
32B - Site Concrete		98	02/06/2026 A	06/26/2026
BUY.32B.100	Site Concrete 32B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.32B.110	Site Concrete 32B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.32B.120	Site Concrete 32B - Subcontractor Award	0		06/26/2026
32C - Site Fencing		77	02/06/2026 A	05/27/2026
BUY.05C.100	Site Fencing 05C - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.05C.110	Site Fencing 05C - WT Scope Review	10	03/10/2026	03/23/2026
BUY.05C.120	Site Fencing 05C - Subcontractor Award	0		05/27/2026
33A - Utilities		77	02/06/2026 A	05/27/2026
BUY.33A.100	Utilities 33A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.33A.110	Utilities 33A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.33A.120	Utilities 33A - Subcontractor Award	0		05/27/2026
Priority 2 Subcontractors		88	02/06/2026 A	06/11/2026
07B - Insulation		88	02/06/2026 A	06/11/2026
BUY.07B.100	Insulation 07B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.07B.110	Insulation 07B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.07B.120	Insulation 07B - Subcontractor Award	0		06/11/2026
07D - Roofing		88	02/06/2026 A	06/11/2026
BUY.07D.100	Roofing 07D - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.07D.110	Roofing 07D - WT Scope Review	10	03/10/2026	03/23/2026
BUY.07D.120	Roofing 07D - Subcontractor Award	0		06/11/2026
08A - Hollow Metal Doors		88	02/06/2026 A	06/11/2026
BUY.08A.100	Hollow Metal Doors 08A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.08A.110	Hollow Metal Doors 08A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.08A.120	Hollow Metal Doors 08A - Subcontractor Award	0		06/11/2026
08B - Overhead Doors		88	02/06/2026 A	06/11/2026
BUY.08B.100	Overhead Doors 08B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.08B.110	Overhead Doors 08B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.08B.120	Overhead Doors 08B - Subcontractor Award	0		06/11/2026
08C - Storefront & Windows		88	02/06/2026 A	06/11/2026
BUY.08C.100	Storefront & Windows 08C - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.08C.110	Storefront & Windows 08C - WT Scope Review	10	03/10/2026	03/23/2026
BUY.08C.120	Storefront & Windows 08C - Subcontractor Award	0		06/11/2026
09A - Framing & Drywall		88	02/06/2026 A	06/11/2026
BUY.09A.100	Framing & Drywall 09A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.09A.110	Framing & Drywall 09A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.09A.120	Framing & Drywall 09A - Subcontractor Award	0		06/11/2026
10A - Signage & Graphics		88	02/06/2026 A	06/11/2026
BUY.10A.100	Signage & Graphics 10A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.10A.110	Signage & Graphics 10A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.10A.120	Signage & Graphics 10A - Subcontractor Award	0		06/11/2026
11A - Appliances		88	02/06/2026 A	06/11/2026
BUY.11A.100	Appliances 11A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.11A.110	Appliances 11A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.11A.120	Appliances 11A - Subcontractor Award	0		06/11/2026
12B - Maintenance Building Equipment		88	02/06/2026 A	06/11/2026
BUY.12B.100	Maintenance Building Equipment 12B - Subcontractor Bidding Period	17	02/06/2026 A	03/09/2026
BUY.12B.110	Maintenance Building Equipment 12B - WT Scope Review	10	03/10/2026	03/23/2026

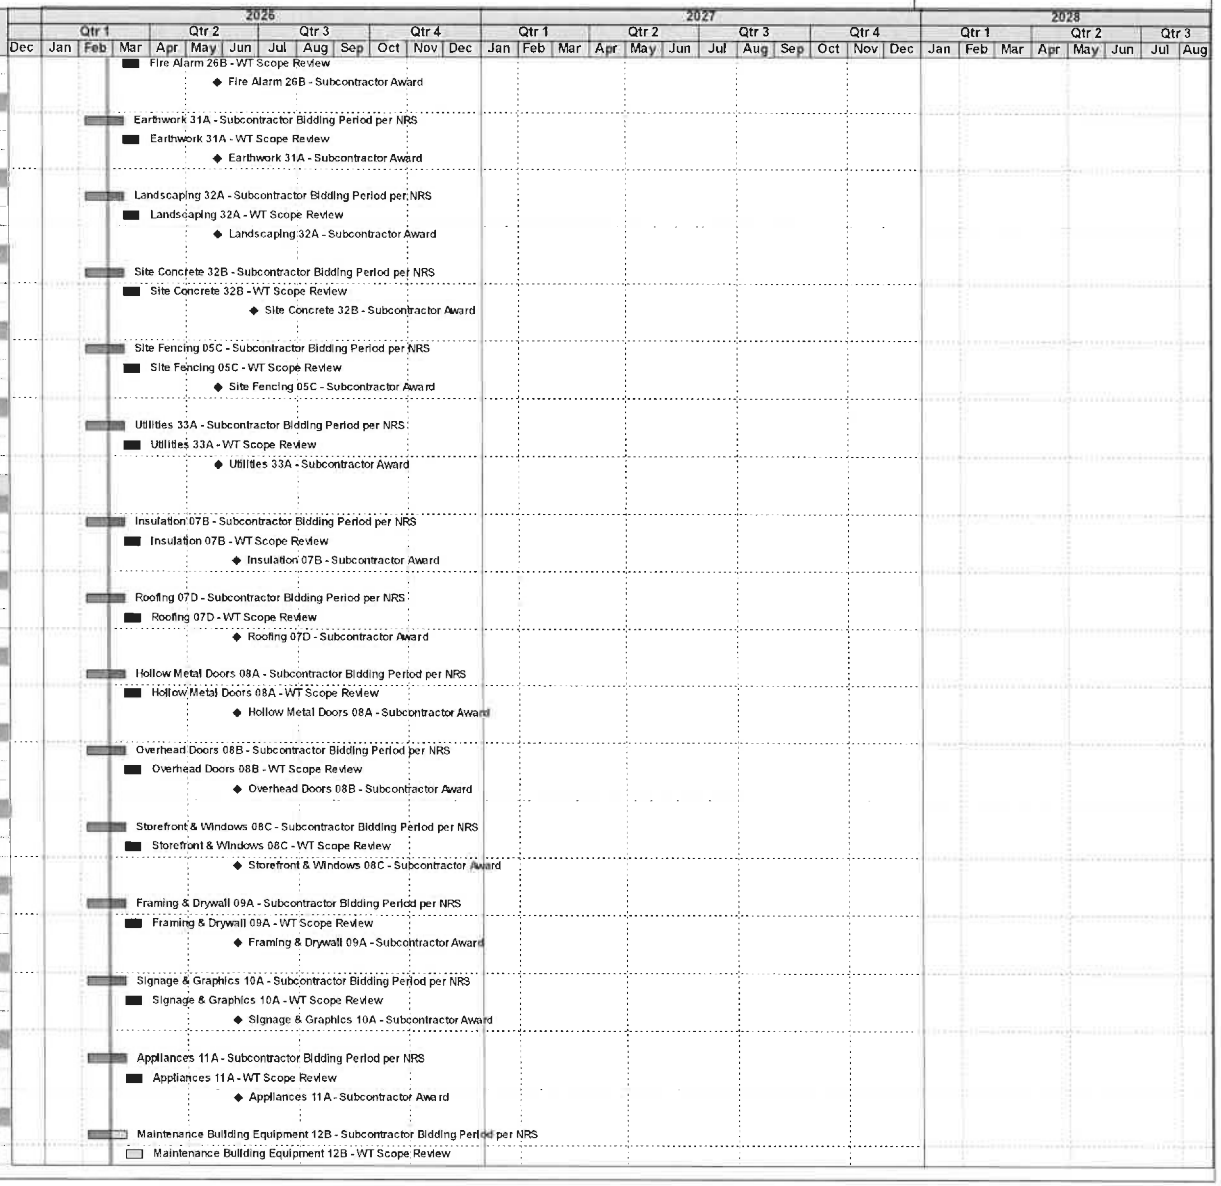

Activity ID	Activity Name	Orig Dur	Start	Finish
BUY.12B.120	Maintenance Building Equipment 12B - Subcontractor Award	0		06/11/2026
27A - Low Voltage		98	02/06/2026 A	06/11/2026
BUY.27A.100	Low Voltage 27A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.27A.110	Low Voltage 27A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.27A.120	Low Voltage 27A - Subcontractor Award	0		06/11/2026
Priority 3 Subcontractors		98	02/06/2026 A	06/26/2026
05B - Decorative Metals		98	02/06/2026 A	06/11/2026
BUY.05B.100	Decorative Metals 05B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.05B.110	Decorative Metals 05B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.05B.120	Decorative Metals 05B - Subcontractor Award	0		06/11/2026
06A - Millwork		98	02/06/2026 A	06/26/2026
BUY.06A.100	Millwork 06A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.06A.110	Millwork 06A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.06A.120	Millwork 06A - Subcontractor Award	0		06/26/2026
06C - Countertops		98	02/06/2026 A	06/26/2026
BUY.06C.100	Countertops 06C - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.06C.110	Countertops 06C - WT Scope Review	10	03/10/2026	03/23/2026
BUY.06C.120	Countertops 06C - Subcontractor Award	0		06/26/2026
09B - Tile & Stone		98	02/06/2026 A	06/26/2026
BUY.09B.100	Tile & Stone 09B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.09B.110	Tile & Stone 09B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.09B.120	Tile & Stone 09B - Subcontractor Award	0		06/26/2026
09C - ACT		98	02/06/2026 A	06/26/2026
BUY.09C.100	ACT 09C - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.09C.110	ACT 09C - WT Scope Review	10	03/10/2026	03/23/2026
BUY.09C.120	ACT 09C - Subcontractor Award	0		06/26/2026
09D - Resilient Flooring		98	02/06/2026 A	06/26/2026
BUY.09D.100	Resilient Flooring 09D - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.09D.110	Resilient Flooring 09D - WT Scope Review	10	03/10/2026	03/23/2026
BUY.09D.120	Resilient Flooring 09D - Subcontractor Award	0		06/26/2026
09E - Carpet		98	02/06/2026 A	06/26/2026
BUY.09E.100	Carpet 09E - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.09E.110	Carpet 09E - WT Scope Review	10	03/10/2026	03/23/2026
BUY.09E.120	Carpet 09E - Subcontractor Award	0		06/26/2026
09G - Paint		98	02/06/2026 A	06/26/2026
BUY.09G.100	Paint 09G - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.09G.110	Paint 09G - WT Scope Review	10	03/10/2026	03/23/2026
BUY.09G.120	Paint 09G - Subcontractor Award	0		06/26/2026
10B - Restroom Specialties		98	02/06/2026 A	06/26/2026
BUY.10B.100	Restroom Specialities 10B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.10B.110	Restroom Specialities 10B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.10B.120	Restroom Specialities 10B - Subcontractor Award	0		06/26/2026
10C - Lockers		98	02/06/2026 A	06/26/2026
BUY.10C.100	Lockers 10C - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.10C.110	Lockers 10C - WT Scope Review	10	03/10/2026	03/23/2026
BUY.10C.120	Lockers 10C - Subcontractor Award	0		06/26/2026
12A - Window Treatments		98	02/06/2026 A	06/26/2026
BUY.12A.100	Window Treatments 12A - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.12A.110	Window Treatments 12A - WT Scope Review	10	03/10/2026	03/23/2026
BUY.12A.120	Window Treatments 12A - Subcontractor Award	0		06/26/2026
12B - Furnishing		98	02/06/2026 A	06/26/2026
BUY.12B.140	Furnishing 12B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.12B.150	Furnishing 12B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.12B.160	Furnishing 12B - Subcontractor Award	0		06/26/2026
31B - Striping		98	02/06/2026 A	06/26/2026
BUY.31B.100	Striping 31B - Subcontractor Bidding Period per NRS	17	02/06/2026 A	03/09/2026
BUY.31B.110	Striping 31B - WT Scope Review	10	03/10/2026	03/23/2026
BUY.31B.120	Striping 31B - Subcontractor Award	0		06/26/2026

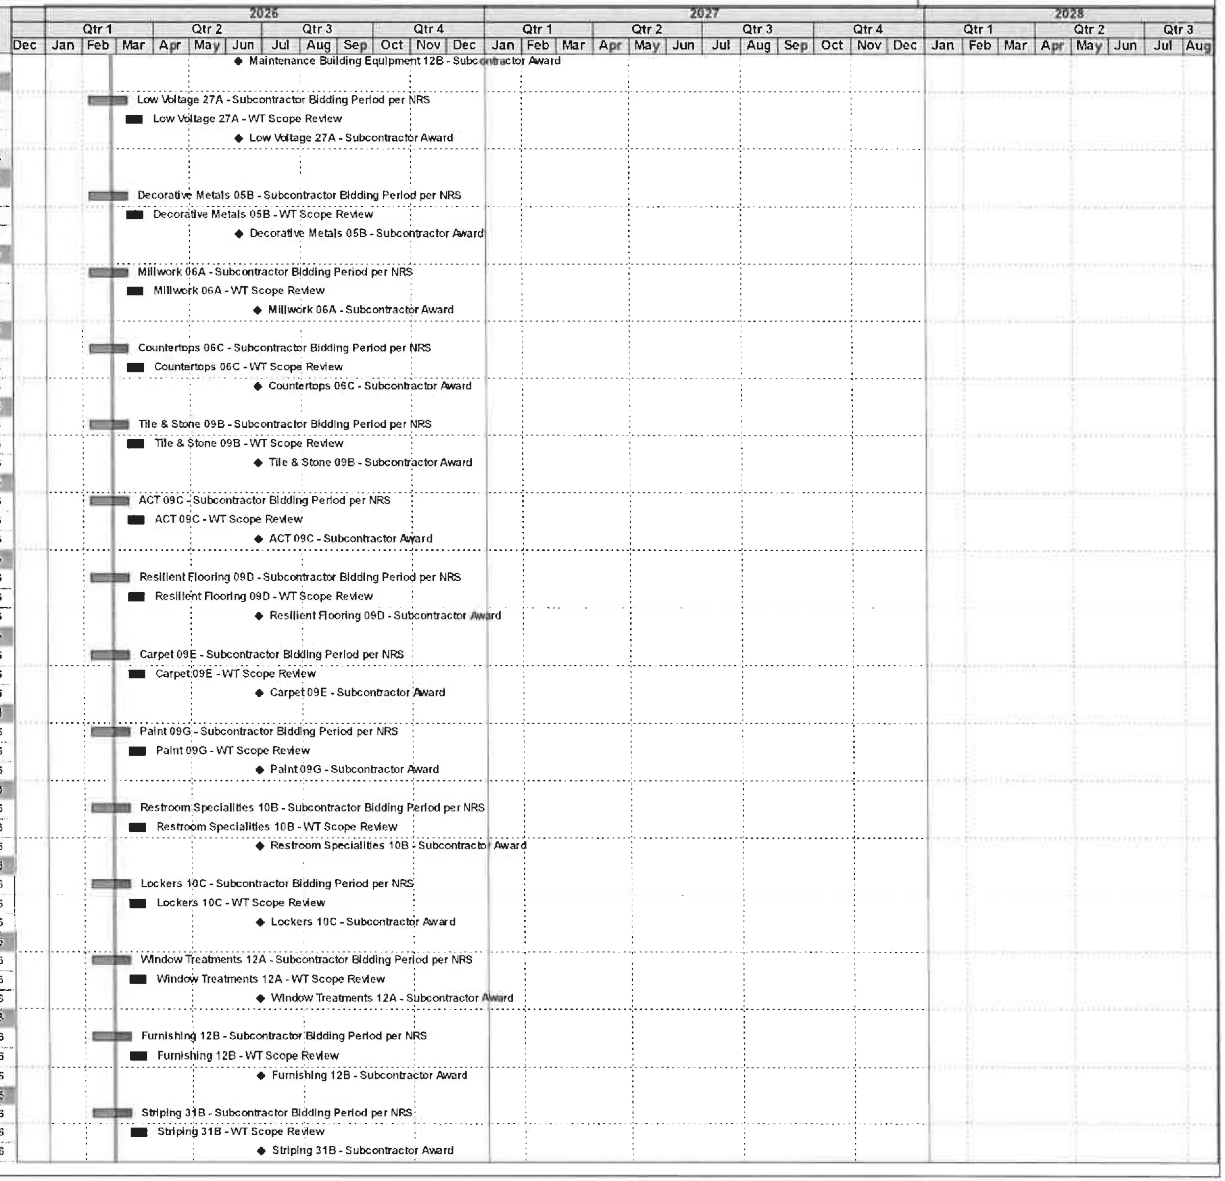

Clark County Fire Training Center Baseline Schedule
Full Schedule

Activity ID	Activity Name	Orig Dur	Start	Finish
Submittal Review & Approvals		325	05/28/2026	09/10/2027
02A - Survey		22	05/28/2026	06/29/2026
SUB.02A.100	Survey 02A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.02A.110	Survey 02A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.02A.120	Survey 02A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
03A - Concrete		22	06/12/2026	07/15/2026
SUB.03A.100	Concrete 03A - Generate Submittal	10	06/12/2026	06/26/2026
SUB.03A.120	Concrete 03A - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.03A.140	Concrete 03A - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
03A - Reinforcement		27	05/28/2026	07/07/2026
SUB.03A.110	Reinforcement 03A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.03A.130	Reinforcement 03A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.03A.150	Reinforcement 03A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.03A.100	Reinforcement 03A - Rebar Procurement	5	06/30/2026	07/07/2026
04A - Masonry		27	05/28/2026	07/07/2026
SUB.04A.100	Masonry 04A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.04A.110	Masonry 04A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.04A.120	Masonry 04A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.04A.100	Masonry 04A - Procurement	5	06/30/2026	07/07/2026
05A - Structural Steel		27	05/28/2026	07/07/2026
SUB.05A.100	Structural Steel 05A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.05A.110	Structural Steel 05A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.05A.120	Structural Steel 05A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.05A.100	Structural Steel 05A - Procurement	5	06/30/2026	07/07/2026
05B - Decorative Metals		27	06/12/2026	07/22/2026
SUB.05B.100	Decorative Metals 05B - Generate Submittal	10	06/12/2026	06/26/2026
SUB.05B.110	Decorative Metals 05B - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.05B.120	Decorative Metals 05B - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
PRO.05B.100	Decorative Metals 05B - Procurement	5	07/16/2026	07/22/2026
05C - Site Fencing		27	05/28/2026	07/07/2026
SUB.05C.100	Site Fencing 05C - Generate Submittal	10	05/28/2026	06/10/2026
SUB.05C.110	Site Fencing 05C - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.05C.120	Site Fencing 05C - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.05C.100	Site Fencing 05C - Procurement	5	06/30/2026	07/07/2026
05D - PEMB		27	05/28/2026	07/07/2026
SUB.05D.100	PEMB 05D - Generate Submittal	10	05/28/2026	06/10/2026
SUB.05D.110	PEMB 05D - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.05D.120	PEMB 05D - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.05D.100	PEMB 05D - Procurement	5	06/30/2026	07/07/2026
06A - Millwork		52	06/29/2026	09/10/2026
SUB.06A.100	Millwork 06A - Generate Submittal	10	06/29/2026	07/13/2026
SUB.06A.110	Millwork 06A - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.06A.120	Millwork 06A - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.06A.100	Millwork 06A - Procurement	30	07/30/2026	09/10/2026
06C - Countertops		304	06/29/2026	09/10/2027
SUB.06C.100	Countertops 06C - Generate Submittal	10	06/29/2026	07/13/2026
SUB.06C.110	Countertops 06C - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.06C.120	Countertops 06C - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.06C.130	Countertops 06C - Fabrication Maintenance Building	5	04/29/2027	05/05/2027
PRO.06C.120	Countertops 06C - Fabrication Fire Station	5	05/03/2027	05/07/2027
PRO.06C.100	Countertops 06C - Fabrication Level 3	5	08/31/2027	09/07/2027
PRO.06C.110	Countertops 06C - Fabrication Level 4	5	09/03/2027	09/10/2027
07B - Insulation		27	06/12/2026	07/22/2026
SUB.07B.100	Insulation 07B - Generate Submittal	10	06/12/2026	06/26/2026
SUB.07B.110	Insulation 07B - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.07B.120	Insulation 07B - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
PRO.07B.100	Insulation 07B - Procurement	5	07/16/2026	07/22/2026
07D - Roofing		27	06/12/2026	07/22/2026

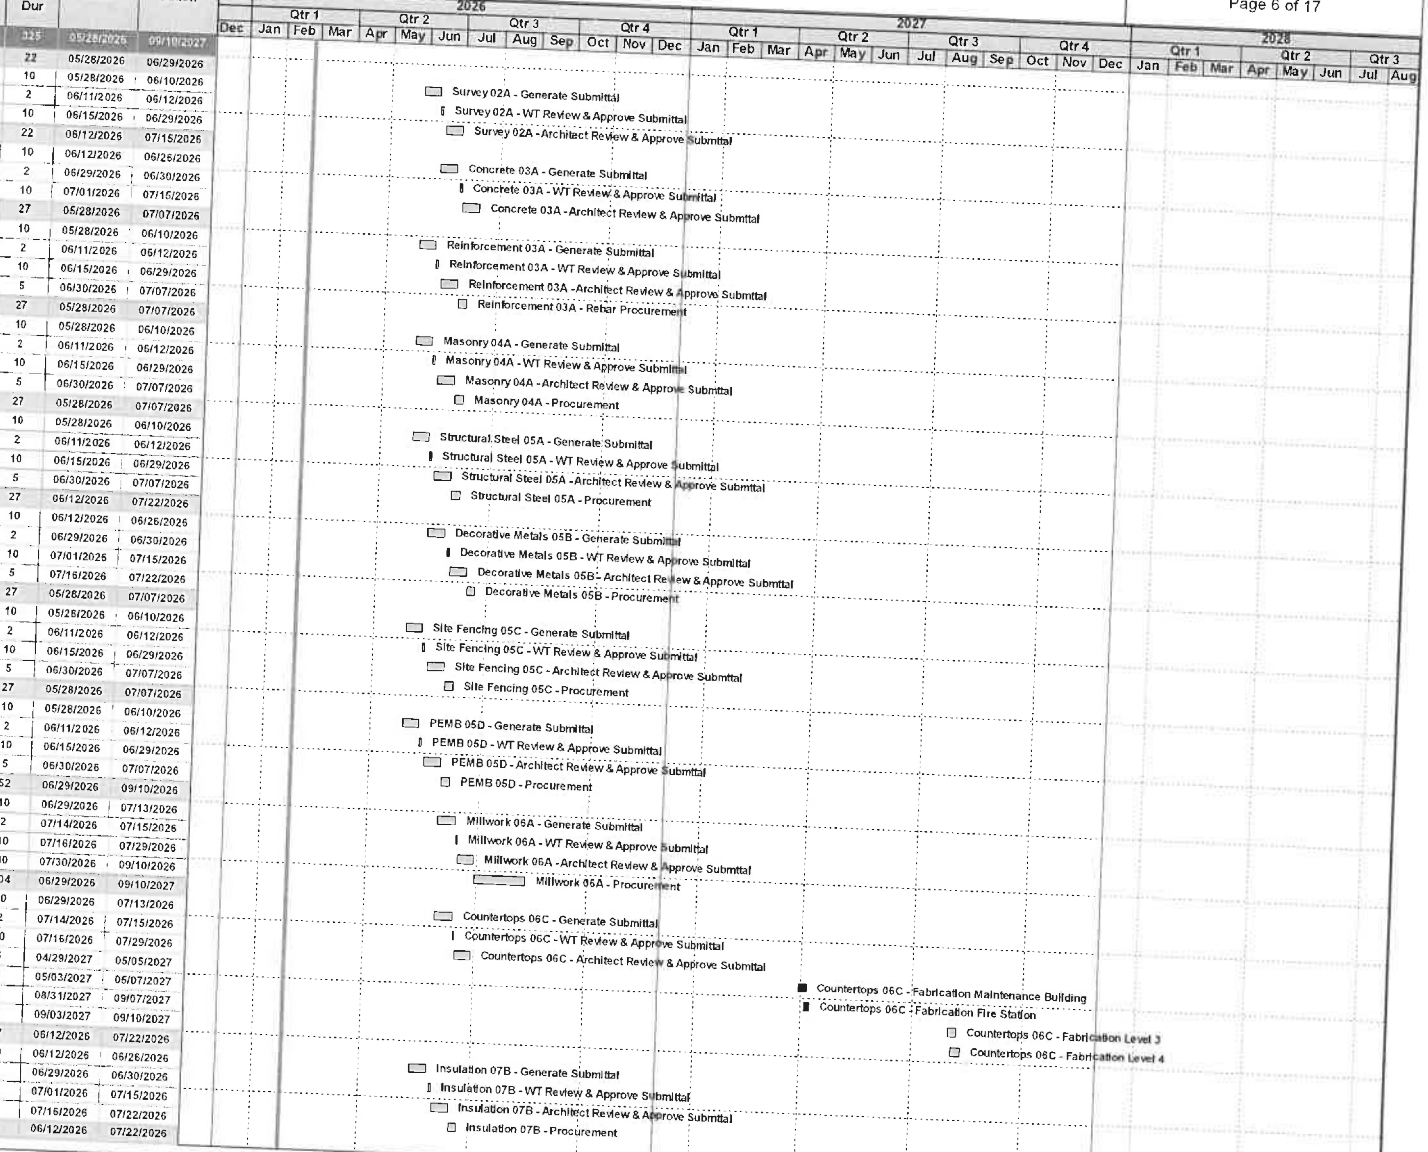

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
SUB.07D.100	Roofing 07D - Generate Submittal	10	06/12/2026	06/26/2026
SUB.07D.110	Roofing 07D - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.07D.120	Roofing 07D - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
PRO.07D.100	Roofing 07D - Procurement	5	07/16/2026	07/22/2026
08A - Hollw Metal Doors		27	06/12/2026	07/22/2026
SUB.08A.100	Hollow Metal Doors 08A - Generate Submittal	10	06/12/2026	06/26/2026
SUB.08A.110	Hollow Metal Doors 08A - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.08A.120	Hollow Metal Doors 08A - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
PRO.08A.100	Hollow Metal Doors 08A - Procurement	5	07/16/2026	07/22/2026
08B - Overhead Doors		27	06/12/2026	07/22/2026
SUB.08B.100	Overhead Doors 08B - Generate Submittal	10	06/12/2026	06/26/2026
SUB.08B.110	Overhead Doors 08B - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.08B.120	Overhead Doors 08B - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
PRO.08B.100	Overhead Doors 08B - Procurement	5	07/16/2026	07/22/2026
08C - Storefront & Windows		72	06/12/2026	09/24/2026
SUB.08C.100	Storefront & Windows 08C - Generate Submittal	10	06/12/2026	06/26/2026
SUB.08C.110	Storefront & Windows 08C - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.08C.120	Storefront & Windows 08C - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
PRO.08C.100	Storefront & Windows 08C - Procurement	50	07/16/2026	09/24/2026
09A - Framing & Drywall		22	06/12/2026	07/15/2026
SUB.09A.100	Framing & Drywall 09A - Generate Submittal	10	06/12/2026	06/26/2026
SUB.09A.110	Framing & Drywall 09A - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.09A.120	Framing & Drywall 09A - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
09B - Tile & Stone		27	06/29/2026	08/05/2026
SUB.09B.100	Tile & Stone 09B - Generate Submittal	10	06/29/2026	07/13/2026
SUB.09B.110	Tile & Stone 09B - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.09B.120	Tile & Stone 09B - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.09B.100	Tile & Stone 09B - Procurement	5	07/30/2026	08/05/2026
09C - ACT		27	06/29/2026	08/05/2026
SUB.09C.100	ACT 09C - Generate Submittal	10	06/29/2026	07/13/2026
SUB.09C.110	ACT 09C - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.09C.120	ACT 09C - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.09C.100	ACT 09C - Procurement	5	07/30/2026	08/05/2026
09D - Resilient Flooring		27	06/29/2026	08/05/2026
SUB.09D.100	Resilient Flooring 09D - Generate Submittal	10	06/29/2026	07/13/2026
SUB.09D.110	Resilient Flooring 09D - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.09D.120	Resilient Flooring 09D - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.09D.100	Resilient Flooring 09D - Procurement	5	07/30/2026	08/05/2026
09E - Carpet		27	06/29/2026	08/05/2026
SUB.09E.100	Carpet 09E - Generate Submittal	10	06/29/2026	07/13/2026
SUB.09E.110	Carpet 09E - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.09E.120	Carpet 09E - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.09E.100	Carpet 09E - Procurement	5	07/30/2026	08/05/2026
09G - Paint		27	06/29/2026	08/05/2026
SUB.09G.100	Paint 09G - Generate Submittal	10	06/29/2026	07/13/2026
SUB.09G.110	Paint 09G - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.09G.120	Paint 09G - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.09G.100	Paint 09G - Procurement	5	07/30/2026	08/05/2026
10A - Signage & Graphics		27	06/12/2026	07/22/2026
SUB.10A.100	Signage & Graphics 10A - Generate Submittal	10	06/12/2026	06/26/2026
SUB.10A.110	Signage & Graphics 10A - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.10A.120	Signage & Graphics 10A - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
PRO.10A.100	Signage & Graphics 10A - Procurement	5	07/16/2026	07/22/2026
10B - Restroom Specialities		27	06/29/2026	08/05/2026
SUB.10B.100	Restroom Specialities 10B - Generate Submittal	10	06/29/2026	07/13/2026
SUB.10B.110	Restroom Specialities 10B - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.10B.120	Restroom Specialities 10B - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.10B.100	Restroom Specialities 10B - Procurement	5	07/30/2026	08/05/2026

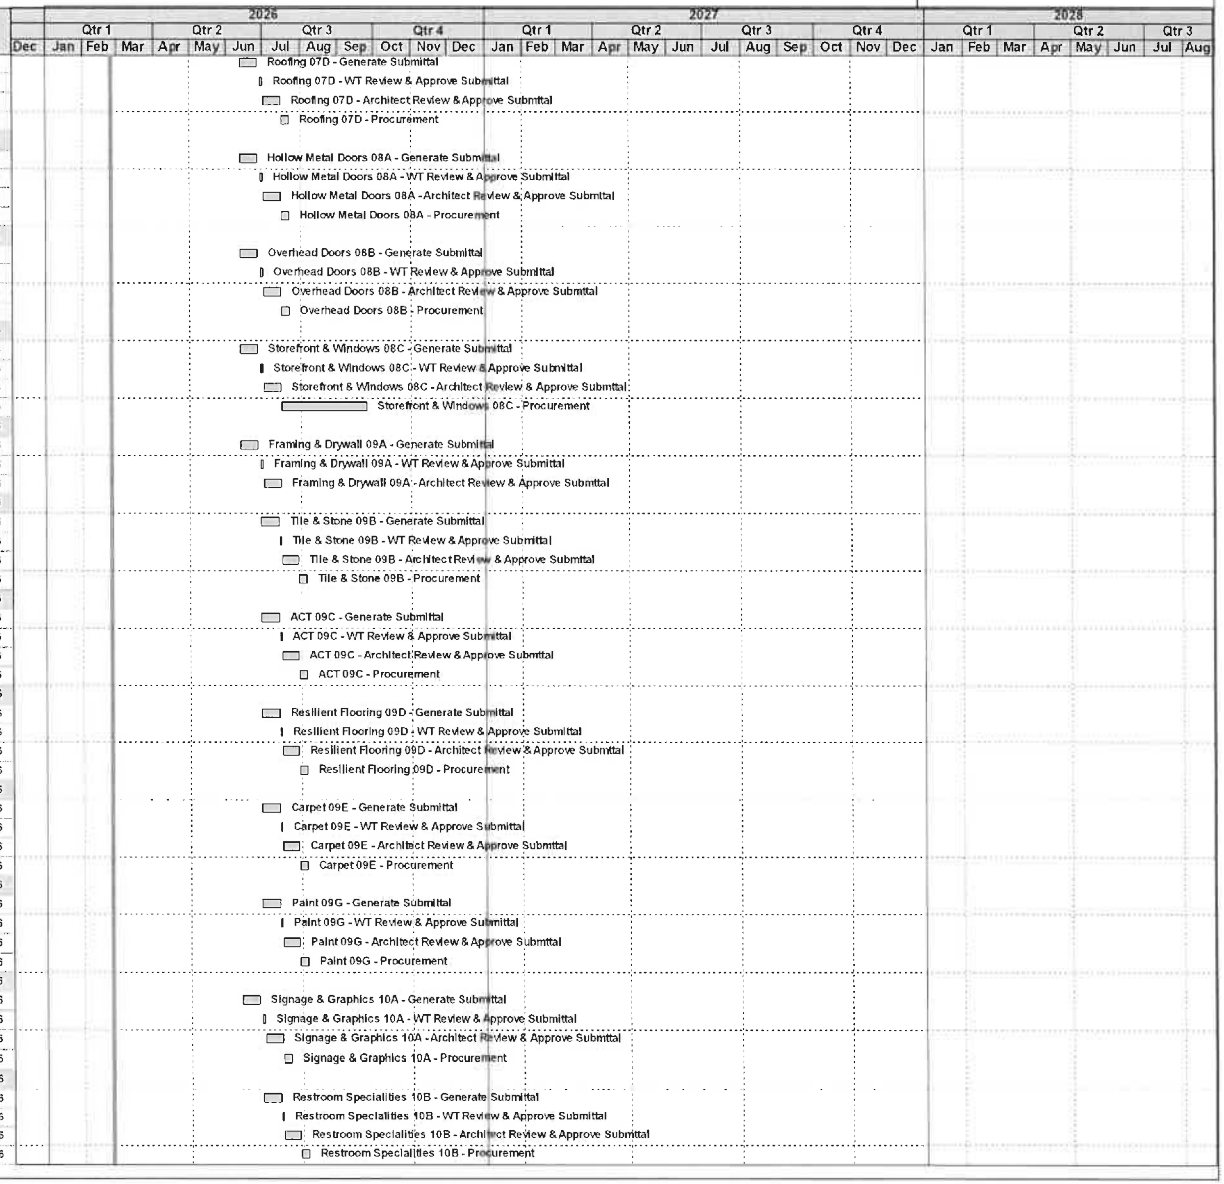

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
10C - Lockers		27	06/29/2026	08/05/2026
SUB.10C.100	Lockers 10C - Generate Submittal	10	06/29/2026	07/13/2026
SUB.10C.110	Lockers 10C - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.10C.120	Lockers 10C - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.10C.100	Lockers 10C - Procurement	5	07/30/2026	08/05/2026
11A - Appliances		27	06/12/2026	07/22/2026
SUB.11A.100	Appliances 11A - Generate Submittal	10	06/12/2026	06/26/2026
SUB.11A.110	Appliances 11A - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.11A.120	Appliances 11A - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
PRO.11A.100	Appliances 11A - Procurement	5	07/16/2026	07/22/2026
12A - Window Treatment		27	06/29/2026	08/05/2026
SUB.12A.100	Window Treatment 12A - Generate Submittal	10	06/29/2026	07/13/2026
SUB.12A.110	Window Treatment 12A - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.12A.120	Window Treatment 12A - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.12A.100	Window Treatment 12A - Procurement	5	07/30/2026	08/05/2026
12B - Furnishings		27	06/29/2026	08/05/2026
SUB.12B.100	Furnishings 12B - Generate Submittal	10	06/29/2026	07/13/2026
SUB.12B.110	Furnishings 12B - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.12B.120	Furnishings 12B - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.12B.100	Furnishings 12B - Procurement	5	07/30/2026	08/05/2026
14A - Elevator		126	05/28/2026	11/30/2026
SUB.14A.100	Elevator 14A - Generate Submittal	15	05/28/2026	06/17/2026
SUB.14A.110	Elevator 14A - WT Review & Approve Submittal	1	06/18/2026	06/18/2026
SUB.14A.120	Elevator 14A - Architect Review & Approve Submittal	10	06/22/2026	07/06/2026
PRO.14A.100	Elevator 14A - Procurement	100	07/07/2026	11/30/2026
21A - Fire Suppression		27	05/28/2026	07/07/2026
SUB.21A.100	Fire Suppression 21A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.21A.110	Fire Suppression 21A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.21A.120	Fire Suppression 21A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.21A.100	Fire Suppression 21A - Procurement	5	06/30/2026	07/07/2026
22A - Plumbing		27	05/28/2026	07/07/2026
SUB.22A.100	Plumbing 22A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.22A.110	Plumbing 22A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.22A.120	Plumbing 22A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.22A.100	Plumbing 22A - Procurement	5	06/30/2026	07/07/2026
23A - HVAC		27	05/28/2026	07/07/2026
SUB.23A.100	HVAC 23A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.23A.120	HVAC 23A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.23A.140	HVAC 23A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.23A.100	HVAC 23A - Procurement	5	06/30/2026	07/07/2026
23A - Plymovent		22	05/28/2026	06/29/2026
SUB.23A.110	Plymovent 23A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.23A.130	Plymovent 23A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.23A.150	Plymovent 23A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
26A - Electrical		22	05/28/2026	06/29/2026
SUB.26A.100	Electrical 26A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.26A.110	Electrical 26A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.26A.120	Electrical 26A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
26B - Fire Alarm		22	05/28/2026	06/29/2026
SUB.26B.100	Fire Alarm 26B - Generate Submittal	10	05/28/2026	06/10/2026
SUB.26B.110	Fire Alarm 26B - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.26B.120	Fire Alarm 26B - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
27A - Low Voltage		22	06/12/2026	07/15/2026
SUB.27A.100	Low Voltage 27A - Generate Submittal	10	06/12/2026	06/26/2026
SUB.27A.110	Low Voltage 27A - WT Review & Approve Submittal	2	06/29/2026	06/30/2026
SUB.27A.120	Low Voltage 27A - Architect Review & Approve Submittal	10	07/01/2026	07/15/2026
31A - Earthwork		27	05/28/2026	07/07/2026
SUB.31A.100	Earthwork 31A - Generate Submittal	10	05/28/2026	06/10/2026

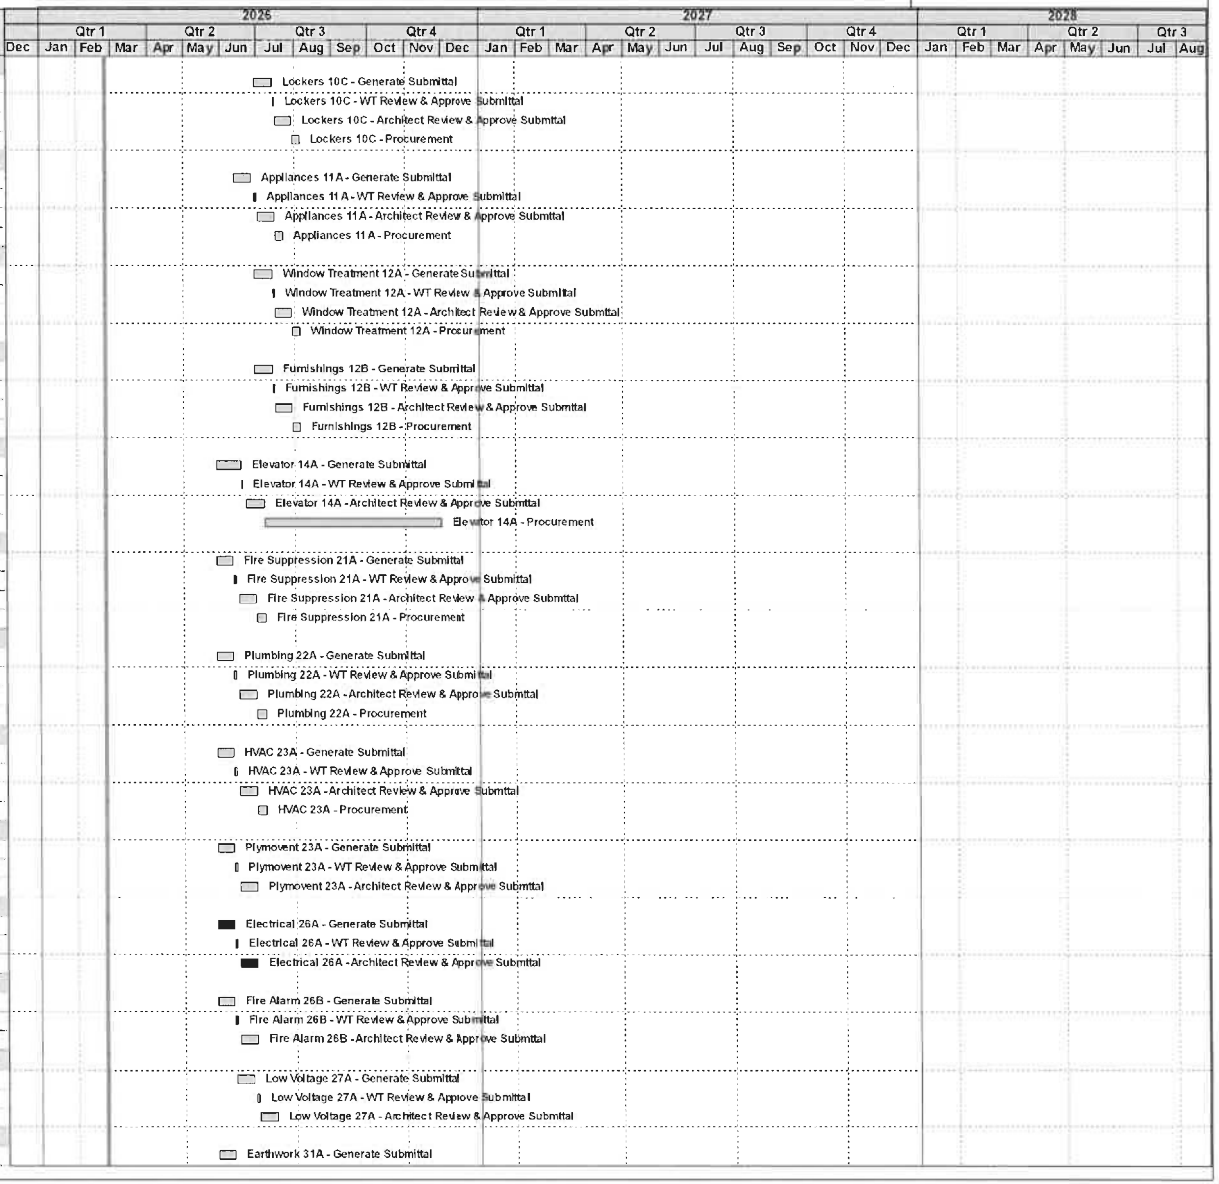

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
SUB.31A.110	Earthwork 31A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.31A.120	Earthwork 31A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.31A.100	Earthwork 31A - Procurement	5	06/30/2026	07/07/2026
31B - Striping		27	06/29/2026	08/05/2026
SUB.31B.100	Striping 31B - Generate Submittal	10	06/29/2026	07/13/2026
SUB.31B.110	Striping 31B - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.31B.120	Striping 31B - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.31B.100	Striping 31B - Procurement	5	07/30/2026	08/05/2026
32A - Landscaping		22	05/28/2026	06/29/2026
SUB.32A.100	Landscaping 32A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.32A.110	Landscaping 32A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.32A.120	Landscaping 32A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
32B - Site Concrete		27	06/29/2026	08/05/2026
SUB.32B.100	Site Concrete 32B - Generate Submittal	10	06/29/2026	07/13/2026
SUB.32B.110	Site Concrete 32B - WT Review & Approve Submittal	2	07/14/2026	07/15/2026
SUB.32B.120	Site Concrete 32B - Architect Review & Approve Submittal	10	07/16/2026	07/29/2026
PRO.32B.100	Site Concrete 32B - Procurement	5	07/30/2026	08/05/2026
33A - Utilities		27	05/28/2026	07/07/2026
SUB.33A.100	Site Utilities 33A - Generate Submittal	10	05/28/2026	06/10/2026
SUB.33A.110	Site Utilities 33A - WT Review & Approve Submittal	2	06/11/2026	06/12/2026
SUB.33A.120	Site Utilities 33A - Architect Review & Approve Submittal	10	06/15/2026	06/29/2026
PRO.33A.100	Site Utilities 33A - Procurement	5	06/30/2026	07/07/2026
Long Lead Procurement		260	06/30/2026	07/12/2027
LONG.100	Generator Procurement	260	06/30/2026	07/12/2027
LONG.110	Transformers	200	06/30/2026	04/15/2027
LONG.120	Switchgears	160	06/30/2026	02/18/2027
LONG.130	Structural Steel	80	06/30/2026	10/21/2026
LONG.140	Curtain Wall/Storefront	80	07/16/2026	11/06/2026
CONSTRUCTION		457	06/01/2026	03/27/2028
Mobilization		10	06/01/2026	06/12/2026
MOB.140	Cut & Cap Utilities	3	06/01/2026	06/03/2026
MOB.100	Mobilize Site Office/Conex	10	06/01/2026	06/12/2026
MOB.110	Abatement of Existing Materials	3	06/01/2026	06/03/2026
MOB.120	Set Up Site Fencing	10	06/01/2026	06/12/2026
MOB.150	Install Track Out	3	06/01/2026	06/03/2026
MOB.130	Install Temp Power	3	06/01/2026	06/03/2026
Demolition		53	06/15/2026	08/28/2026
Phase 1		10	06/15/2026	06/29/2026
P1.DEM.120	Clear & Grub	3	06/15/2026	06/17/2026
P1.DEM.100	Install UG Site Domestic Water	5	06/18/2026	06/25/2026
P1.DEM.110	Install UG Site Sanitary Sewer	5	06/18/2026	06/25/2026
P1.DEM.140	Install Fire Loop	5	06/18/2026	06/25/2026
P1.DEM.130	Install UG Site Electrical	5	06/23/2026	06/29/2026
Phase 2		15	06/18/2026	07/10/2026
P2.DEM.120	Clear & Grub	5	06/18/2026	06/25/2026
P2.DEM.130	Install UG Site Domestic Water	8	06/26/2026	07/08/2026
P2.DEM.140	Install UG Site Sanitary Sewer	8	06/26/2026	07/08/2026
P2.DEM.100	Install Fire Loop	8	06/26/2026	07/08/2026
P2.DEM.150	Install UG Site Electrical	8	06/30/2026	07/10/2026
P2.DEM.160	Install UG Low Voltage	8	06/30/2026	07/10/2026
Phase 3		15	06/26/2026	07/17/2026
P3.DEM.100	Clear & Grub	5	06/26/2026	07/02/2026
P3.DEM.110	Install UG Site Domestic Water	5	07/09/2026	07/15/2026
P3.DEM.120	Install UG Site Sanitary Sewer	5	07/09/2026	07/15/2026
P3.DEM.140	Install Fire Loop	5	07/09/2026	07/15/2026
P3.DEM.130	Install UG Site Electrical	5	07/13/2026	07/17/2026
P3.DEM.160	Install UG Low Voltage	5	07/13/2026	07/17/2026
Phase 4		25	07/06/2026	08/07/2026

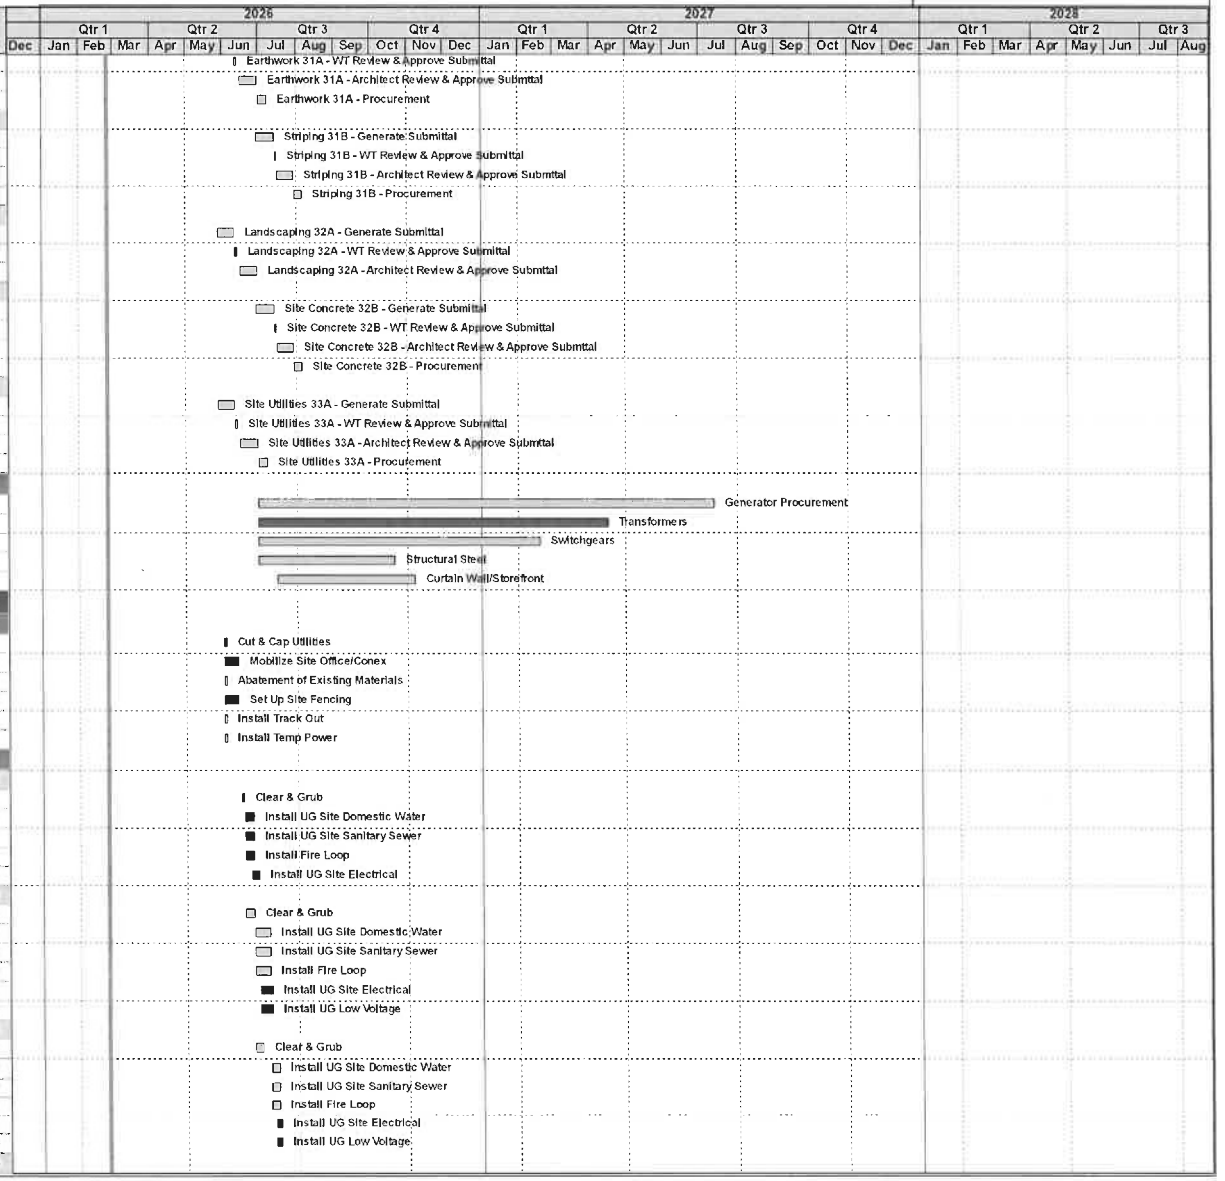

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
P4.DEM.100	Clear & Grub	3	07/06/2026	07/08/2026
P4.DEM.110	Install UG Site Domestic Water	15	07/16/2026	08/05/2026
P4.DEM.120	Install UG Site Sanitary Sewer	15	07/16/2026	08/05/2026
P4.DEM.140	Install Fire Loop	15	07/16/2026	08/05/2026
P4.DEM.130	Install UG Site Electrical	15	07/20/2026	08/07/2026
P4.DEM.160	Install UG Low Voltage	15	07/20/2026	08/07/2026
Phase 5		37	07/09/2026	08/28/2026
P5.DEM.100	Clear & Grub	3	07/09/2026	07/13/2026
P5.DEM.150	Install UG Storm Drain	15	07/14/2026	08/03/2026
P5.DEM.110	Install UG Site Domestic Water	15	08/06/2026	08/26/2026
P5.DEM.120	Install UG Site Sanitary Sewer	15	08/06/2026	08/26/2026
P5.DEM.140	Install Fire Loop	15	08/06/2026	08/26/2026
P5.DEM.130	Install UG Site Electrical	15	08/10/2026	08/28/2026
P5.DEM.160	Install UG Low Voltage	15	08/10/2026	08/28/2026
Earthwork		20	08/10/2026	09/04/2026
Parking Garage Training Center		5	08/10/2026	08/14/2026
EW.TC.100	Subgrade Prep Training Center	3	08/10/2026	08/12/2026
EW.TC.110	Build Up Building Pad for Parking Garage Training Center	2	08/13/2026	08/14/2026
EW.TC.120	Receive all Certified Building Pads Training Center	0		08/14/2026
Maintenance Building		5	08/17/2026	08/21/2026
EW.MB.100	Subgrade Prep Maintenance Building	3	08/17/2026	08/19/2026
EW.MB.110	Build Up Building Pad for Maintenance Building	2	08/20/2026	08/21/2026
EW.MB.120	Receive all Certified Building Pads Maintenance Building	0		08/21/2026
Fire Station		5	08/24/2026	08/28/2026
EW.FS.100	Subgrade Prep Fire Station	3	08/24/2026	08/26/2026
EW.FS.110	Build Up Building Pad for Parking Garage Fire Station	2	08/27/2026	08/28/2026
EW.FS.120	Receive all Certified Building Pads Fire Station	0		08/28/2026
Burn Tower		5	08/31/2026	09/04/2026
EW.BT.100	Subgrade Prep Burn Tower	3	08/31/2026	09/02/2026
EW.BT.110	Build Up Building Pad for Burn Tower	2	09/03/2026	09/04/2026
EW.BT.120	Receive all Certified Building Pads Burn Tower	0		09/04/2026
Site Utilities		233	09/21/2026	07/26/2027
Onsite Utilities		182	11/04/2026	07/26/2027
Phase 1		182	11/04/2026	07/26/2027
Generator/Mechanical/Trash Enclosures		182	11/04/2026	07/26/2027
ON.UT.180	F/R/P CMU Footings	5	11/04/2026	11/10/2026
ON.UT.190	Install First CMU Lift	1	11/12/2026	11/12/2026
ON.UT.200	F/R/P Generator Pad	2	11/13/2026	11/16/2026
ON.UT.210	Install Remaining CMU	2	11/17/2026	11/18/2026
ON.UT.220	Install Generator	5	07/13/2027	07/19/2027
ON.UT.230	Install Gates	5	07/20/2027	07/26/2027
Offsite Work		77	08/21/2026	12/14/2026
Tropicana Turn Lane		28	08/21/2026	09/30/2026
TROP.100	Install Traffic Barricades	1	08/21/2026	08/21/2026
TROP.110	Demo Curb and Gutter Remove Landscaping	2	08/24/2026	08/25/2026
TROP.120	Sawcut Street and Demo Asphalt	2	08/26/2026	08/27/2026
TROP.130	Grade Street Install Type II	3	08/28/2026	09/01/2026
TROP.140	Form and Pour Sidewalk, Curb & Gutter	10	09/02/2026	09/16/2026
TROP.150	Lay Asphalt Paving	2	09/17/2026	09/18/2026
TROP.160	Install CMU Fencing & Metal Panels	10	09/17/2026	09/30/2026
TROP.170	Line and Stripe (Paint Curb as Reqd')	1	09/21/2026	09/21/2026
TROP.180	Install New Signage	1	09/22/2026	09/22/2026
Arville Entrances		76	08/24/2026	12/14/2026
ARV.100	Install Traffic Barricades	1	08/24/2026	08/24/2026
ARV.110	Demo Curb and Gutter Remove Landscaping	3	08/25/2026	08/27/2026
ARV.120	Sawcut Street and Demo Asphalt	3	08/28/2026	09/01/2026
ARV.130	Grade Street Install Type II	4	09/02/2026	09/08/2026
ARV.140	Form and Pour Sidewalk, Curb & Gutter	15	09/09/2026	09/29/2026

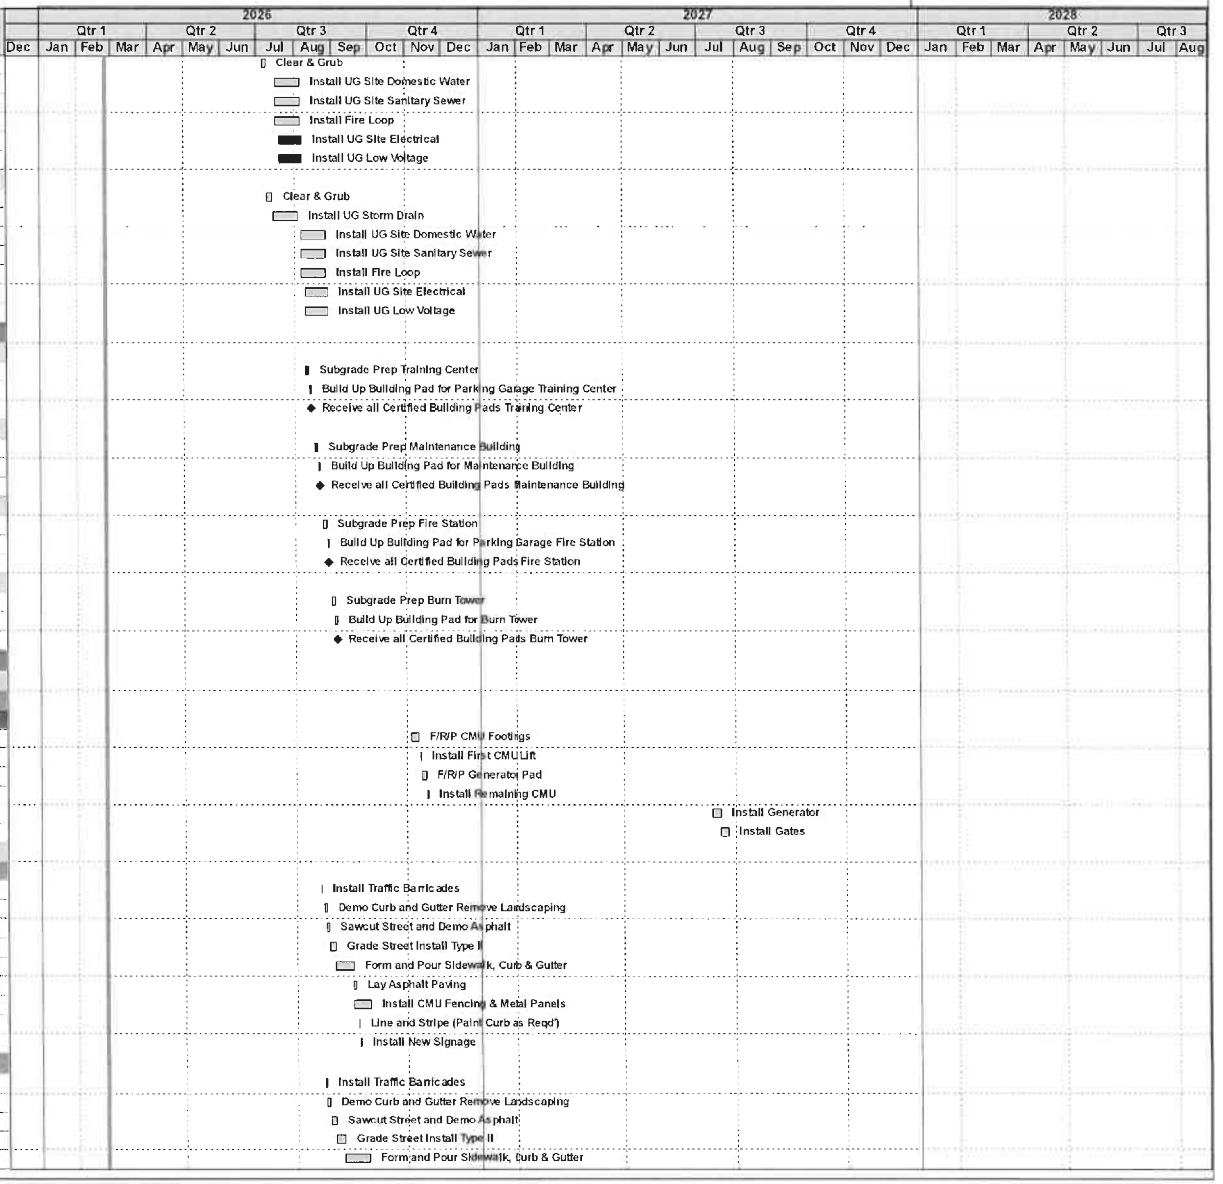

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
ARV.150	Lay Asphalt Paving	1	09/30/2026	09/30/2026
ARV.160	Install CMU Fencing	20	09/30/2026	10/27/2026
ARV.170	Line and Stripe (Paint Curb as Reqd')	1	10/01/2026	10/01/2026
ARV.180	Install New Signage	1	10/02/2026	10/02/2026
ARV.190	Install Rolling Gates	30	10/28/2026	12/14/2026
Training Building		404	08/17/2026	03/17/2028
Building Structure		222	08/17/2026	07/02/2027
Parking Garage Levels 1-3		80	08/17/2026	12/11/2026
Level 1		55	08/17/2026	11/03/2026
Level 1-A		45	08/17/2026	10/19/2026
TB.L1A.100	Survey	1	08/17/2026	08/17/2026
TB.L1A.110	Layout	3	08/18/2026	08/20/2026
TB.L1A.120	F/R/P Footings	10	08/21/2026	09/03/2026
TB.L1A.130	F/R/P Elevator Pits	5	08/28/2026	09/03/2026
TB.L1A.140	Excavate Footings/MEPs	5	09/04/2026	09/11/2026
TB.L1A.150	Install UG Plumbing	5	09/14/2026	09/18/2026
TB.L1A.160	Install UG Electrical	5	09/14/2026	09/18/2026
TB.L1A.170	Fine Grade Building Pad	5	09/21/2026	09/25/2026
TB.L1A.180	Install Vapor Barrier	3	09/28/2026	09/30/2026
TB.L1A.190	Install Type II	3	10/01/2026	10/05/2026
TB.L1A.200	F/R/P SOG	5	10/06/2026	10/12/2026
TB.L1A.210	F/R/P Columns	5	10/13/2026	10/19/2026
Level 1-B		54	08/18/2026	11/03/2026
TB.L1B.100	Survey	1	08/18/2026	08/18/2026
TB.L1B.110	Layout	3	08/21/2026	08/25/2026
TB.L1B.120	F/R/P Footings	10	09/04/2026	09/18/2026
TB.L1B.130	Excavate Footings/MEPs	5	09/21/2026	09/25/2026
TB.L1B.140	Install UG Plumbing	5	09/28/2026	10/02/2026
TB.L1B.150	Install UG Electrical	5	09/28/2026	10/02/2026
TB.L1B.160	Fine Grade Building Pad	5	10/05/2026	10/09/2026
TB.L1B.170	Install Vapor Barrier	3	10/12/2026	10/14/2026
TB.L1B.180	Install Type II	3	10/15/2026	10/19/2026
TB.L1B.190	F/R/P SOG	5	10/20/2026	10/26/2026
TB.L1B.200	F/R/P Columns	5	10/27/2026	11/03/2026
Level 2		25	11/04/2026	12/11/2026
Level 2-A		15	11/04/2026	11/25/2026
TB.L2A.100	Level 2 Deck - Form	5	11/04/2026	11/10/2026
TB.L2A.110	Level 2 Deck - MEP Rough	2	11/12/2026	11/13/2026
TB.L2A.120	Level 2 Deck - Rebar/PT Cable	2	11/16/2026	11/17/2026
TB.L2A.130	Level 2 Deck - Pour	2	11/18/2026	11/19/2026
TB.L2A.140	Level 2 Deck - F/R/P Columns	2	11/20/2026	11/23/2026
TB.L2A.150	Level 3 Transfer Slab - F/R/P	2	11/24/2026	11/25/2026
Level 2-B		16	11/12/2026	12/04/2026
TB.L2B.100	Level 2 Deck - Form	5	11/12/2026	11/18/2026
TB.L2B.110	Level 2 Deck - MEP Rough	2	11/19/2026	11/20/2026
TB.L2B.120	Level 2 Deck - Rebar/PT Cable	2	11/23/2026	11/24/2026
TB.L2B.130	Level 2 Deck - Pour	2	11/25/2026	11/30/2026
TB.L2B.140	Level 2 Deck - F/R/P Columns	2	12/01/2026	12/02/2026
TB.L2B.150	Level 3 Transfer Slab - F/R/P	2	12/03/2026	12/04/2026
Level 2-C		15	11/19/2026	12/11/2026
TB.L2C.100	Level 2 Deck - Form	5	11/19/2026	11/25/2026
TB.L2C.110	Level 2 Deck - MEP Rough	2	11/30/2026	12/01/2026
TB.L2C.120	Level 2 Deck - Rebar/PT Cable	2	12/02/2026	12/03/2026
TB.L2C.130	Level 2 Deck - Pour	2	12/04/2026	12/07/2026
TB.L2C.140	Level 2 Deck - F/R/P Columns	2	12/08/2026	12/09/2026
TB.L2C.150	Level 3 Transfer Slab - F/R/P	2	12/10/2026	12/11/2026
Level 3		25	11/30/2026	01/05/2027
Level 3-A		15	11/30/2026	12/18/2026

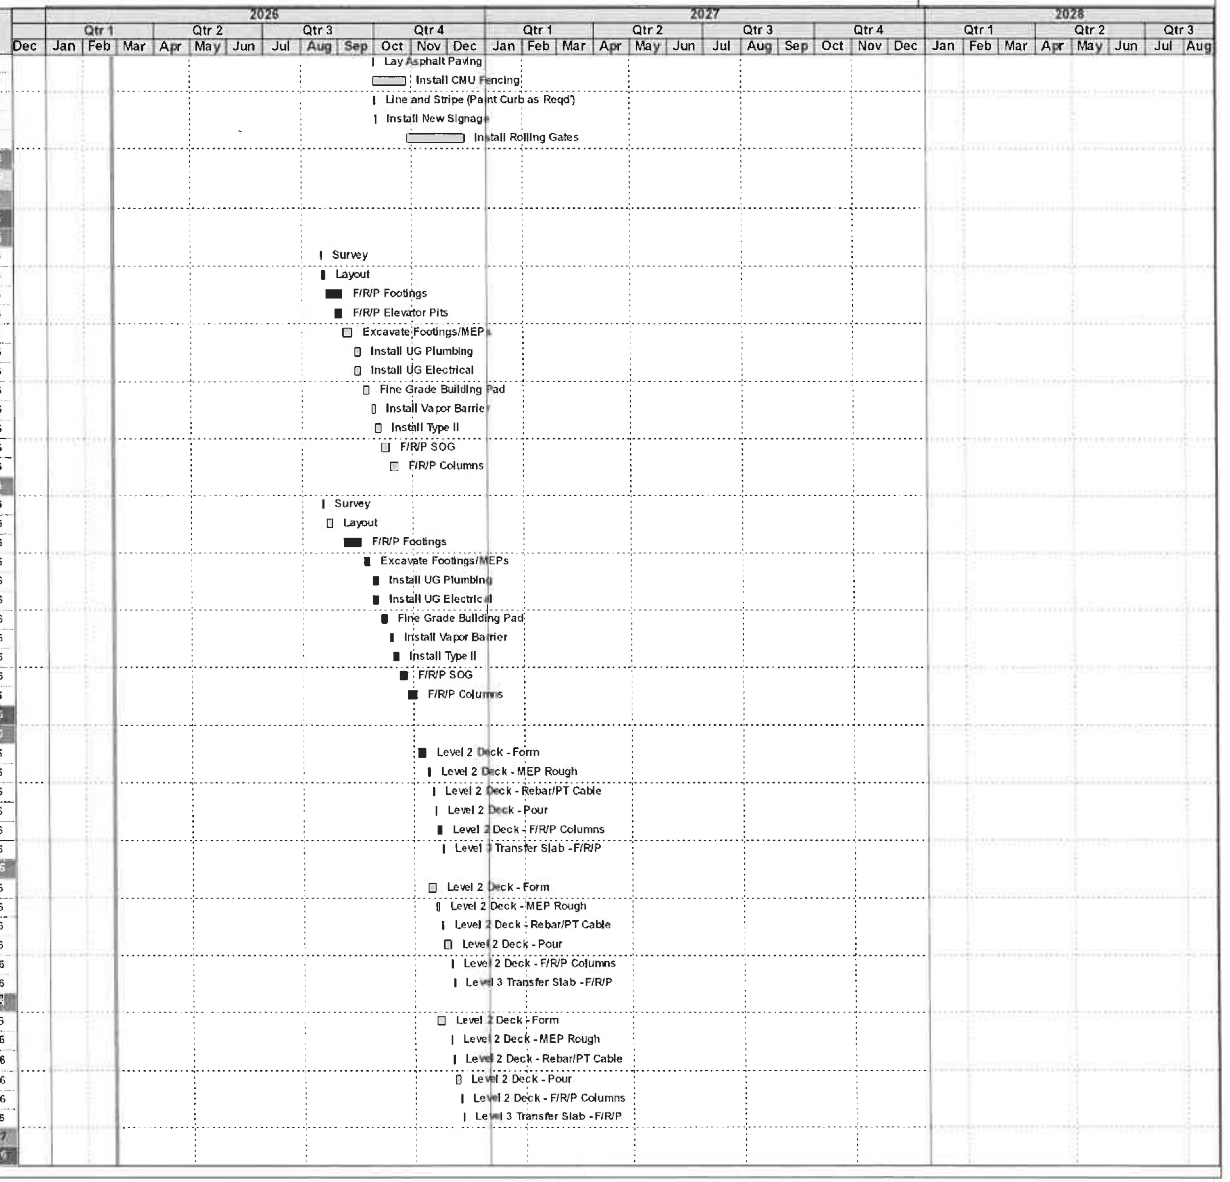

Activity ID	Activity Name	Orig Dur	Start	Finish
TB.L3A.100	Install Structural Steel	5	11/30/2026	12/04/2026
TB.L3A.110	Install Metal Deck at Level 4	5	12/07/2026	12/11/2026
TB.L3A.120	Pour Level 4 Deck	5	12/14/2026	12/18/2026
Level 3-B		15	12/07/2026	12/28/2026
TB.L3B.100	Install Structural Steel	5	12/07/2026	12/11/2026
TB.L3B.110	Install Metal Deck at Level 4	5	12/14/2026	12/18/2026
TB.L3B.120	Pour Level 4 Deck	5	12/21/2026	12/28/2026
Level 3-C		15	12/14/2026	01/05/2027
TB.L3C.100	Install Structural Steel	5	12/14/2026	12/18/2026
TB.L3C.110	Install Metal Deck at Level 4	5	12/21/2026	12/28/2026
TB.L3C.120	Pour Level 4 Deck	5	12/29/2026	01/05/2027
Level 4		35	12/21/2026	02/09/2027
Level 4-A		15	12/21/2026	01/12/2027
TB.L4A.100	Install Structural Steel	10	12/21/2026	01/04/2027
TB.L4A.110	Install Roof Structural Steel	5	01/06/2027	01/12/2027
Level 4-B		15	01/06/2027	01/26/2027
TB.L4B.100	Install Structural Steel	10	01/06/2027	01/19/2027
TB.L4B.110	Install Roof Structural Steel	5	01/20/2027	01/26/2027
Level 4-C		15	01/20/2027	02/09/2027
TB.L4C.100	Install Structural Steel	10	01/20/2027	02/02/2027
TB.L4C.110	Install Roof Structural Steel	5	02/03/2027	02/09/2027
Roof		45	02/10/2027	04/13/2027
TB.R.100	Install Roof Deck	5	02/10/2027	02/16/2027
TB.R.110	Install Roof Drains	5	02/10/2027	02/16/2027
TB.R.120	Install Roof System	20	02/17/2027	03/16/2027
TB.R.130	Install Rooftop Mechanical	20	03/17/2027	04/13/2027
Elevators		209	09/04/2026	07/02/2027
TB.ELEV.110	Erect Concrete Shafts Elevator Tower 2	20	09/04/2026	10/02/2026
TB.ELEV.100	Erect Concrete Shafts Elevator Tower 1	15	10/13/2026	11/03/2026
TB.ELEV.120	Install Sump In Shafts	5	11/04/2026	11/10/2026
TB.ELEV.130	Install Elevators	50	04/16/2027	06/25/2027
TB.ELEV.140	Elevator State Inspection	5	06/28/2027	07/02/2027
Exterior		226	09/04/2026	07/28/2027
TB.EXT.100	Install CMU	20	09/04/2026	10/02/2026
TB.EXT.120	Install HM Door Frames	5	10/05/2026	10/09/2026
TB.EXT.110	Install Storefront Frames	5	11/09/2026	11/16/2026
TB.EXT.130	Install Stair Structures	30	11/12/2026	12/28/2026
TB.EXT.140	Install Building Skin S/W	40	02/17/2027	04/13/2027
TB.EXT.190	Install Building Skin N/E	40	04/14/2027	06/09/2027
TB.EXT.150	Install Storefront	5	06/10/2027	06/16/2027
TB.EXT.160	Install HM Doors	5	06/10/2027	06/16/2027
TB.EXT.170	Install Exterior Finishes	10	06/17/2027	06/30/2027
TB.EXT.180	Install Glass Railing	20	07/01/2027	07/28/2027
Interior MEP & Finishes		235	01/05/2027	12/09/2027
Parking Garage Levels 1-3		130	01/06/2027	07/08/2027
Level 1-2		130	01/06/2027	07/08/2027
TB.PG.100	Patch Concrete Level 1-3	30	01/06/2027	02/16/2027
TB.PG.110	Install Storm Drain	5	02/17/2027	02/23/2027
TB.PG.120	Install MEP Roughs Level 1-3	10	02/24/2027	03/09/2027
TB.PG.130	Install Wheel Stops	10	03/10/2027	03/23/2027
TB.PG.140	Install Bollards	10	03/24/2027	04/06/2027
TB.PG.150	Install Parking Signage	10	04/07/2027	04/20/2027
TB.PG.160	Install Striping	15	04/21/2027	05/11/2027
TB.PG.170	Install MEP Trims	20	05/12/2027	06/09/2027
TB.PG.180	Miscellaneous Paint Interior	20	06/10/2027	07/08/2027
Level 3		205	02/17/2027	12/09/2027
INT.TB.L3.100	Install OH Rough Plumbing	15	02/17/2027	03/09/2027
INT.TB.L3.110	Install OH Rough Mechanical	25	02/17/2027	03/23/2027

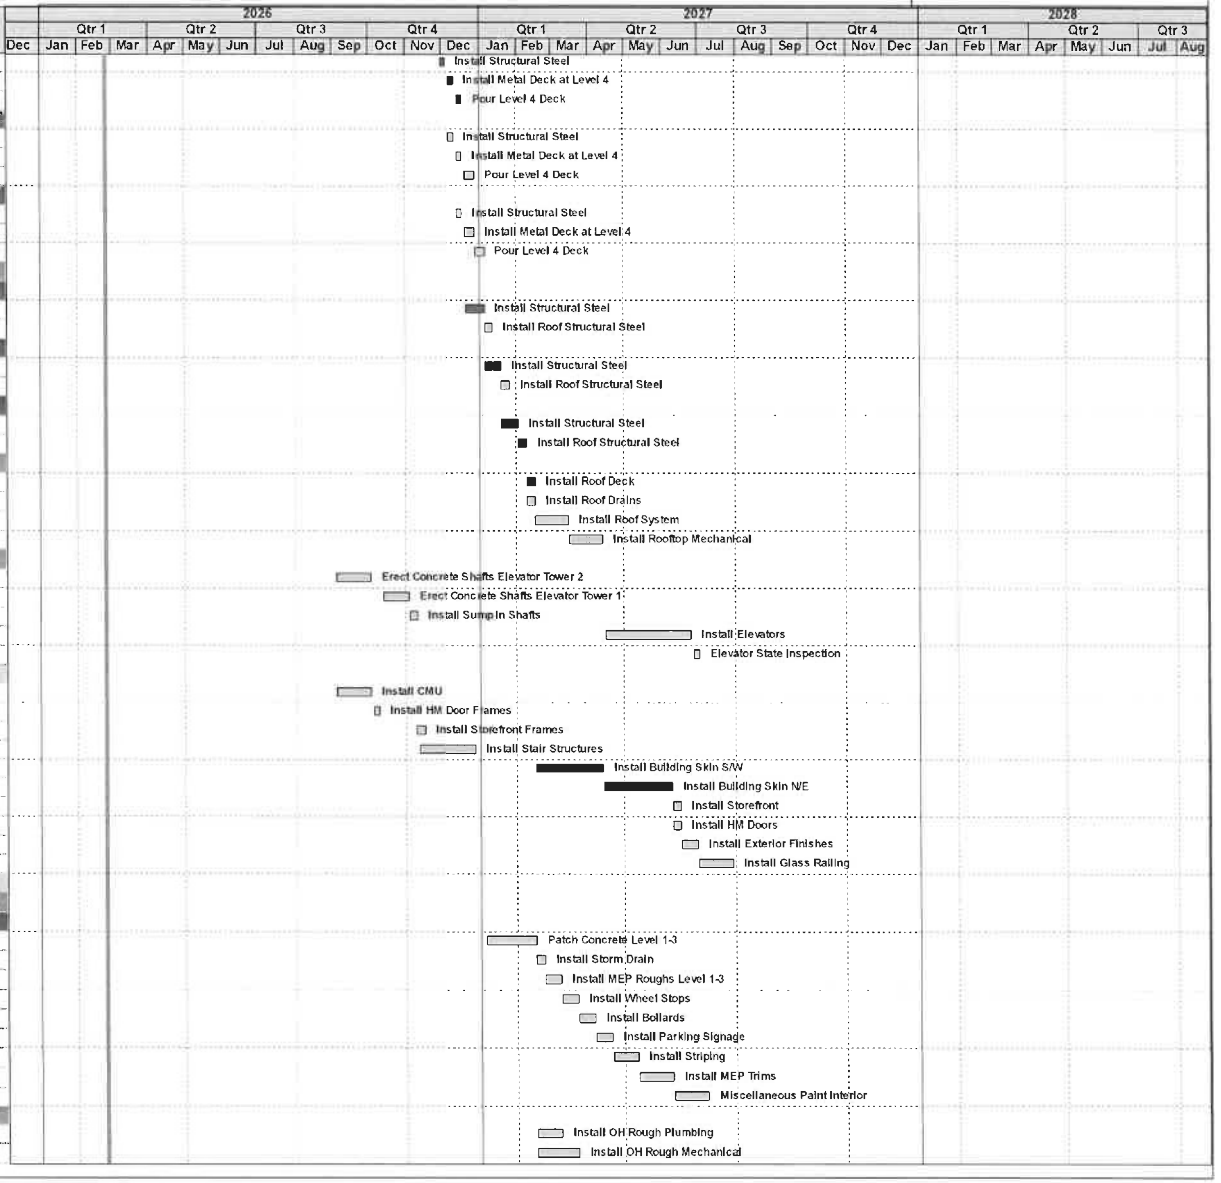

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
INT.TB.L3.120	Install OH Rough Electrical	25	02/17/2027	03/23/2027
INT.TB.L3.130	Install OH Rough Fire Sprinkler	20	02/17/2027	03/16/2027
INT.TB.L3.140	Layout Framing	2	03/24/2027	03/25/2027
INT.TB.L3.150	Frame Walls	15	03/25/2027	04/14/2027
INT.TB.L3.400	Install Operable Partition Supports Steel	5	03/26/2027	04/01/2027
INT.TB.L3.160	Install In-Wall Rough Electrical	20	03/29/2027	04/23/2027
INT.TB.L3.170	Install In-Wall Rough Plumbing	20	03/29/2027	04/23/2027
INT.TB.L3.180	Install Shower Pans	20	04/15/2027	05/12/2027
INT.TB.L3.190	Install Door Frames	10	04/15/2027	04/28/2027
INT.TB.L3.200	MEP Inspection Complete	1	04/26/2027	04/26/2027
INT.TB.L3.210	Install Insulation	10	06/10/2027	06/23/2027
INT.TB.L3.220	Install Drywall	15	06/17/2027	07/08/2027
INT.TB.L3.230	Tape & Mud Drywall	20	06/21/2027	07/19/2027
INT.TB.L3.240	Paint Walls/Ceilings/Soffits	20	07/13/2027	08/09/2027
INT.TB.L3.250	Install Tile at Bathrooms	20	07/20/2027	08/16/2027
INT.TB.L3.260	Install Ceiling Grid	20	07/27/2027	08/23/2027
INT.TB.L3.270	Install Fire Sprinkler Trim at Grid Ceiling	20	08/10/2027	09/07/2027
INT.TB.L3.280	Install Operable Partition Track	5	08/10/2027	08/16/2027
INT.TB.L3.450	Install Millwork	5	08/10/2027	08/16/2027
INT.TB.L3.290	Install Operable Partition Panels	5	08/17/2027	08/23/2027
INT.TB.L3.420	Install Subtops	5	08/17/2027	08/23/2027
INT.TB.L3.300	Install Mechanical Trim at Grid Ceiling	15	08/24/2027	09/14/2027
INT.TB.L3.310	Install Electrical Trim at Grid Ceiling	20	08/24/2027	09/21/2027
INT.TB.L3.320	Install Doors & Hardware	30	08/24/2027	10/05/2027
INT.TB.L3.430	Field Measure for Countertops	5	08/24/2027	08/30/2027
INT.TB.L3.440	Install Countertops	5	09/08/2027	09/14/2027
INT.TB.L3.330	Install Remaining Ceiling Tile	2	09/22/2027	09/23/2027
INT.TB.L3.340	Install Plumbing Trim	20	09/22/2027	10/19/2027
INT.TB.L3.350	Install Electrical Trim	10	09/24/2027	10/07/2027
INT.TB.L3.370	Install Flooring	20	09/27/2027	10/22/2027
INT.TB.L3.410	Install Food Service Equipment	15	10/25/2027	11/16/2027
INT.TB.L3.390	Install Lockers	5	11/17/2027	11/23/2027
INT.TB.L3.360	Install Bathroom Specialities	10	11/17/2027	12/02/2027
INT.TB.L3.380	Install Retractable Seating System (OFOI)	15	11/17/2027	12/09/2027
Level 4		185	03/10/2027	11/01/2027
INT.TB.L4.100	Install OH Rough Plumbing	10	03/10/2027	03/23/2027
INT.TB.L4.130	Install OH Rough Fire Sprinkler	15	03/17/2027	04/06/2027
INT.TB.L4.110	Install OH Rough Mechanical	20	03/24/2027	04/20/2027
INT.TB.L4.120	Install OH Rough Electrical	20	03/24/2027	04/20/2027
INT.TB.L4.140	Layout Framing	5	04/15/2027	04/21/2027
INT.TB.L4.150	Frame Walls	20	04/22/2027	05/19/2027
INT.TB.L4.160	Install In-Wall Rough Electrical	15	05/20/2027	06/10/2027
INT.TB.L4.170	Install In-Wall Rough Plumbing	10	05/20/2027	06/03/2027
INT.TB.L4.180	Install Door Frames	5	05/20/2027	05/26/2027
INT.TB.L4.190	MEP Inspection Complete	2	06/11/2027	06/14/2027
INT.TB.L4.200	Install Insulation	15	06/15/2027	07/06/2027
INT.TB.L4.210	Install Drywall	15	06/29/2027	07/20/2027
INT.TB.L4.220	Tape & Mud Drywall	20	07/01/2027	07/29/2027
INT.TB.L4.230	Paint Walls/Ceilings/Soffits	10	07/30/2027	08/12/2027
INT.TB.L4.240	Install Tile at Bathrooms	10	07/30/2027	08/12/2027
INT.TB.L4.250	Install Ceiling Grid	10	08/13/2027	08/26/2027
INT.TB.L4.350	Install Millwork	5	08/13/2027	08/19/2027
INT.TB.L4.360	Install Subtops	5	08/20/2027	08/26/2027
INT.TB.L4.260	Install Fire Sprinkler Trim at Grid Ceiling	5	08/27/2027	09/02/2027
INT.TB.L4.270	Install Mechanical Trim at Grid Ceiling	5	08/27/2027	09/02/2027
INT.TB.L4.280	Install Electrical Trim at Grid Ceiling	10	08/27/2027	09/10/2027
INT.TB.L4.290	Install Doors & Hardware	10	08/27/2027	09/10/2027
INT.TB.L4.370	Field Measure for Countertops	5	08/27/2027	09/02/2027

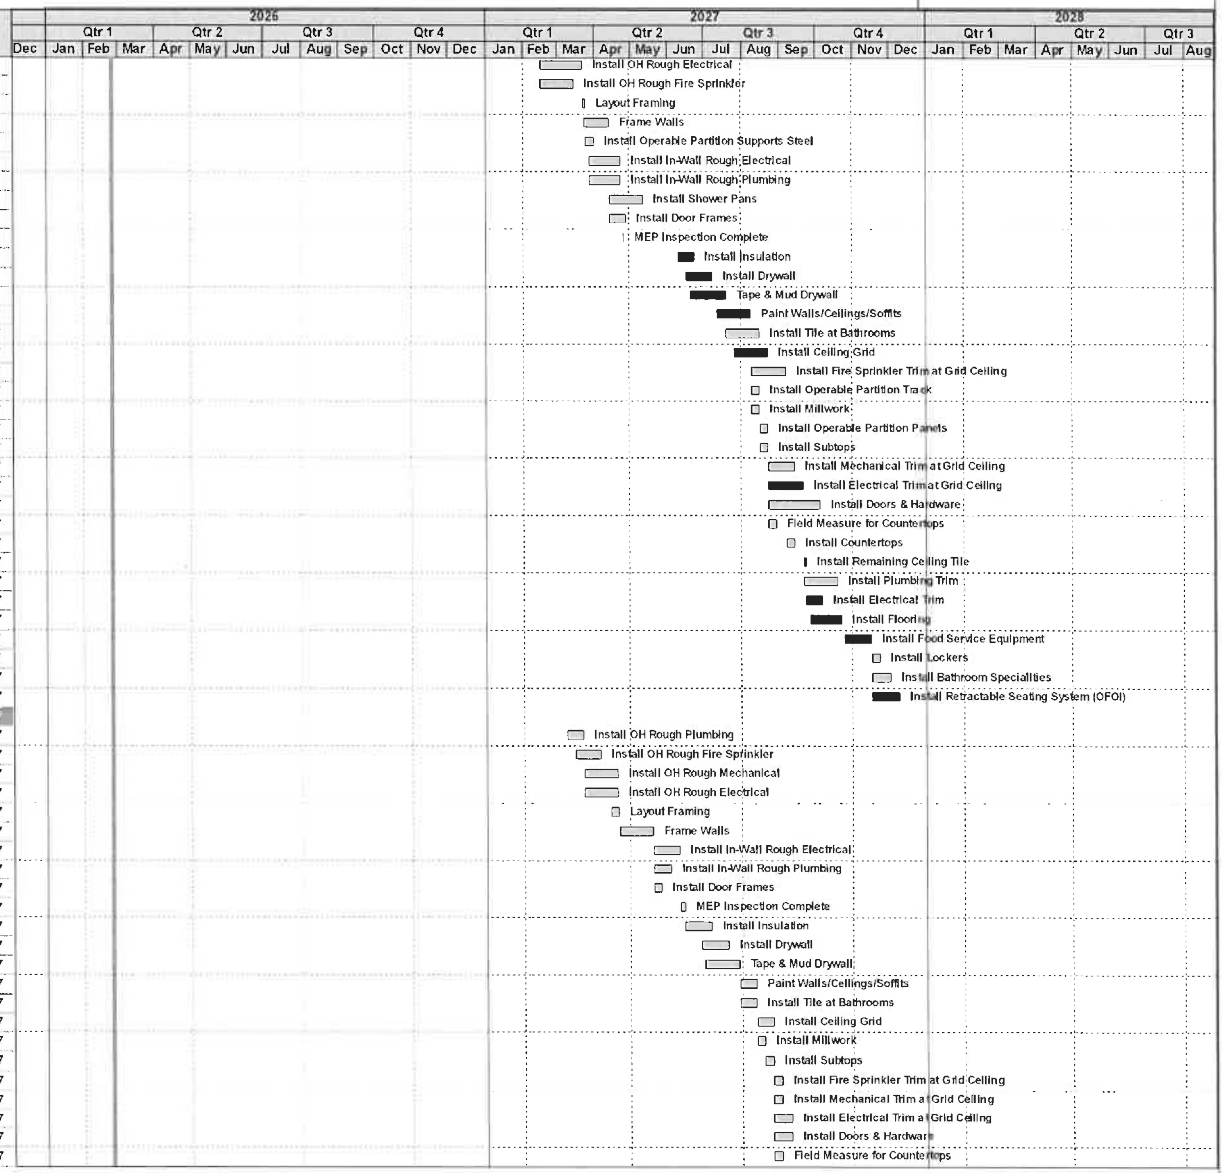

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
INT.TB.L4.300	Install Remaining Ceiling Tile	5	09/13/2027	09/17/2027
INT.TB.L4.380	Install Countertops	5	09/13/2027	09/17/2027
INT.TB.L4.310	Install Plumbing Trim	10	09/20/2027	10/01/2027
INT.TB.L4.320	Install Electrical Trim	10	09/20/2027	10/01/2027
INT.TB.L4.330	Install Flooring	15	10/04/2027	10/22/2027
INT.TB.L4.340	Install Bathroom Specialities	5	10/25/2027	11/01/2027
Commissioning & Closeout		74	12/10/2027	03/27/2028
TB.CC.100	WT Incomplete Worklist	10	12/10/2027	12/23/2027
TB.CC.110	Owner Punch	30	12/28/2027	02/08/2028
TB.CC.120	Equipment Start-Up & Testing	10	12/28/2027	01/11/2028
TB.CC.130	Life Safety Testing	10	02/09/2028	02/22/2028
TB.CC.140	Sprinkler Sign-Off by CCFD	5	02/09/2028	02/15/2028
TB.CC.150	MEP Finals	8	02/23/2028	03/03/2028
TB.CC.160	Final Clean	10	03/06/2028	03/17/2028
TB.CC.170	C of O	1	03/20/2028	03/20/2028
TB.CC.190	SNHD Final Inspection	5	03/21/2028	03/27/2028
Maintenance Building		225	08/24/2026	07/15/2027
Building Structure		87	08/24/2026	12/30/2026
Phase A		66	08/24/2026	12/29/2026
MB.BSA.100	Survey	1	08/24/2026	08/24/2026
MB.BSA.110	Layout Footings/MEPs	5	08/25/2026	08/31/2026
MB.BSA.120	Excavate Footings/MEPs	10	08/25/2026	09/08/2026
MB.BSA.130	F/R/P Footings	5	09/09/2026	09/15/2026
MB.BSA.140	F/R/P Pit Walls x2	10	09/09/2026	09/22/2026
MB.BSA.150	Install UG Plumbing	5	09/23/2026	09/29/2026
MB.BSA.160	Install UG Electrical	5	09/23/2026	09/29/2026
MB.BSA.170	Fine Grade Building Pad	5	09/30/2026	10/06/2026
MB.BSA.180	Install Vapor Barrier	5	10/07/2026	10/13/2026
MB.BSA.190	Install Type II	5	10/14/2026	10/20/2026
MB.BSA.200	F/R/P SOG	5	10/21/2026	10/27/2026
MB.BSA.210	Install Structural Steel	30	10/28/2026	12/14/2026
MB.BSA.220	Install Roof Rafters	20	12/01/2026	12/29/2026
Phase B		66	08/25/2026	12/30/2026
MB.BSB.100	Survey	1	08/25/2026	08/25/2026
MB.BSB.110	Layout Footings/MEPs	5	08/26/2026	09/01/2026
MB.BSB.120	Excavate Footings/MEPs	10	08/26/2026	09/09/2026
MB.BSB.130	F/R/P Footings	5	09/10/2026	09/16/2026
MB.BSB.140	F/R/P Pit Walls x2	10	09/10/2026	09/23/2026
MB.BSB.150	Install UG Plumbing	5	09/24/2026	09/30/2026
MB.BSB.160	Install UG Electrical	5	09/24/2026	09/30/2026
MB.BSB.170	Fine Grade Building Pad	5	10/01/2026	10/07/2026
MB.BSB.180	Install Vapor Barrier	5	10/08/2026	10/14/2026
MB.BSB.190	Install Type II	5	10/15/2026	10/21/2026
MB.BSB.200	F/R/P SOG	5	10/22/2026	10/28/2026
MB.BSB.210	Install Structural Steel	30	10/29/2026	12/15/2026
MB.BSB.220	Install Roof Rafters	20	12/02/2026	12/30/2026
Exterior		20	12/30/2026	01/27/2027
MB.EXT.100	Install Insulated Metal Panels	20	12/30/2026	01/27/2027
Interior MEP & Finishes		93	01/28/2027	06/08/2027
MB.INT.100	Layout Framing	2	01/28/2027	01/29/2027
MB.INT.400	Install Interior CMU	20	01/28/2027	02/24/2027
MB.INT.110	Frame Priority Walls	5	02/01/2027	02/05/2027
MB.INT.120	Install OH Rough Plumbing	5	02/08/2027	02/12/2027
MB.INT.130	Install OH Rough Mechanical	5	02/08/2027	02/12/2027
MB.INT.140	Install OH Rough Electrical	5	02/08/2027	02/12/2027
MB.INT.150	Install OH Rough Fire Sprinkler	10	02/08/2027	02/19/2027
MB.INT.160	Frame Remaining Walls	5	02/22/2027	02/26/2027
MB.INT.170	Install In-Wall Rough Plumbing	5	03/01/2027	03/05/2027

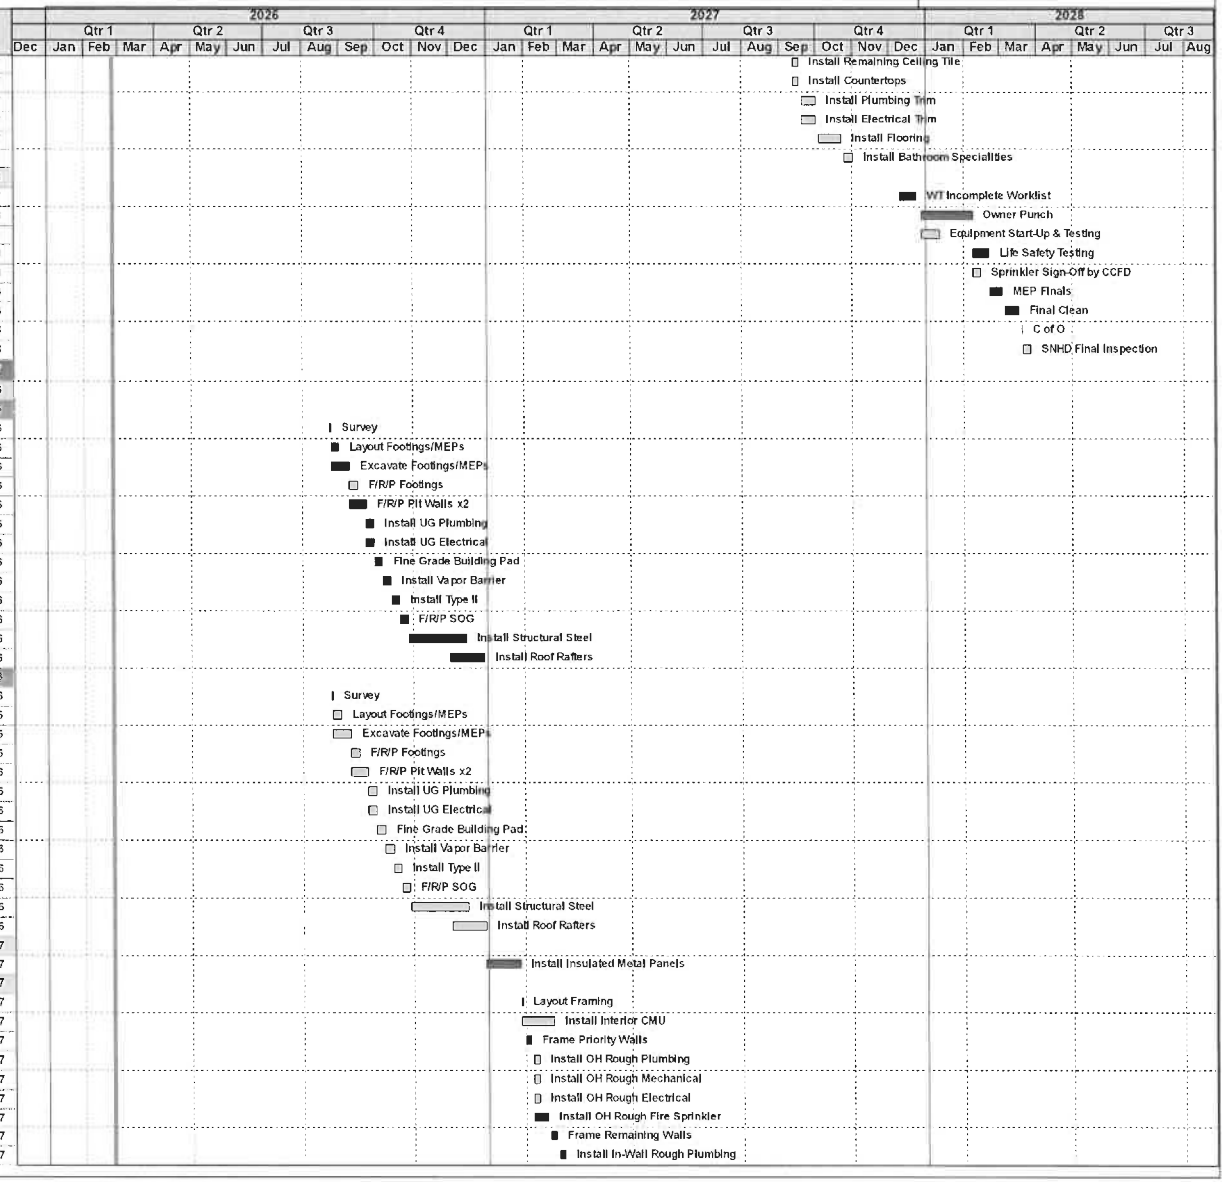

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
MB.INT.180	Install Shower Pan	5	03/01/2027	03/05/2027
MB.INT.190	Install Door Frames	5	03/01/2027	03/05/2027
MB.INT.200	Install In-Wall Rough Electrical	5	03/08/2027	03/12/2027
MB.INT.210	MEP Inspection Complete	1	03/12/2027	03/12/2027
MB.INT.220	Install Insulation	5	03/15/2027	03/19/2027
MB.INT.230	Install Drywall	5	03/22/2027	03/26/2027
MB.INT.240	Tape & Mud Drywall	10	03/24/2027	04/06/2027
MB.INT.250	Paint Walls/Ceilings/Soffits	10	03/31/2027	04/13/2027
MB.INT.260	Install Garage Bay Doors	30	03/31/2027	05/11/2027
MB.INT.270	Install Tile at Bathrooms	10	04/07/2027	04/20/2027
MB.INT.280	Install Ceiling Grid	5	04/14/2027	04/20/2027
MB.INT.290	Install Oil Room Equipment	10	04/14/2027	04/27/2027
MB.INT.300	Install Ventilation System	10	04/14/2027	04/27/2027
MB.INT.410	Install Millwork	5	04/14/2027	04/20/2027
MB.INT.310	Install Fire Sprinkler Trim	5	04/21/2027	04/27/2027
MB.INT.320	Install Mechanical Trim	5	04/21/2027	04/27/2027
MB.INT.330	Install Electrical Trim at Grid Ceiling	5	04/21/2027	04/27/2027
MB.INT.340	Install Doors & Hardware	5	04/21/2027	04/27/2027
MB.INT.420	Install Subtops	5	04/21/2027	04/27/2027
MB.INT.350	Install Remaining Ceiling Tile	5	04/28/2027	05/04/2027
MB.INT.430	Field Measure for Countertops	1	04/28/2027	04/28/2027
MB.INT.440	Install Countertops	5	05/06/2027	05/12/2027
MB.INT.360	Install Plumbing Trim	5	05/13/2027	05/19/2027
MB.INT.370	Install Flooring	15	05/13/2027	06/03/2027
MB.INT.380	Install Lockers	3	06/04/2027	06/08/2027
MB.INT.390	Install Bathroom Specialities	2	06/04/2027	06/07/2027
Roof		30	12/30/2026	02/10/2027
MB.R.100	Install Roof Deck	10	12/30/2026	01/13/2027
MB.R.110	Install Roof Insulation	5	01/14/2027	01/20/2027
MB.R.120	Install Roof Sheet (Metal Seam)	10	01/21/2027	02/03/2027
MB.R.130	Install Rooftop Mechanical	5	02/04/2027	02/10/2027
Commissioning & Closeout		26	06/09/2027	07/15/2027
MB.CC.100	WT Incomplete Worklist	10	06/09/2027	06/22/2027
MB.CC.110	Owner Punch	10	06/23/2027	07/07/2027
MB.CC.120	Equipment Start-Up & Testing	3	06/23/2027	06/25/2027
MB.CC.130	Life Safety Testing	2	07/08/2027	07/09/2027
MB.CC.140	Sprinkler Sign-Off by CCFD	1	07/08/2027	07/08/2027
MB.CC.150	MEP Finals	1	07/12/2027	07/12/2027
MB.CC.160	Final Clean	2	07/13/2027	07/14/2027
MB.CC.170	C of O	1	07/15/2027	07/15/2027
Fire Station		240	08/31/2026	08/12/2027
Building Structure		50	08/31/2026	11/10/2026
FS.BS.100	Survey	2	08/31/2026	09/01/2026
FS.BS.110	Layout Footings/MEPs	3	09/02/2026	09/04/2026
FS.BS.120	Excavate Footings/MEPs	5	09/08/2026	09/14/2026
FS.BS.130	F/R/P Footings	10	09/15/2026	09/28/2026
FS.BS.140	Install UG Plumbing	10	09/29/2026	10/12/2026
FS.BS.150	Install UG Electrical	10	09/29/2026	10/12/2026
FS.BS.160	Fine Grade Building Pad	5	10/13/2026	10/19/2026
FS.BS.170	Install Vapor Barrier	5	10/20/2026	10/26/2026
FS.BS.180	Install Type II	5	10/27/2026	11/03/2026
FS.BS.190	F/R/P SOG	5	11/04/2026	11/10/2026
Exterior		70	11/12/2026	02/23/2027
FS.EXT.100	Erect CMU	20	11/12/2026	12/11/2026
FS.EXT.110	Install Storefront Frames	10	12/14/2026	12/28/2026
FS.EXT.120	Install HM Door Frames	5	12/14/2026	12/18/2026
FS.EXT.170	Install Structural Steel	5	12/14/2026	12/18/2026
FS.EXT.130	Install HM Doors	5	12/21/2026	12/28/2026

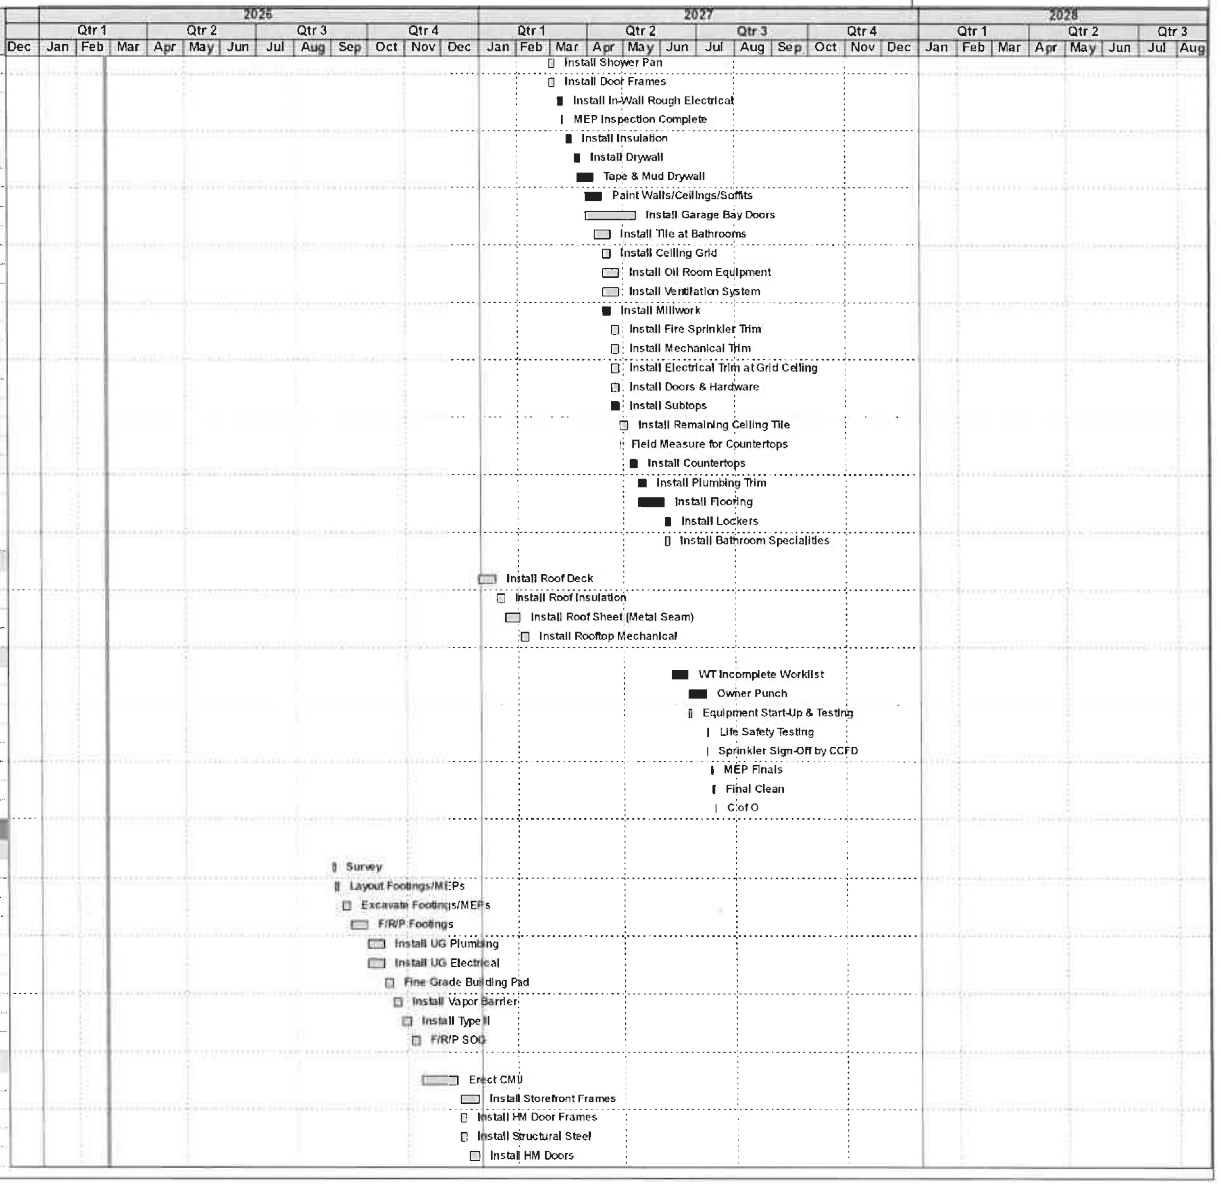

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
FS.EXT.180	Install Structural Steel Supports	5	12/21/2026	12/28/2026
FS.EXT.140	Install Storefront Glass	5	12/29/2026	01/05/2027
FS.EXT.150	Install Building Skin	30	01/06/2027	02/16/2027
FS.EXT.160	Install Building Signage	5	02/17/2027	02/23/2027
Interior MEP & Finishes		121	01/06/2027	06/24/2027
FS.INT.110	Install OH Rough Plumbing	10	01/06/2027	01/19/2027
FS.INT.120	Install OH Rough Mechanical	10	01/06/2027	01/19/2027
FS.INT.130	Install OH Rough Electrical	10	01/06/2027	01/19/2027
FS.INT.140	Install OH Rough Fire Sprinkler	15	01/06/2027	01/26/2027
FS.INT.150	Layout Framing	2	01/27/2027	01/28/2027
FS.INT.160	Frame Walls	10	01/28/2027	02/10/2027
FS.INT.170	Install In-Wall Rough Electrical	5	02/11/2027	02/17/2027
FS.INT.180	Install In-Wall Rough Plumbing	5	02/11/2027	02/17/2027
FS.INT.190	Install Door Frames	5	02/11/2027	02/17/2027
FS.INT.100	Install 4-Fold Doors	10	02/17/2027	03/02/2027
FS.INT.200	MEP Inspection Complete	1	02/18/2027	02/18/2027
FS.INT.220	Install Insulation	5	02/19/2027	02/25/2027
FS.INT.440	Shim & Shave	2	02/26/2027	03/01/2027
FS.INT.450	Install Shower Pans	2	03/02/2027	03/03/2027
FS.INT.230	Install Drywall	10	03/04/2027	03/17/2027
FS.INT.240	Tape & Mud Drywall	10	03/08/2027	03/19/2027
FS.INT.250	Paint Walls/Ceilings/Soffits	5	03/22/2027	03/26/2027
FS.INT.260	Install Tile at Bathrooms	10	03/22/2027	04/02/2027
FS.INT.270	Install Ceiling Grid	5	03/29/2027	04/02/2027
FS.INT.280	Install Fire Sprinkler Trim at Grid Ceiling	5	04/05/2027	04/09/2027
FS.INT.290	Install Mechanical Trim at Grid Ceiling	5	04/05/2027	04/09/2027
FS.INT.300	Install Electrical Trim at Grid Ceiling	5	04/05/2027	04/09/2027
FS.INT.310	Install Doors & Hardware	5	04/05/2027	04/09/2027
FS.INT.390	Install Low Voltage Trim	5	04/05/2027	04/09/2027
FS.INT.320	Install Remaining Ceiling Tile	5	04/12/2027	04/16/2027
FS.INT.460	Install Plymovent at App Bay	5	04/12/2027	04/16/2027
FS.INT.480	Install Locution System & Programming	10	04/12/2027	04/23/2027
FS.INT.400	Install Millwork	5	04/16/2027	04/22/2027
FS.INT.340	Install Electrical Trim	10	04/19/2027	04/30/2027
FS.INT.420	Install Subtops	5	04/23/2027	04/29/2027
FS.INT.410	Field Measure for Countertops	1	04/30/2027	04/30/2027
FS.INT.430	Install Counter Tops	5	05/10/2027	05/14/2027
FS.INT.330	Install Plumbing Trim	5	05/17/2027	05/21/2027
FS.INT.350	Install Bathroom Specialities	5	05/24/2027	05/28/2027
FS.INT.360	Install Flooring	10	05/24/2027	06/07/2027
FS.INT.370	Install Lockers	5	06/08/2027	06/14/2027
FS.INT.470	Install Cord Reels at App Bay	3	06/15/2027	06/17/2027
FS.INT.380	Install Epoxy Coating at Bays	5	06/18/2027	06/24/2027
Roof		30	12/21/2026	02/02/2027
FS.R.100	Install Roof Structure	5	12/21/2026	12/28/2026
FS.R.110	Install Roof Deck	5	12/29/2026	01/05/2027
FS.R.120	Install Roof Drains	5	12/29/2026	01/05/2027
FS.R.130	Install Roof System	10	01/06/2027	01/19/2027
FS.R.140	Install RTU's	5	01/20/2027	01/26/2027
FS.R.150	Terminate Electrical at RTU's	5	01/27/2027	02/02/2027
Commissioning & Closeout		34	06/25/2027	08/12/2027
FS.CC.100	WT Incomplete Worklist	10	06/25/2027	07/09/2027
FS.CC.110	Owner Punch	15	07/12/2027	07/30/2027
FS.CC.120	Equipment Start-Up & Testing	5	07/12/2027	07/16/2027
FS.CC.130	Life Safety Testing	3	08/02/2027	08/04/2027
FS.CC.140	Sprinkler Sign-Off by CCFD	1	08/02/2027	08/02/2027
FS.CC.150	MEP Finals	2	08/05/2027	08/06/2027
FS.CC.160	Final Clean	3	08/09/2027	08/11/2027

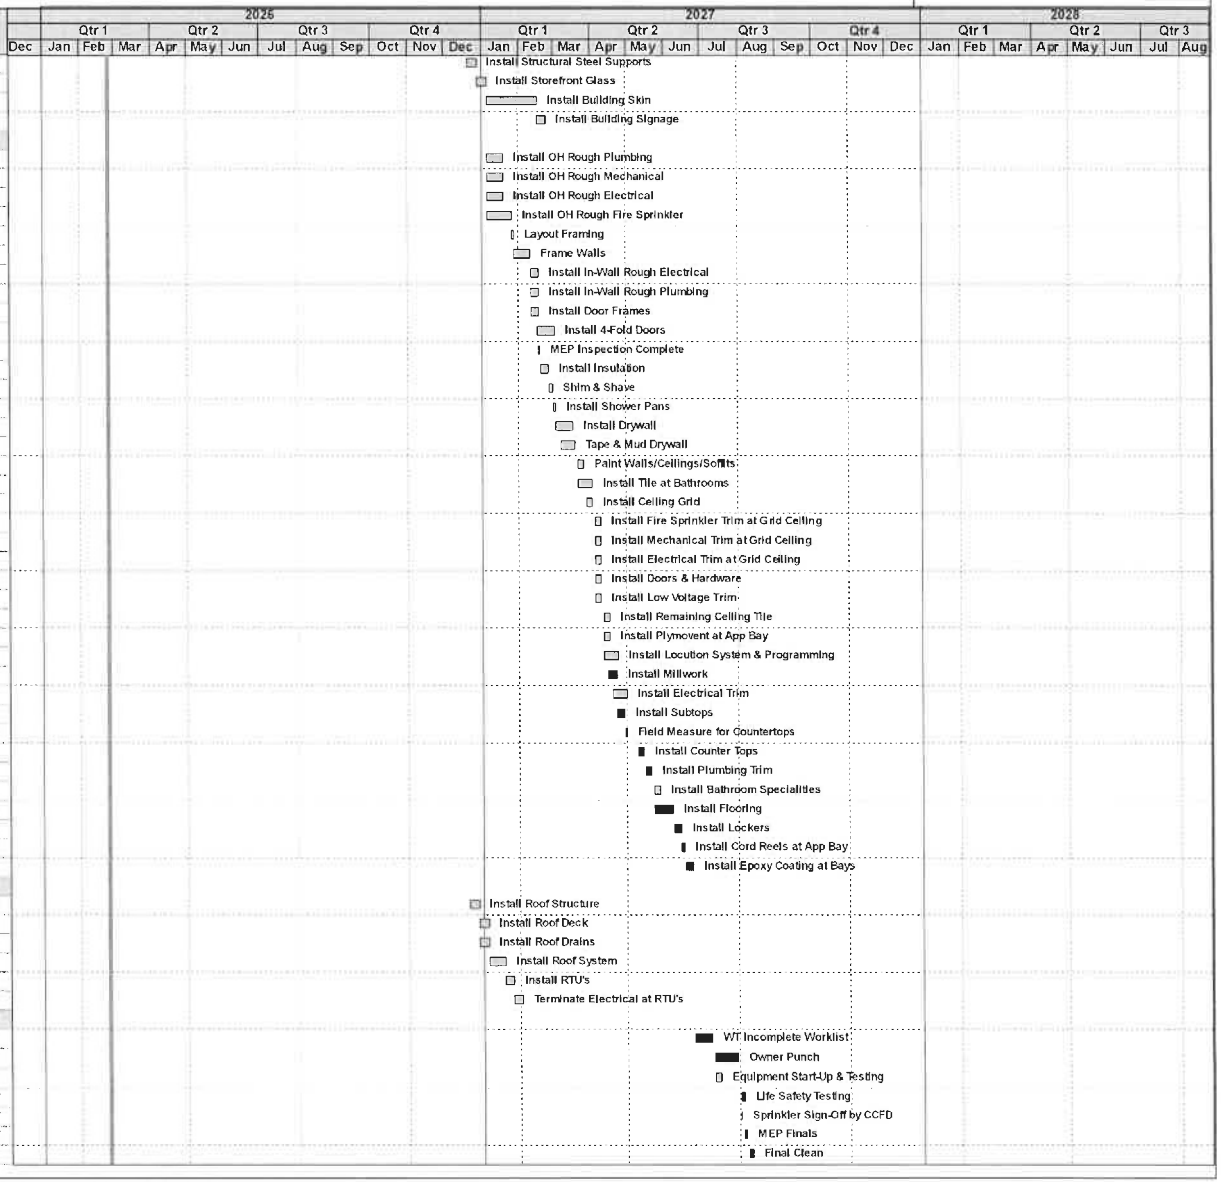

WHITING-TURNER

Clark County Fire Training Center Baseline Schedule
Full Schedule

Data Date: 02/25/2026
Print Date: 03/09/2026

Activity ID	Activity Name	Orig Dur	Start	Finish
FS.CC.170	C of O	1	08/12/2027	08/12/2027
Burn Tower		263	08/25/2026	08/12/2027
Building Structure		45	08/25/2026	10/27/2026
BT.BS.100	Survey	5	08/25/2026	08/31/2026
BT.BS.110	Layout	5	09/01/2026	09/08/2026
BT.BS.120	Excavate Footings/MEPs	5	09/09/2026	09/15/2026
BT.BS.130	F/R/P Footings	5	09/16/2026	09/22/2026
BT.BS.140	Install UG Plumbing	5	09/23/2026	09/29/2026
BT.BS.150	Install UG Electrical	5	09/23/2026	09/29/2026
BT.BS.160	Fine Grade Building Pad	5	09/30/2026	10/06/2026
BT.BS.170	Install Vapor Barrier	5	10/07/2026	10/13/2026
BT.BS.180	Install Type II	5	10/14/2026	10/20/2026
BT.BS.190	F/R/P SOG	5	10/21/2026	10/27/2026
Tower Build		95	04/06/2027	08/18/2027
BT.TB.100	Erect Burn Tower	80	04/06/2027	07/28/2027
BT.TB.120	Interior Buildout/Trim by WHP	5	07/29/2027	08/04/2027
BT.TB.110	Install MEP's & Props by Fire Blast	10	08/05/2027	08/18/2027
Final Inspections		15	08/19/2027	09/09/2027
BT.FI.100	Burn Tower Inspection & Final Acceptance	5	08/19/2027	08/25/2027
BT.FI.110	Commissioning/Startup/Training	10	08/26/2027	09/09/2027
Site Finishes (Hardscape/Landscape)		55	07/29/2027	10/14/2027
Hardscape/Landscape		55	07/29/2027	10/14/2027
SITE.100	Grade Site for Landscape	10	07/29/2027	08/11/2027
SITE.110	Install Landscape Sleeves & Irrigation	5	08/12/2027	08/18/2027
SITE.180	Perimeter CMU Wall Footings	10	08/12/2027	08/25/2027
SITE.120	Install Low Voltage Sleeves	5	08/19/2027	08/25/2027
SITE.130	F/R/P Curb & Sidewalk	15	08/26/2027	09/16/2027
SITE.190	Perimeter CMU Wall Install	20	08/26/2027	09/23/2027
SITE.140	Install Landscape	10	09/17/2027	09/30/2027
SITE.150	Install Running Track	10	09/17/2027	09/30/2027
SITE.200	Install Perimeter Fencing	15	09/24/2027	10/14/2027
SITE.160	Prep & Lay Asphalt	5	10/01/2027	10/07/2027
SITE.170	Striping	1	10/08/2027	10/08/2027
OCCUPANCY & CLOSE OUT		10	10/11/2027	10/22/2027
Closeout		10	10/11/2027	10/22/2027
CLO.100	WT Incomplete Worklist	5	10/11/2027	10/15/2027
CLO.110	Owner Punch	5	10/18/2027	10/22/2027

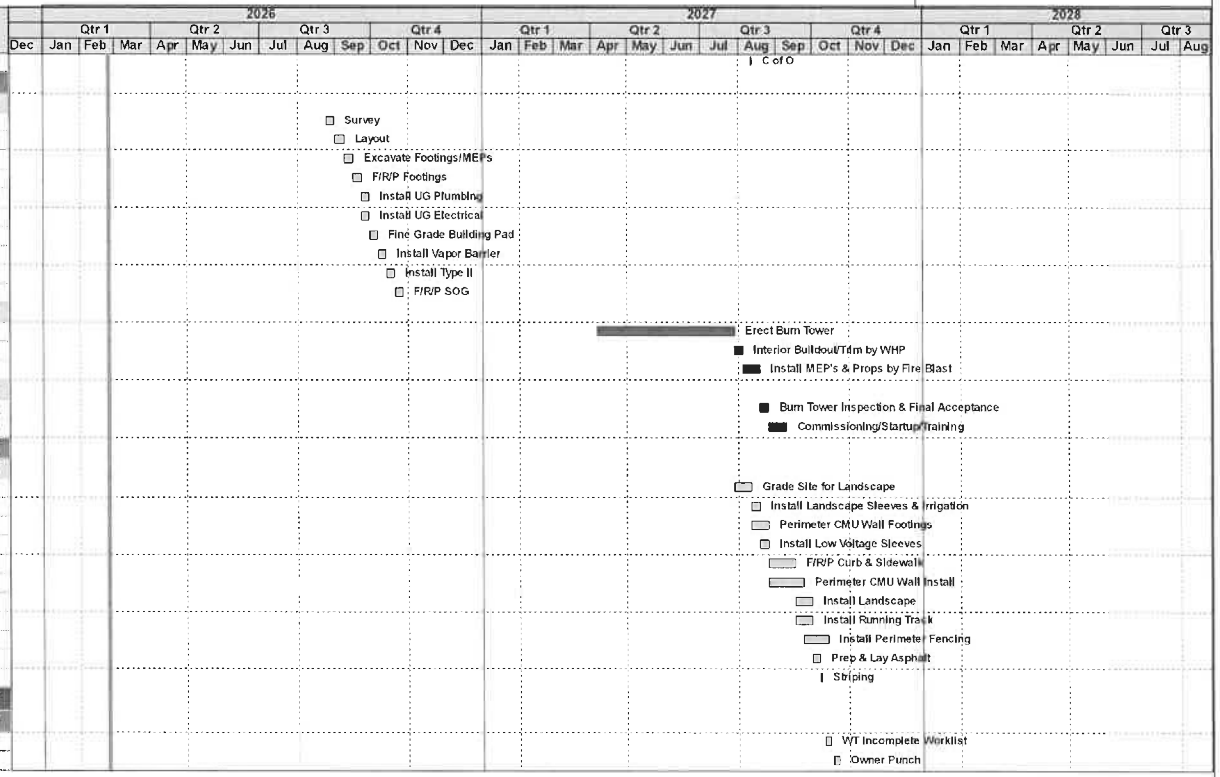

EXHIBIT I
NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE
PREVAILING WAGE RATES (ATTACHED TO FINAL CONTRACT)

Left intentionally blank

EXHIBIT J

BONDS AND INSURANCE REQUIREMENTS AND FORMS

1. BONDS

   A. Contractor shall furnish bonds covering the faithful performance of the Contract, payment of all obligations arising thereunder and a Guaranty Bond to take effect upon substantial completion of the project, utilizing the bond forms. Bonds may be secured through Contractor's usual sources, provided that the surety is authorized and licensed to do business in the State of Nevada. All bonds specified shall indicate the State of Nevada Insurance Division license number, the surety company name, address, telephone number, and include the appointed agent of record who issued the bond. Surety Bonds issued by an individual are not acceptable to Clark County.

   B. Not later than **ten (10) business days** after COUNTY'S written request for insurance, Contractor shall furnish contract bonds to the Purchasing and Contracts Division as follows:

      1. Labor and Material Payment Bond in the amount of 100% of the Contract price.

      2. Performance Bond in the amount of 100% of the Contract price.

      3. Guaranty Bond in the amount of 100% of the Contract price. The Guaranty Bond will go into effect from the date of Notice of Substantial Completion.

      Award will become final after the Governing Body has authorized the award and Contractor has submitted its required bonds utilizing COUNTY'S Bond forms.

   C. Form of Bonds

      1. The bonds referred to herein **shall be written on the Performance Bond, Labor and Material Payment Bond, and Guaranty Bond forms provided by COUNTY.**

      2. Contractor shall require the attorney-in-fact who executes the required bonds on behalf of the surety to affix thereto a certified and current copy of his power of attorney.

      3. **Any Performance Bond, Labor and Material Payment Bond, or Guaranty Bond prepared by an appointed agent must provide their license number and the issuing state.**

      4. The bonds specified in this section must be issued by a certified surety which is listed in the Department of the Treasury, Fiscal Service, (Department Circular 570; Current Revision) companies holding certificates of authority as acceptable sureties on Federal Bonds and as acceptable reinsuring companies.

2. INSURANCE

   A. Contractor further agrees, as a precondition to the performance of any work under this contract and as a precondition to any obligation of COUNTY to make any payment under this contract, to provide COUNTY with a certificate of insurance and/or a certificate issued by an insurer qualified to underwrite workers' compensation insurance in the state of Nevada in accordance with Nevada Revised Statutes Chapters §616A through 616D, inclusive, whether or not Contractor has employees.

   B. Contractor agrees to maintain required workers' compensation coverage (statutory) and employer's liability in the amount of $1,000,000 for each accident, disease for each employee, and disease – policy limit throughout the entire term of the contract. If Contractor does not maintain coverage throughout the entire term of the contract, Contractor agrees that COUNTY may, at any time the coverage is not maintained by Contractor, order Contractor to stop work, assess liquidated damages as defined herein, suspend the contract, or terminate the contract.

   C. Contractor shall furnish not later than **ten (10) business days** after COUNTY'S written request for insurance, the insurance as indicated below. The certificates for each insurance policy shall be signed by a person authorized by that insurer and licensed by the State of Nevada.

   D. As a condition precedent to receiving payments, Contractor shall have on file with COUNTY current certificates of insurance evidencing the required coverage. Insurance certificates for COUNTY should contain the information shown on the sample certificates attached.

E. Each insurance company's rating as shown in the latest Best's Key Rating Guide shall be fully disclosed and entered on the required certificate of insurance. COUNTY requires insurance carriers to maintain a Best's Key Rating of A.VII or higher (i.e., A.VII, A.VIII, A.IX, A.X, etc.). The adequacy of the insurance supplied by Contractor, including the rating and financial health of each insurance company providing coverage, is subject to the approval of COUNTY.

F. COUNTY, its officers, employees, agents, and volunteers, NV Energy, must be expressly covered as insured's with respect to liability arising out of the activities by or on behalf of the named insured in connection with this project.

1. Contractor's insurance shall be primary as respects COUNTY, its officers, employees, agents, and volunteers, NV Energy, any other coverage (insurance or otherwise) available to COUNTY, its officers, employees and volunteers shall be excess over the insurance required of Contractor and shall not contribute with it.

G. Contractor's commercial general liability and automobile liability insurance policy shall be endorsed to recognize specifically Contractor's contractual obligation of additional insured to COUNTY. All policies must note that COUNTY will be given 30-calendar days advance notice by certified mail "return receipt requested" of any policy changes, cancellations, or any erosion of insurance limits. **Separate copies of additional insured endorsements are required and must be attached to any certificate of insurance. Policy number must be referenced on endorsement or the form number must be referenced on certificate.**

H. All deductibles and self-insured retentions shall be fully disclosed in the Certificate of Insurance. ***If the deductible is "zero" it must still be referenced on the certificate.***

I. If aggregate limits are imposed on the insurance coverage, then the amount of such limits must not be less than **$4,000,000** per occurrence or per accident. All aggregates must be fully disclosed, and the amount entered on the required certificate of insurance. Contractor's insurer must notify COUNTY of any erosion of the aggregate limits. The "per occurrence" limits of insurance required herein must be maintained in full, irrespective of any erosion of aggregate.

J. Contractor shall obtain and maintain, for the duration of the Contract or longer period if specified herein, insurance against claims for injuries to persons or damages to property which may arise from or in connection with the performance of the work hereunder by Contractor, it agents, representatives, employees or subcontractors of any tier. The cost of such insurance shall be included in Contractor's RFP. Contractor is required to obtain and maintain the following coverage:

1. Commercial General Liability: Commercial General Liability coverage shall be on "occurrence" basis only and not "claims made." The coverage must be provided on either an ISO Commercial General Liability form or an ISO Broad Form Comprehensive General Liability (including a Broad Form CGL Endorsement) insurance form. Policies must contain a primary and non-contributory clause and must contain a waiver of subrogation endorsement. Any exceptions to coverage must be fully disclosed on the required certificates. If other than these forms are submitted as evidence of compliance, complete copies of such policy forms must be submitted to COUNTY within **ten (10) business days** after COUNTY'S written request of insurance. Policies must include, but need not be limited to, coverage for bodily injury, property damage, personal injury, Broad Form property damage, premises and operations, severability of interest, products and completed operations (coverage maintained for at least 10 years after completion), and contractual and independent contractors. Contractor shall maintain limits of no less than **$2,000,000** per occurrence for bodily injury (including death), medical expenses, personal and advertising injury and property damages. **A separate copy of the waiver of subrogation endorsement must be provided. A separate copy of the additional insured endorsement is required and must be provided for Commercial General Liability. Policy number must be referenced on endorsement or the form number must be referenced on certificate.**

2. Auto Liability: Auto Liability must provide coverage for claims for damage due to bodily injury or death of any person, or property damage arising out of the ownership, maintenance or use of **any motor vehicles whether owned, hired or non-owned**. Contractor shall maintain limits of no less than **$2,000,000** combined single limit "per accident" for bodily injury and property damage**. A separate copy of the additional insured endorsement is required and must be provided for Automobile Liability policies. Policy number must be referenced on endorsement or the form number must be referenced on certificate.**

3. Umbrella or Excess Liability: Umbrella or Excess Liability coverage shall be provided in an amount of no less than $10,000,000 per occurrence and $10,000,000 aggregate, excess over the underlying Commercial General Liability, Business Auto Liability, Employers' Liability, and any other required primary insurance policies. Coverage shall be on an "occurrence" basis and not "claims made." The policy shall follow form of the underlying insurance, contain a primary and non-contributory clause

with respect to County, and include a waiver of subrogation endorsement in favor of Clark County. Any exceptions to coverage must be fully disclosed on the certificate of insurance. Complete copies of the policy forms shall be provided to Clark County within ten (10) business days upon written request. The policy shall include coverage for bodily injury (including death), property damage, personal and advertising injury, and any other coverages provided by the underlying policies. A separate copy of the waiver of subrogation endorsement and the additional insured endorsement must be provided. The policy number or form number must be referenced on the endorsement or certificate.

4. Professional Liability (Errors and Omissions): Policy shall cover professional misconduct or lack of ordinary skill for those positions defined in the scope of services of this contract. Each claim with a limit no less than $1,000,000 and $2,000,000 annual aggregate. If the professional liability insurance provided is on a claims-made basis, Contractor warrants that any retroactive date under the policy shall precede the effective date of this contract, and that either continuous coverage will be maintained or an extended discovery period will be exercised for a period of two (2) years beginning at the time of work under this contract is completed.

   A separate copy of the Extended Reporting Period or 'Tail Coverage' endorsement is required and must be provided for the Professional Liability policy. Policy number must be referenced on endorsement, or the form number must be referenced on the certificate with the retroactive date.

5. Contractor's Pollution Liability (including Errors and Omissions): Per occurrence limit of no less than $1,000,000 and general aggregate of $2,000,000 for losses caused by pollution conditions that arise from the operations of the Contractor. The policy shall include Asbestos Liability or include an additional Asbestos Liability endorsement and provide protection against claims for third-party bodily injury, property damage, or environmental damage caused by pollution conditions resulting from general contracting activities for which the Contractor is legally liable. The policy shall provide for cleanup costs when mandated by governmental entities, when required by law, or as a result of third-party claims. The policy shall be endorsed to cover Non-Owned Disposal Sites, cover transportation of pollutants and policies should have a 5 year tail provision.

6. Builders Risk or Course of Construction (Owned and Non-Owned County Property): Unless otherwise provided in the Contract Documents, Contractor shall purchase and maintain property insurance (builder's risk or course of construction) on an "All-Risk" or "Special Form" basis at full replacement cost of all work, including temporary works, materials in transit and off-site, and County-owned property to be incorporated into the project This insurance shall include the interests of, COUNTY, COUNTY'S designated representative, Contractor, Subcontractors, and Subcontractors of any tier. Coverage shall be written on forms including theft, vandalism, collapse, testing, resulting damage, fire, and extended coverage. Contractor is responsible for the deductible for any claim made against the policy.

K. If Contractor fails to maintain any of the insurance coverage required herein, then COUNTY will have the option to declare Contractor in breach or may purchase replacement insurance or pay the premiums that are due on existing policies in order that the required coverage may be maintained. Contractor is responsible for any expenses paid by COUNTY to maintain such insurance and COUNTY may collect the same from Contractor or deduct the amount paid from any sums due Contractor under the contract.

L. The insurance requirements specified herein do not relieve Contractor of its responsibility or limit the amount of their liability to COUNTY or other persons and Contractor is encouraged to purchase such additional insurance, as it deems necessary.

M. Contractor is responsible for and must remedy all damage or loss to any property, including property of COUNTY, caused in whole or in part by Contractor, any subcontractor or anyone employed, directed or supervised by Contractor. Contractor is responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the work.

N. Contractor shall pay all premiums and costs of insurance.

O. Regardless of the coverage provided by any insurance policy, Contractor shall indemnify, defend and hold COUNTY, NV Energy, harmless from any and all claims, demands, actions, attorneys' fees, costs, and expenses based upon or arising out of any acts, errors, omissions, fault or negligence of Contractor or its principals, employees, subcontractors or other agents while performing services under this Contract. Contractor shall indemnify, defend and hold harmless COUNTY and others specified from any attorney's fees or other costs of defense, even if the allegations of the claim are groundless, false or fraudulent.

POLICY NUMBER: _____ COMMERCIAL GENERAL AND AUTOMOBILE LIABILITY

RFP NUMBER AND PROJECT NAME: _____

THIS ENDORSEMENT CHANGED THE POLICY. PLEASE READ IT CAREFULLY

ADDITIONAL INSURED – DESIGNATED PERSON OR ORGANIZATION

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY AND AUTOMOBILE LIABILITY COVERAGE PART.

SCHEDULE

Name of Person or Organization:

CLARK COUNTY, NEVADA
C/O PURCHASING & CONTRACTS DIVISION
500 S. GRAND CENTRAL PKWY 4TH FL
PO BOX 551217
LAS VEGAS, NEVADA 89155-1217

(If no entry appears above, information required to complete this endorsement will be shown in the Declarations as applicable to this endorsement.)

WHO IS AN INSURED (Section II) is amended to include as an insured the person or organization shown in the Schedule as an insured but only with respect to liability arising out of your operations or premises owned by or rented to you.

CLARK COUNTY, ITS OFFICERS, EMPLOYEES AND VOLUNTEERS, NV ENERGY, ARE INSUREDS WITH RESPECT TO LIABILITY ARISING OUT OF THE ACTIVITIES BY OR ON BEHALF OF THE NAMED INSURED IN CONNECTION WITH THIS PROJECT.

SAMPLE

BOND NUMBER: _____
RFP No. 607319-24
CLARK COUNTY, NEVADA

PERFORMANCE BOND

IMPORTANT: SURETY COMPANIES EXECUTING BONDS MUST BE LICENSED TO ISSUE SURETY BY THE STATE OF NEVADA INSURANCE DIVISION PURSUANT TO NEVADA REVISED STATUTE 683A AND ISSUED BY AN APPOINTED PRODUCER OF INSURANCE PURSUANT TO NEVADA REVISED STATUTE 683A. INDIVIDUAL SURETY BONDS ARE NOT ACCEPTABLE.

KNOW ALL MEN BY THESE PRESENTS,

That _____, as Principal Contractor, and _____, as Surety, are held and firmly bound unto CLARK COUNTY, NEVADA, hereinafter called COUNTY, in the sum of _____ dollars, for the payment of which sum well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents.

WHEREAS, said Contractor has been recommended for award and shall enter into the contract with said COUNTY to perform all work required under the bidding Schedule(s) **RFP NO. 607319-24** of COUNTY'S specifications, entitled **NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE .**

NOW THEREFORE, if said Contractor shall perform all the requirements of said contract required to be performed on their part, at the times and in the manner specified therein, then this obligation shall be null and void, otherwise it shall remain in full force and effect.

PROVIDED, that any change order(s), alterations in the work to be done or the materials to be furnished, which may be made pursuant to the terms of said contract, shall not in any way release said Contractor or said Surety thereunder, nor shall any extensions of time granted under the provisions of said contract release either said Contractor or said Surety, and notice of such change order(s), alterations or extensions of the contract is hereby waived by said Surety.

SIGNED this _____ day of _____, 20 _____

(SEAL AND NOTARIAL ACKNOWLEDGMENT OF SURETY)

_____
(Principal Contractor)

_____
(Authorized Representative and Title)

By: _____
(Signature)

Surety: _____

_____
(Appointed Agent Name)

_____
(State of Nevada, License Number)

By: _____
(Signature)

_____
(Appointed Agent Name)

_____
(License Number and Issuing State)

By: _____
(Signature)

Address: _____

_____

Address: _____

_____

Telephone: _____

Telephone: _____

ISSUING COMPANY MUST HOLD CERTIFICATES OF AUTHORITY AS ACCEPTABLE SURETY ON FEDERAL BONDS AND AS ACCEPTABLE REINSURING COMPANY WITH LISTING IN THE DEPARTMENT OF TREASURY, FISCAL SERVICE, (DEPARTMENT OF CIRCULAR "570," CURRENT REVISIONS).

BOND NUMBER: _____
RFP No. 607319-24
CLARK COUNTY, NEVADA

LABOR AND MATERIAL PAYMENT BOND

IMPORTANT: SURETY COMPANIES EXECUTING BONDS MUST BE LICENSED TO ISSUE SURETY BY THE STATE OF NEVADA INSURANCE DIVISION PURSUANT TO NEVADA REVISED STATUTE 683A AND ISSUED BY AN APPOINTED PRODUCER OF INSURANCE PURSUANT TO NEVADA REVISED STATUTE 683A. INDIVIDUAL SURETY BONDS ARE NOT ACCEPTABLE.

KNOW ALL MEN BY THESE PRESENTS,

That _____, as Contractor, and _____, as Surety, are held and firmly bound unto CLARK COUNTY, NEVADA, hereinafter called COUNTY, in the sum of _____ dollars, for the payment of which sum well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents.

WHEREAS, said Contractor has been recommended for award and shall enter into the contract with said COUNTY to perform all work required under the Bid Schedule(s), **RFP NO. 607319-24, NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE** .

NOW THEREFORE, if said Contractor, or subcontractors, fails to pay for any materials, equipment, or other supplies, or for rental of same, used in connection with the performance of work contracted to be done, or for amounts due under applicable State law for any work or labor thereon, said Surety will pay for the same in an amount not exceeding the sum specified above and, in the event suit is brought upon this bond, a reasonable attorney's fee to be fixed by the court. This bond shall insure to the benefit of any persons, companies or corporations entitled to file claims under applicable State law.

PROVIDED, that any change order(s), alterations in the work to be done or the materials to be furnished, which may be made pursuant to the terms of said Contract, shall not in any way release either said Contractor or said Surety thereunder, nor shall any extensions of time granted under the provisions of said Contract release either said Contractor or said Surety, and notice of such change order(s), alterations or extensions of the Contract is hereby waived by said Surety.

SIGNED this _____ day of _____, 20 _____

(SEAL AND NOTARIAL ACKNOWLEDGMENT OF SURETY)

_____
(Principal Contractor)

_____
(Authorized Representative and Title)

By: _____
(Signature)

Surety: _____

_____
(Appointed Agent Name)

_____
(State of Nevada, License Number)

By: _____
(Signature)

_____
(Appointed Agent Name)

_____
(License Number and Issuing State)

By: _____
(Signature)

Address: _____

_____

Address: _____

_____

Telephone: _____

Telephone: _____

ISSUING COMPANY MUST HOLD CERTIFICATES OF AUTHORITY AS ACCEPTABLE SURETY ON FEDERAL BONDS AND AS ACCEPTABLE REINSURING COMPANY WITH LISTING IN THE DEPARTMENT OF TREASURY, FISCAL SERVICE, (DEPARTMENT OF CIRCULAR "570," CURRENT REVISIONS).

BOND NUMBER: _____
RFP No. 607319-24
CLARK COUNTY, NEVADA

GUARANTY BOND

IMPORTANT: SURETY COMPANIES EXECUTING BONDS MUST BE LICENSED TO ISSUE SURETY BY THE STATE OF NEVADA INSURANCE DIVISION PURSUANT TO NEVADA REVISED STATUTE 683A AND ISSUED BY AN APPOINTED PRODUCER OF INSURANCE PURSUANT TO NEVADA REVISED STATUTE 683A. INDIVIDUAL SURETY BONDS ARE NOT ACCEPTABLE.

GUARANTEE for _____

_____
(Name and Address of Prime Contractor)

We hereby guarantee that the **RFP NO. 607319-24, NEW FIRE TRAINING CENTER & SITE IMPROVEMENTS WITH PARKING GARAGE** , which we have constructed, has been done in accordance with the plans and specifications; that the work as constructed will fulfill the requirements of the guaranties included in the Contract Documents. We agree to repair or replace any or all of our work together with any other adjacent work which may be damaged in so doing, that may prove to be defective in workmanship or materials within a period of one year from the date of the Notice of Substantial Completion of the above named work by the County of Clark, State of Nevada, without any expense whatsoever to said County of Clark, State of Nevada, ordinary wear and unusual abuse or neglect excepted.

In the event of our failure to comply with the above mentioned conditions within 14 calendar days after being notified in writing by Clark County, Nevada, we collectively or separately, do hereby authorize Clark County, Nevada to proceed to have said defects repaired and made good at our expense and we will honor and pay the costs and charges therefore upon demand. When correction work is started, it shall be carried through to completion.

SIGNED this _____ day of _____, 20 _____

(SEAL AND NOTARIAL ACKNOWLEDGMENT OF SURETY)

_____
(Principal Contractor)

_____
(Authorized Representative and Title)

By: _____
(Signature)

Surety: _____

_____
(State of Nevada, License Number)

_____
(Appointed Agent Name)

By: _____
(Signature)

_____
(Appointed Agent Name)

By: _____
(Signature)

_____
(License Number and Issuing State)

Address: _____

_____

Telephone: _____

Address: _____

_____

Telephone: _____

ISSUING COMPANY MUST HOLD CERTIFICATES OF AUTHORITY AS ACCEPTABLE SURETY ON FEDERAL BONDS AND AS ACCEPTABLE REINSURING COMPANY WITH LISTING IN THE DEPARTMENT OF TREASURY, FISCAL SERVICE, (DEPARTMENT OF CIRCULAR "570," CURRENT REVISIONS).

EXHIBIT K
SUBCONTRACTOR INFORMATION

DEFINITIONS:

- MINORITY OWNED BUSINESS ENTERPRISE (MBE): An independent and continuing **Nevada** business for profit which performs a commercially useful function and is at least 51% owned and controlled by one or more minority persons of Black American, Hispanic American, Asian-Pacific American or Native American ethnicity.
- WOMEN OWNED BUSINESS ENTERPRISE (WBE): An independent and continuing **Nevada** business for profit which performs a commercially useful function and is at least 51% owned and controlled by one or more women.
- PHYSICALLY CHALLENGED BUSINESS ENTERPRISE (PBE): An independent and continuing **Nevada** business for profit which performs a commercially useful function and is at least 51% owned and controlled by one or more disabled individuals pursuant to the federal Americans with Disabilities Act.
- SMALL BUSINESS ENTERPRISE (SBE): An independent and continuing **Nevada** business for profit which performs a commercially useful function, is **not** owned and controlled by individuals designated as minority, women, or physically challenged, and where gross annual sales does not exceed $2,000,000.
- VETERAN OWNED ENTERPRISE (VET): A Nevada business at least 51% owned/controlled by a veteran.
- DISABLED VETERAN OWNED ENTERPRISE (DVET): A Nevada business at least 51% owned/controlled by a disabled veteran.
- EMERGING SMALL BUSINESS (ESB): Certified by the Nevada Governor's Office of Economic Development effective January, 2014. Approved into Nevada law during the 77th Legislative session as a result of AB294.

It is our intent to utilize the following MBE, WBE, PBE, SBE, VET, DVET and ESB subcontractors in association with CONTRACT:

1. Subcontractor Name: _____
   Contact Person: _____ Telephone Number: _____
   Description of Work: _____
   Estimated Percentage of Total Dollars: _____
   Business Type: ☐ MBE ☐ WBE ☐ PBE ☐ SBE ☐ VET
   ☐ DVET ☐ ESB

2. Subcontractor Name: _____
   Contact Person: _____ Telephone Number: _____
   Description of Work: _____
   Estimated Percentage of Total Dollars: _____
   Business Type: ☐ MBE ☐ WBE ☐ PBE ☐ SBE ☐ VET
   ☐ DVET ☐ ESB

3. Subcontractor Name: _____
   Contact Person: _____ Telephone Number: _____
   Description of Work: _____
   Estimated Percentage of Total Dollars: _____
   Business Type: ☐ MBE ☐ WBE ☐ PBE ☐ SBE ☐ VET
   ☐ DVET ☐ ESB

☐ No MBE, WBE, PBE, SBE, VET, DVET, or ESB subcontractors will be used.
